Well Location Plat

CNX Applicant / Well Operator Name	**DEP ID#**	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	**Well #** **MAJ8CHSM**

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8CHSM OH As Drilled_ KOP	5601.21	39.93138254	-80.57544742	5861.00
MAJ8CHSM OH As Drilled_ LP	6616.52	39.93018991	-80.57366707	7293.00
MAJ8CHSM OH As Drilled_BHL	6734.22	39.90118148	-80.54486568	20596.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1076.50	Survey #1 (OH)	GYD_CT+WIR
1190.50	2210.50	Survey #2 (OH)	MWD+IFR1+Sag
2350.00	20596.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

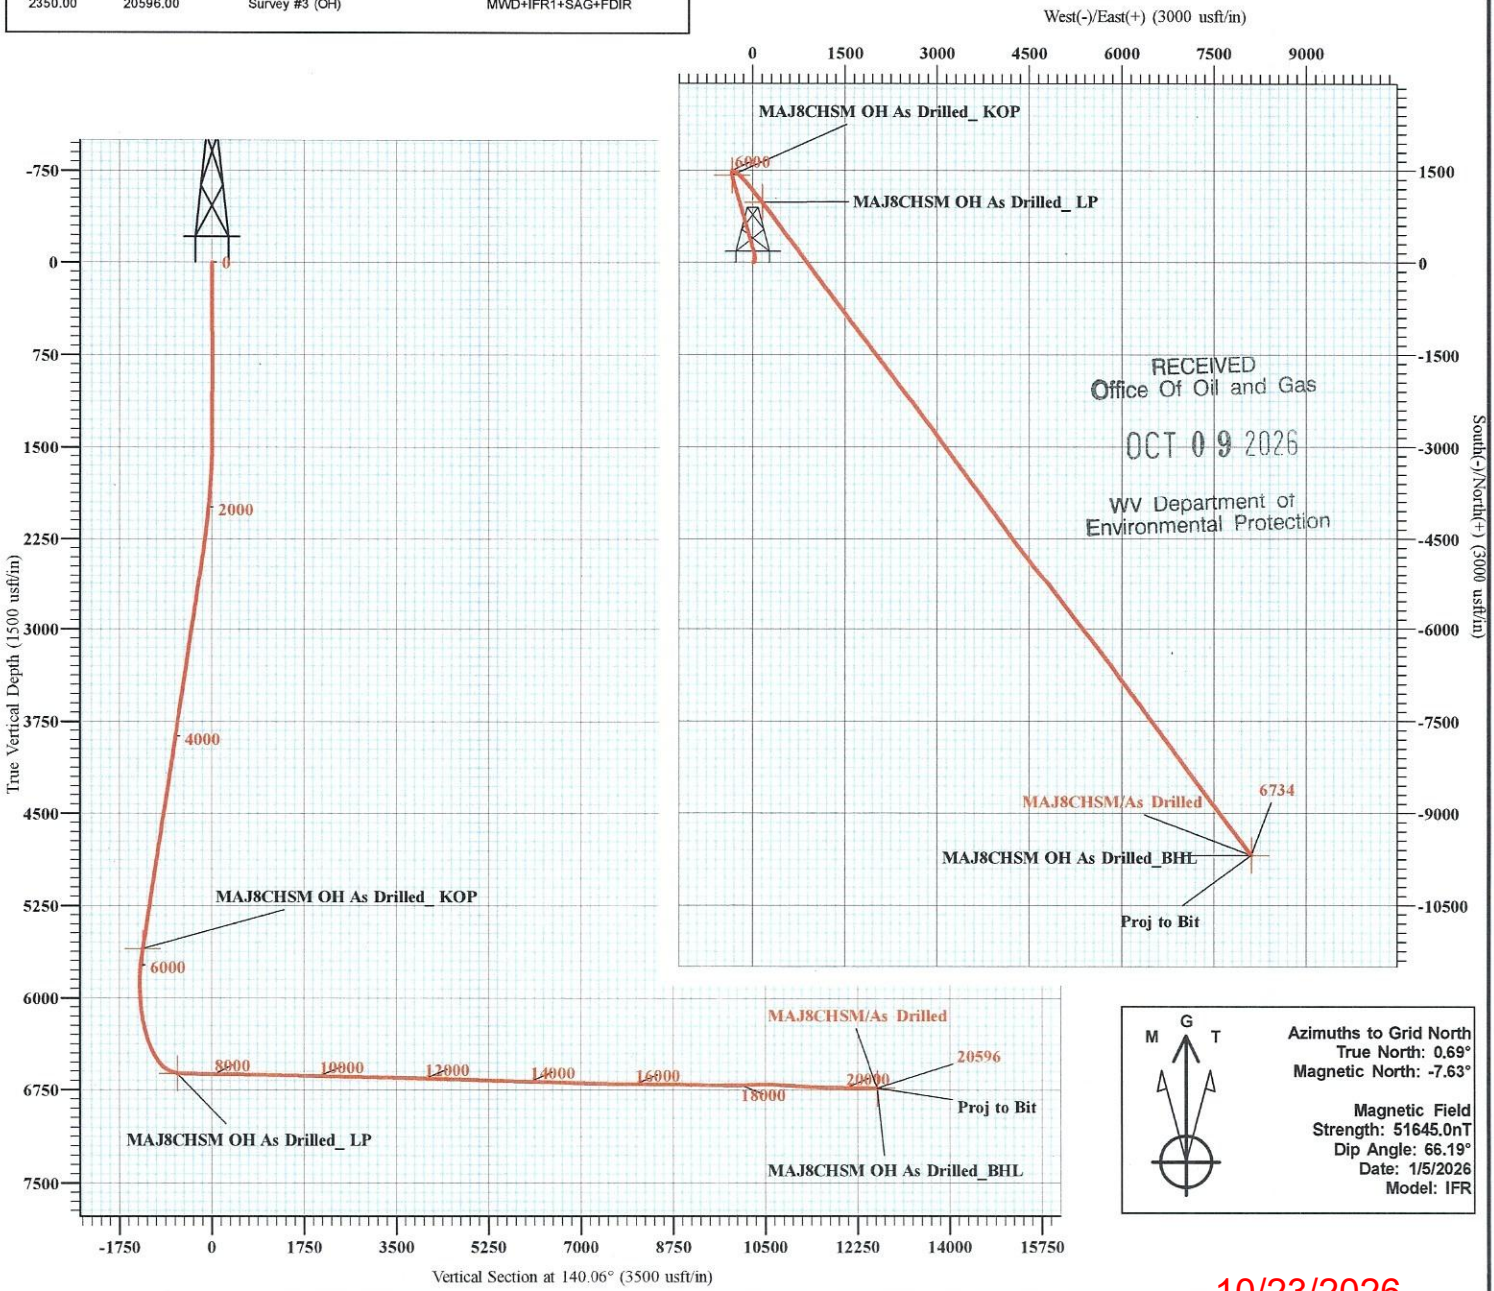


Azimuths to Grid North
True North: 0.69°
Magnetic North: -7.63°

Magnetic Field
Strength: 51645.0nT
Dip Angle: 66.19°
Date: 1/5/2026
Model: IFR

10/23/2026

JANUARY 5 2026
SURVEY REPORT

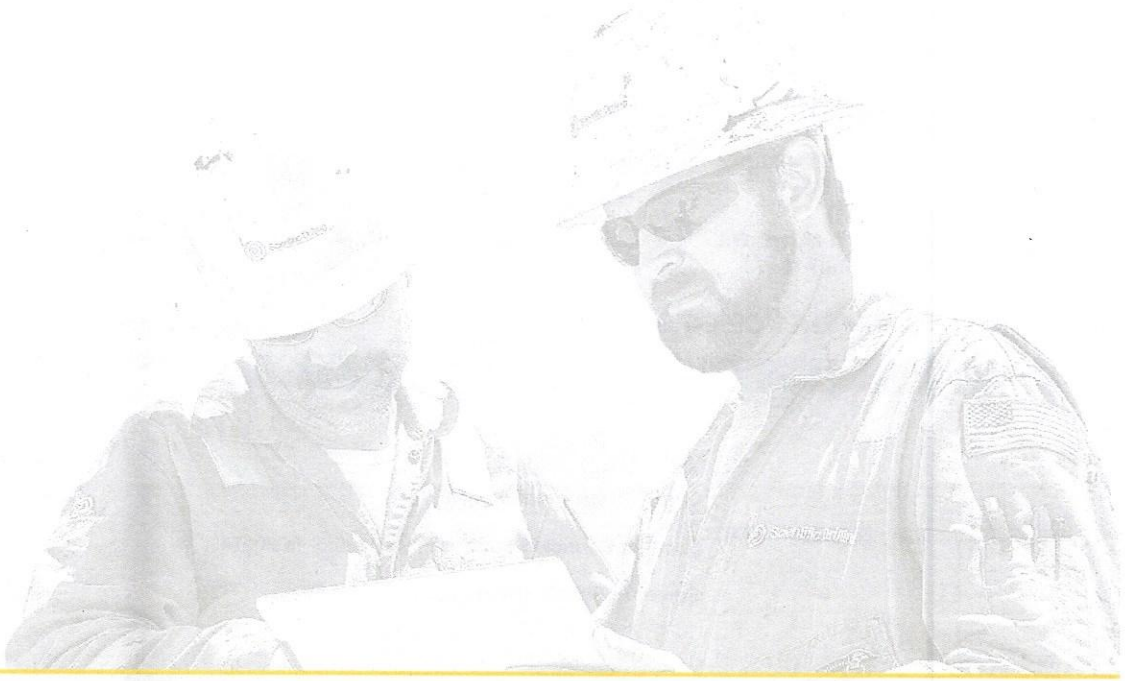

CNX RESOURCES
WELL: MAJ8 CHSM
RIG: PRECISION DRILLING 539

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

CUSTOMER	**CNX Resources**	SDI JOB NO.	**OP.051495**
PROJECT	**MAJ8 CHSM**	SDI DISTRICT	**Northeast**
FIELD	**Marcellus**	SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**	Section	-
Lat/Long	**39.927526 N, 80.574227 W**	Township	-
Northing	**521,744.52 ft**	Range	-
Easting	**1,698,736.42 ft**		

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.927493 N, 80.57417 W**
Northing	**521,732.13 ft**
Easting	**1,698,752.12 ft**
UWI	**47-051-02544**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.28°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-20596 ft	IFR1	05 Jan 2026	-8.32°	add 0.69°	subtract 7.63°

WELL NOTES

Gyro Surveys From 0' To 1076.5'

Superior Corrected Surveys From 1190.5' To 20574'

Survey At 20596' Is A Projection To The Bit

OPERATORS

D. BARKER, J. WITKOWSKI

SDI Operator Name (Printed) SIGNATURE DATE

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.34	61.92	54.50	0.02	0.08	0.14	0.62
104.50	0.48	86.42	104.50	0.16	0.16	0.48	0.44
154.50	0.28	93.17	154.50	0.35	0.17	0.81	0.41
204.50	0.41	96.26	204.50	0.55	0.14	1.11	0.26
254.50	0.51	94.92	254.49	0.82	0.10	1.51	0.20
304.50	0.25	79.62	304.49	1.02	0.10	1.84	0.55
354.50	0.50	68.83	354.49	1.13	0.20	2.15	0.52
404.50	0.51	82.07	404.49	1.29	0.31	2.58	0.23
454.50	0.57	96.62	454.49	1.57	0.31	3.04	0.30
504.50	0.57	87.74	504.49	1.88	0.29	3.54	0.18
554.50	0.59	95.89	554.48	2.20	0.28	4.04	0.17
604.50	0.62	93.90	604.48	2.55	0.23	4.57	0.07
654.50	0.67	96.95	654.48	2.93	0.18	5.13	0.12
704.50	0.43	96.92	704.48	3.26	0.12	5.61	0.48
754.50	0.51	95.70	754.47	3.54	0.07	6.01	0.16
804.50	0.50	96.71	804.47	3.84	0.03	6.45	0.03
854.50	0.54	80.78	854.47	4.10	0.04	6.90	0.30
904.50	0.59	83.11	904.47	4.33	0.11	7.39	0.11
954.50	0.63	92.64	954.46	4.63	0.13	7.92	0.22
1004.50	0.73	88.46	1004.46	4.99	0.12	8.51	0.22
1054.50	0.69	80.22	1054.46	5.31	0.18	9.13	0.22
1076.50	0.63	76.26	1076.46	5.42	0.23	9.38	0.34
1190.50	0.94	76.55	1190.44	6.03	0.60	10.89	0.27
1278.50	2.12	61.83	1278.41	6.56	1.54	13.03	1.40
1363.50	3.91	45.15	1363.29	6.38	4.32	16.47	2.32
1451.50	5.70	29.48	1450.98	4.20	10.24	20.75	2.50
1538.50	7.33	16.62	1537.42	-0.86	19.32	24.46	2.50
1624.50	9.83	12.27	1622.45	-8.96	31.76	27.59	3.00
1711.50	11.15	9.18	1708.00	-19.68	47.32	30.51	1.65
1796.50	11.91	2.31	1791.29	-32.22	64.20	32.18	1.84
1884.50	12.94	355.36	1877.23	-47.62	83.09	31.75	2.06
1971.50	14.41	351.95	1961.76	-65.37	103.52	29.44	1.93

RECEIVED Office Of Oil and Gas OCT 09 2026 WV Department of Environmental Protection 10/23/2026

MD ft	INC deg	AZIM deg	TVD ft	VS ft	+N/-S ft	+E/-W ft	DLS °/100ft
2057.50	15.78	349.95	2044.79	-85.21	125.63	25.90	1.70
2142.50	16.94	347.08	2126.35	-106.87	149.08	21.12	1.66
2210.50	17.54	345.56	2191.30	-125.42	168.66	16.35	1.10
2261.00	17.41	345.46	2239.47	-139.46	183.34	12.55	0.26
2350.00	20.04	344.11	2323.75	-166.04	210.90	5.04	2.99
2440.00	19.78	343.96	2408.37	-194.70	240.37	-3.39	0.29
2529.00	19.88	344.40	2492.09	-222.91	269.42	-11.62	0.20
2619.00	19.91	344.48	2576.72	-251.47	298.92	-19.84	0.05
2708.00	20.56	344.39	2660.23	-280.18	328.58	-28.10	0.73
2798.00	20.66	343.93	2744.47	-309.78	359.05	-36.75	0.21
2887.00	20.70	344.07	2827.73	-339.17	389.27	-45.41	0.07
2976.00	21.09	344.02	2910.88	-368.85	419.78	-54.14	0.44
3066.00	21.22	343.98	2994.81	-399.23	451.01	-63.09	0.15
3155.00	20.43	343.89	3078.00	-428.84	481.41	-71.85	0.89
3245.00	19.69	343.12	3162.54	-457.81	511.01	-80.61	0.87
3335.00	18.97	343.39	3247.46	-485.80	539.54	-89.19	0.81
3424.00	21.52	344.00	3330.96	-514.66	569.10	-97.83	2.87
3514.00	20.94	343.65	3414.85	-545.18	600.40	-106.90	0.66
3603.00	21.58	344.13	3497.79	-575.38	631.40	-115.86	0.75
3693.00	21.55	343.88	3581.49	-606.32	663.20	-124.97	0.11
3782.00	21.36	344.18	3664.33	-636.76	694.50	-133.93	0.25
3872.00	21.23	344.31	3748.18	-667.28	725.96	-142.80	0.15
3961.00	21.20	344.31	3831.15	-697.35	756.96	-151.51	0.03
4051.00	20.17	343.48	3915.35	-727.10	787.51	-160.33	1.19
4141.00	21.59	343.96	3999.44	-757.15	818.30	-169.31	1.59
4230.00	21.61	344.34	4082.19	-787.77	849.81	-178.26	0.16
4320.00	21.59	344.05	4165.87	-818.71	881.69	-187.29	0.12
4409.00	21.50	344.08	4248.65	-849.27	913.12	-196.26	0.10
4499.00	21.29	344.28	4332.44	-879.94	944.71	-205.21	0.25
4588.00	21.57	343.98	4415.29	-910.33	975.99	-214.10	0.34
4678.00	21.76	344.40	4498.93	-941.37	1007.95	-223.15	0.27
4767.00	21.39	344.07	4581.70	-971.93	1039.45	-232.05	0.44

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4856.00	21.18	344.01	4664.63	-1002.14	1070.51	-240.93	0.24
4946.00	21.24	344.44	4748.53	-1032.55	1101.85	-249.78	0.19
5035.00	21.32	343.76	4831.46	-1062.74	1132.91	-258.63	0.29
5125.00	21.10	344.34	4915.37	-1093.18	1164.22	-267.58	0.34
5214.00	21.21	344.39	4998.37	-1123.15	1195.15	-276.23	0.13
5303.00	21.31	343.99	5081.31	-1153.30	1226.20	-285.03	0.20
5393.00	21.24	344.09	5165.18	-1183.84	1257.60	-294.01	0.09
5482.00	21.22	344.02	5248.14	-1213.97	1288.58	-302.86	0.04
5572.00	21.22	344.37	5332.04	-1244.40	1319.93	-311.73	0.14
5661.00	21.15	343.74	5415.02	-1274.47	1350.85	-320.57	0.27
5751.00	21.17	343.70	5498.95	-1304.91	1382.04	-329.67	0.03
5840.00	21.01	343.80	5581.99	-1334.91	1412.78	-338.64	0.18
5930.00	20.48	344.79	5666.16	-1364.67	1443.47	-347.27	0.71
6019.00	13.67	358.86	5751.22	-1387.75	1469.05	-351.57	8.90
6109.00	10.58	18.18	5839.24	-1401.16	1487.55	-349.20	5.62
6198.00	8.93	64.55	5927.08	-1404.51	1498.29	-340.40	8.76
6288.00	12.88	105.88	6015.56	-1395.16	1498.55	-324.42	9.45
6377.00	18.38	121.09	6101.27	-1374.26	1488.58	-302.83	7.66
6467.00	24.00	127.10	6185.16	-1343.52	1470.19	-276.06	6.69
6556.00	30.59	130.29	6264.21	-1304.02	1444.60	-244.31	7.58
6646.00	37.01	133.81	6338.97	-1254.93	1411.00	-207.26	7.46
6735.00	45.86	137.82	6405.64	-1196.59	1368.70	-166.39	10.38
6825.00	52.83	138.41	6464.24	-1128.63	1317.89	-120.85	7.76
6914.00	60.42	138.98	6513.16	-1054.60	1262.09	-71.84	8.54
7003.00	66.36	141.71	6553.02	-975.18	1200.83	-21.13	7.21
7093.00	75.50	141.80	6582.39	-890.24	1134.10	31.47	10.16
7182.00	79.21	141.80	6601.87	-803.44	1065.86	85.16	4.17
7272.00	84.03	141.53	6614.98	-714.46	996.04	140.38	5.36
7361.00	89.88	143.05	6619.71	-625.64	925.76	194.71	6.79
7451.00	89.84	143.70	6619.93	-535.64	853.53	248.40	0.72
7540.00	89.64	143.43	6620.33	-446.65	781.93	301.26	0.38
7629.00	89.47	143.89	6621.02	-357.65	710.24	354.00	0.55
7719.00	89.48	143.43	6621.85	-267.66	637.75	407.33	0.51

RECEIVED Office Of Oil and Gas OCT 09 2026 WV Department of Environmental Protection 10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7808.00	89.81	144.14	6622.40	-178.66	565.95	459.91	0.88
7897.00	88.64	142.50	6623.60	-89.68	494.58	513.06	2.26
7987.00	89.85	143.78	6624.79	0.31	422.58	567.04	1.96
8076.00	89.48	143.22	6625.31	89.31	351.04	619.98	0.75
8166.00	89.37	143.64	6626.21	179.31	278.76	673.60	0.48
8256.00	90.18	144.21	6626.57	269.30	206.02	726.60	1.10
8345.00	89.78	143.52	6626.60	358.29	134.14	779.08	0.90
8435.00	89.64	144.13	6627.05	448.29	61.49	832.20	0.70
8524.00	90.08	144.49	6627.27	537.27	-10.79	884.12	0.64
8614.00	89.51	143.45	6627.59	627.26	-83.57	937.06	1.32
8703.00	90.68	144.94	6627.45	716.25	-155.75	989.12	2.13
8792.00	89.14	142.93	6627.58	805.23	-227.69	1041.51	2.85
8882.00	89.44	142.75	6628.70	895.22	-299.41	1095.87	0.39
8972.00	89.24	143.72	6629.74	985.22	-371.50	1149.74	1.10
9061.00	89.44	142.26	6630.76	1074.21	-442.56	1203.31	1.66
9155.00	89.31	142.76	6631.79	1168.19	-517.14	1260.51	0.55
9240.00	89.81	142.18	6632.44	1253.18	-584.55	1312.29	0.90
9330.00	89.65	143.27	6632.86	1343.18	-656.16	1366.80	1.22
9419.00	89.51	143.41	6633.52	1432.17	-727.56	1419.94	0.22
9509.00	89.98	143.81	6633.92	1522.17	-800.01	1473.33	0.69
9598.00	88.84	142.81	6634.83	1611.16	-871.37	1526.50	1.70
9688.00	89.48	143.33	6636.15	1701.15	-943.30	1580.57	0.92
9777.00	89.01	142.02	6637.33	1790.14	-1014.07	1634.53	1.56
9866.00	89.34	142.44	6638.61	1879.11	-1084.41	1689.03	0.60
9956.00	90.22	143.95	6638.95	1969.11	-1156.47	1742.95	1.94
10045.00	89.41	141.91	6639.24	2058.10	-1227.48	1796.59	2.47
10135.00	88.77	142.59	6640.67	2148.07	-1298.63	1851.69	1.04
10224.00	90.08	142.85	6641.56	2237.06	-1369.44	1905.59	1.50
10313.00	89.54	142.90	6641.86	2326.06	-1440.40	1959.31	0.61
10403.00	89.34	142.21	6642.74	2416.05	-1511.85	2014.02	0.80
10492.00	89.74	143.35	6643.45	2505.04	-1582.72	2067.86	1.36
10582.00	89.68	142.25	6643.91	2595.03	-1654.41	2122.27	1.22

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10672.00	89.91	142.10	6644.23	2685.02	-1725.50	2177.46	0.31
10761.00	89.54	142.59	6644.66	2774.00	-1795.96	2231.83	0.69
10851.00	88.74	143.04	6646.01	2863.99	-1867.65	2286.22	1.02
10940.00	89.37	143.16	6647.48	2952.98	-1938.81	2339.65	0.72
11030.00	89.84	142.73	6648.10	3042.97	-2010.64	2393.88	0.71
11119.00	90.15	143.50	6648.10	3131.97	-2081.82	2447.30	0.93
11209.00	89.74	142.17	6648.19	3221.97	-2153.54	2501.67	1.55
11298.00	88.30	140.74	6649.71	3310.90	-2223.14	2557.11	2.28
11388.00	89.68	143.10	6651.30	3400.86	-2293.96	2612.61	3.04
11477.00	89.68	143.22	6651.80	3489.85	-2365.19	2665.97	0.13
11567.00	89.91	144.76	6652.12	3579.84	-2437.99	2718.88	1.73
11656.00	89.04	143.80	6652.93	3668.82	-2510.24	2770.84	1.46
11746.00	89.11	143.25	6654.39	3758.81	-2582.60	2824.33	0.62
11835.00	88.97	143.23	6655.88	3847.80	-2653.89	2877.59	0.16
11924.00	89.14	143.73	6657.35	3936.79	-2725.41	2930.55	0.59
12014.00	89.51	143.92	6658.41	4026.78	-2798.05	2983.67	0.46
12103.00	89.44	144.19	6659.22	4115.76	-2870.10	3035.91	0.31
12192.00	88.80	144.27	6660.59	4204.74	-2942.31	3087.92	0.72
12282.00	89.38	143.55	6662.02	4294.72	-3015.02	3140.93	1.03
12372.00	89.07	144.29	6663.24	4384.71	-3087.75	3193.93	0.89
12461.00	89.17	143.85	6664.60	4473.69	-3159.81	3246.15	0.51
12551.00	89.91	143.96	6665.32	4563.68	-3232.53	3299.17	0.83
12641.00	89.34	144.43	6665.91	4653.67	-3305.52	3351.82	0.82
12730.00	89.37	143.34	6666.92	4742.65	-3377.41	3404.27	1.23
12820.00	89.51	143.65	6667.80	4832.65	-3449.75	3457.81	0.38
12910.00	88.00	143.35	6669.75	4922.62	-3522.08	3511.33	1.71
12999.00	89.51	143.82	6671.68	5011.60	-3593.68	3564.15	1.78
13089.00	89.78	143.85	6672.24	5101.59	-3666.34	3617.26	0.30
13178.00	89.31	143.61	6672.95	5190.59	-3738.09	3669.91	0.59
13268.00	89.17	143.93	6674.14	5280.58	-3810.69	3723.09	0.39
13357.00	89.48	143.80	6675.19	5369.56	-3882.56	3775.57	0.38
13447.00	89.34	143.81	6676.12	5459.56	-3955.19	3828.72	0.16
13536.00	88.91	143.92	6677.48	5548.54	-4027.06	3881.19	0.50

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13626.00	89.24	143.83	6678.93	5638.52	-4099.74	3934.25	0.38
13715.00	89.68	144.19	6679.77	5727.51	-4171.75	3986.54	0.64
13805.00	89.21	143.69	6680.64	5817.50	-4244.50	4039.52	0.76
13894.00	89.38	143.62	6681.74	5906.49	-4316.18	4092.26	0.21
13984.00	89.38	144.01	6682.71	5996.48	-4388.82	4145.39	0.43
14073.00	89.51	143.64	6683.57	6085.48	-4460.66	4197.92	0.44
14163.00	89.31	143.93	6684.50	6175.47	-4533.27	4251.09	0.39
14252.00	89.37	143.86	6685.52	6264.46	-4605.17	4303.53	0.10
14342.00	89.51	143.22	6686.40	6354.45	-4677.55	4357.01	0.73
14431.00	89.27	142.18	6687.35	6443.44	-4748.34	4410.94	1.20
14521.00	89.31	143.13	6688.47	6533.43	-4819.89	4465.53	1.06
14610.00	89.48	141.93	6689.41	6622.41	-4890.52	4519.67	1.36
14700.00	89.41	142.37	6690.28	6712.39	-4961.58	4574.89	0.50
14789.00	88.74	141.99	6691.71	6801.36	-5031.87	4629.46	0.87
14879.00	89.17	142.74	6693.36	6891.33	-5103.13	4684.41	0.96
14969.00	89.21	142.78	6694.63	6981.32	-5174.78	4738.86	0.06
15058.00	89.64	143.05	6695.52	7070.31	-5245.77	4792.53	0.57
15147.00	89.34	143.51	6696.31	7159.31	-5317.11	4845.74	0.62
15237.00	89.24	142.75	6697.43	7249.30	-5389.10	4899.74	0.85
15326.00	88.97	142.45	6698.82	7338.29	-5459.80	4953.79	0.45
15416.00	89.64	142.75	6699.91	7428.27	-5531.29	5008.44	0.82
15505.00	89.54	143.33	6700.55	7517.27	-5602.40	5061.95	0.66
15595.00	89.74	142.63	6701.11	7607.27	-5674.26	5116.14	0.81
15684.00	89.41	142.75	6701.77	7696.26	-5745.04	5170.09	0.39
15773.00	89.54	142.36	6702.59	7785.25	-5815.70	5224.20	0.46
15863.00	89.48	143.32	6703.36	7875.24	-5887.42	5278.56	1.07
15952.00	89.91	142.16	6703.83	7964.23	-5958.26	5332.44	1.39
16042.00	89.84	142.33	6704.03	8054.22	-6029.41	5387.54	0.20
16131.00	90.15	142.34	6704.04	8143.21	-6099.87	5441.93	0.35
16221.00	90.48	143.03	6703.54	8233.20	-6171.44	5496.48	0.85
16311.00	89.81	142.73	6703.31	8323.20	-6243.20	5550.80	0.82
16400.00	90.42	142.33	6703.13	8412.19	-6313.84	5604.94	0.82

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16489.00	90.52	142.36	6702.40	8501.17	-6384.30	5659.31	0.12
16578.00	89.24	142.31	6702.59	8590.16	-6454.75	5713.69	1.44
16668.00	89.71	143.78	6703.42	8680.15	-6526.67	5767.79	1.71
16757.00	89.38	143.43	6704.12	8769.15	-6598.30	5820.60	0.54
16847.00	89.95	144.41	6704.65	8859.14	-6671.04	5873.60	1.26
16936.00	89.64	143.78	6704.97	8948.13	-6743.13	5925.79	0.79
17026.00	89.28	143.76	6705.82	9038.12	-6815.72	5978.98	0.40
17115.00	89.44	143.85	6706.81	9127.11	-6887.54	6031.54	0.21
17205.00	89.41	143.55	6707.71	9217.10	-6960.07	6084.81	0.33
17294.00	89.65	143.11	6708.44	9306.10	-7031.45	6137.96	0.56
17383.00	89.41	143.41	6709.17	9395.10	-7102.77	6191.20	0.43
17473.00	89.85	143.64	6709.75	9485.09	-7175.14	6244.70	0.55
17562.00	89.55	143.28	6710.22	9574.09	-7246.65	6297.69	0.53
17651.00	89.58	143.78	6710.90	9663.09	-7318.22	6350.59	0.56
17741.00	90.18	143.50	6711.08	9753.09	-7390.69	6403.95	0.74
17830.00	90.12	143.43	6710.85	9842.09	-7462.20	6456.93	0.10
17920.00	90.96	143.48	6710.00	9932.08	-7534.50	6510.52	0.93
18010.00	90.75	143.87	6708.66	10022.07	-7607.01	6563.82	0.49
18099.00	90.65	143.80	6707.57	10111.06	-7678.85	6616.34	0.14
18189.00	91.06	143.63	6706.23	10201.04	-7751.39	6669.60	0.49
18278.00	90.96	143.16	6704.66	10290.03	-7822.83	6722.66	0.54
18368.00	90.82	143.93	6703.26	10380.02	-7895.21	6776.13	0.87
18458.00	89.31	144.53	6703.16	10470.00	-7968.23	6828.73	1.81
18547.00	89.65	143.84	6703.97	10558.99	-8040.39	6880.81	0.86
18637.00	88.44	144.24	6705.47	10648.96	-8113.23	6933.65	1.42
18726.00	88.64	143.81	6707.74	10737.93	-8185.23	6985.92	0.53
18816.00	89.24	143.47	6709.40	10827.91	-8257.70	7039.27	0.77
18905.00	87.19	143.09	6712.17	10916.86	-8329.00	7092.45	2.34
18995.00	88.57	143.65	6715.50	11006.80	-8401.17	7146.11	1.65
19084.00	88.81	144.04	6717.54	11095.77	-8473.02	7198.60	0.51
19174.00	88.50	143.49	6719.65	11185.74	-8545.59	7251.79	0.70
19263.00	88.74	143.73	6721.79	11274.71	-8617.21	7304.57	0.38
19353.00	88.71	143.98	6723.80	11364.69	-8689.87	7357.65	0.28

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19442.00	88.71	143.51	6725.80	11453.66	-8761.62	7410.26	0.53
19532.00	88.50	143.75	6727.99	11543.63	-8834.07	7463.62	0.35
19621.00	89.68	143.85	6729.40	11632.62	-8905.88	7516.17	1.33
19711.00	89.65	142.90	6729.93	11722.61	-8978.11	7569.86	1.06
19800.00	89.48	142.86	6730.61	11811.61	-9049.07	7623.57	0.20
19890.00	89.81	142.43	6731.16	11901.60	-9120.61	7678.18	0.60
19979.00	89.68	142.60	6731.56	11990.59	-9191.23	7732.34	0.24
20068.00	89.78	142.77	6731.98	12079.59	-9262.01	7786.29	0.22
20158.00	89.68	142.94	6732.40	12169.58	-9333.75	7840.64	0.22
20247.00	89.85	142.16	6732.77	12258.57	-9404.41	7894.75	0.90
20336.00	89.65	142.59	6733.16	12347.56	-9474.90	7949.09	0.53
20426.00	89.65	142.66	6733.71	12437.55	-9546.42	8003.72	0.08
20515.00	89.71	142.80	6734.20	12526.55	-9617.24	8057.61	0.17
20574.00	89.71	142.19	6734.50	12585.54	-9664.04	8093.53	1.03
20596.00	89.71	142.19	6734.61	12607.54	-9681.42	8107.02	0.00

10/23/2026
