Well Location Plat

CNX Applicant / Well Operator Name	**DEP ID#**	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	**Well #** **MAJ8DHSM**

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8DHSM OH As Drilled_ KOP	5990.29	39.93009214	-80.57127084	6220.00
MAJ8DHSM OH As Drilled_ LP	6629.19	39.92856305	-80.56867083	7473.00
MAJ8DHSM OH As Drilled_BHL	6742.12	39.90287812	-80.54317258	19251.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1054.50	Survey #1 (OH)	GYD_CT+WIR
1190.50	19251.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

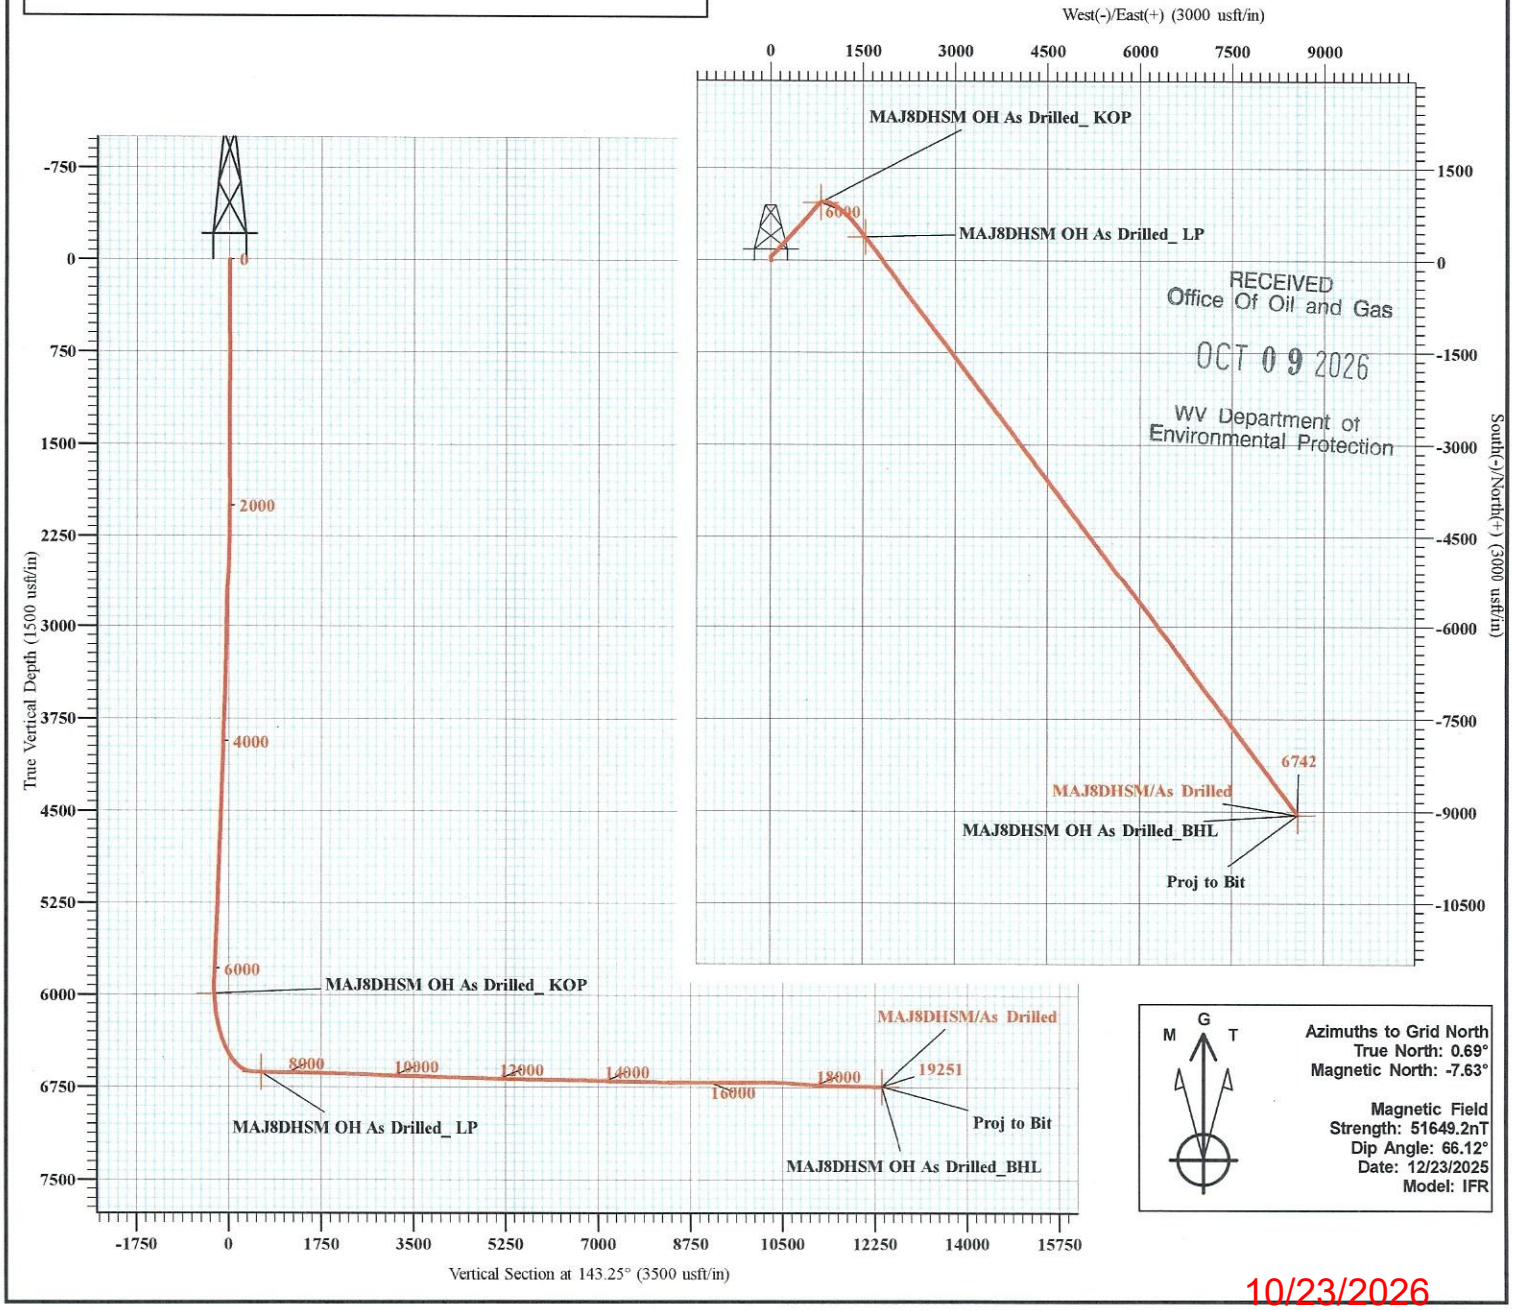


RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

Azimuths to Grid North
True North: 0.69°
Magnetic North: -7.63°

Magnetic Field
Strength: 51649.2nT
Dip Angle: 66.12°
Date: 12/23/2025
Model: IFR

10/23/2026

DECEMBER 24 2025
SURVEY REPORT

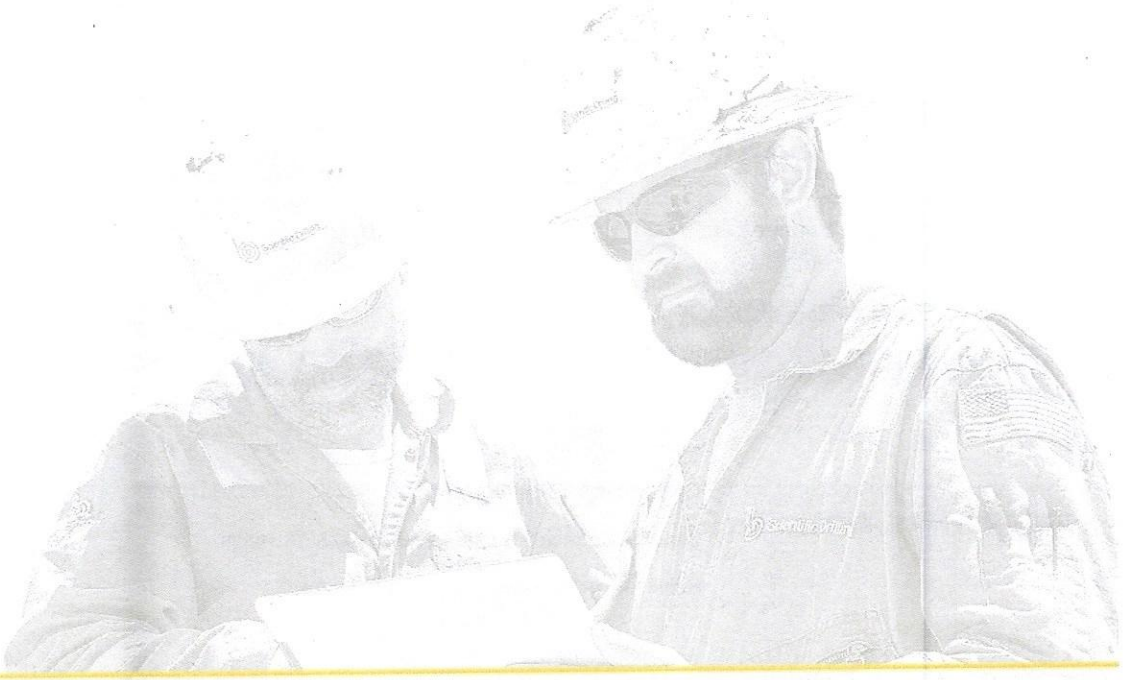

CNX RESOURCES
WELL: MAJ8 DHSM
RIG: PD 539

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

CUSTOMER	**CNX Resources**	SDI JOB NO.	**OP.051494**
PROJECT	**MAJ8 DHSM**	SDI DISTRICT	**Northeast**
FIELD	**Marcellus**	SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**	Section	-
Lat/Long	**39.927526 N, 80.574227 W**	Township	-
Northing	**521,744.52 ft**	Range	-
Easting	**1,698,736.42 ft**		

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.927459 N, 80.574114 W**
Northing	**521,719.75 ft**
Easting	**1,698,767.83 ft**
UWI	**47-051-02545**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.25°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-19251 ft	IFR1	23 Dec 2025	-8.32°	add 0.69°	subtract 7.63°

WELL NOTES

Gyro Surveys From 0' To 1054.5'

Superior Corrected Surveys From 1190.5' To 19229'

Survey At 19251' Is A Projection To The Bit

OPERATORS

SDI Operator Name (Printed) SIGNATURE DATE

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.27	48.31	54.50	-0.01	0.09	0.10	0.50
104.50	0.20	32.80	104.50	-0.05	0.24	0.23	0.19
154.50	0.27	34.29	154.50	-0.12	0.41	0.34	0.14
204.50	0.23	123.71	204.50	-0.06	0.45	0.49	0.71
254.50	0.32	122.80	254.50	0.16	0.32	0.70	0.18
304.50	0.34	116.01	304.50	0.42	0.18	0.95	0.09
354.50	0.36	110.27	354.50	0.69	0.06	1.23	0.08
404.50	0.49	104.05	404.49	0.99	-0.05	1.58	0.28
454.50	0.44	118.38	454.49	1.32	-0.19	1.96	0.25
504.50	0.40	105.42	504.49	1.64	-0.33	2.30	0.21
554.50	0.42	118.69	554.49	1.94	-0.46	2.62	0.19
604.50	0.40	126.02	604.49	2.27	-0.65	2.93	0.11
654.50	0.34	136.99	654.49	2.59	-0.87	3.17	0.19
704.50	0.26	116.34	704.49	2.84	-1.02	3.37	0.27
754.50	0.42	92.10	754.49	3.05	-1.08	3.66	0.42
804.50	0.44	63.31	804.49	3.20	-1.00	4.01	0.43
854.50	0.35	87.50	854.48	3.32	-0.91	4.33	0.37
904.50	0.40	95.07	904.48	3.52	-0.92	4.66	0.14
954.50	0.36	94.54	954.48	3.74	-0.95	4.99	0.08
1004.50	0.30	89.04	1004.48	3.92	-0.96	5.28	0.14
1054.50	0.35	98.66	1054.48	4.11	-0.98	5.56	0.15
1190.50	0.56	345.10	1190.48	3.79	-0.40	5.80	0.57
1278.50	1.06	333.44	1278.47	2.59	0.75	5.33	0.60
1363.50	1.11	326.78	1363.45	0.99	2.14	4.52	0.16
1450.50	0.37	316.95	1450.45	-0.13	3.05	3.87	0.86
1538.50	0.26	159.21	1538.45	-0.22	3.07	3.75	0.70
1624.50	0.52	144.72	1624.44	0.36	2.57	4.04	0.32
1710.50	0.82	159.51	1710.44	1.34	1.67	4.48	0.40
1796.50	1.13	150.61	1796.42	2.77	0.36	5.11	0.40
1884.50	0.99	164.33	1884.41	4.34	-1.13	5.75	0.33
1970.50	0.61	221.84	1970.40	5.13	-2.19	5.64	0.98
2057.50	0.92	264.37	2057.40	4.86	-2.60	4.64	0.72

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2142.50	1.16	292.78	2142.38	3.76	-2.33	3.16	0.66
2209.50	1.42	305.46	2209.37	2.39	-1.59	1.86	0.57
2261.00	1.40	297.09	2260.85	1.22	-0.93	0.78	0.40
2305.00	1.46	298.00	2304.84	0.23	-0.42	-0.19	0.15
2350.00	2.06	334.55	2349.82	-1.09	0.58	-1.04	2.76
2440.00	7.44	357.94	2439.48	-7.47	7.86	-1.95	6.23
2529.00	7.43	355.97	2527.73	-17.05	19.36	-2.56	0.29
2619.00	7.71	355.18	2616.95	-27.07	31.18	-3.48	0.33
2708.00	8.32	358.24	2705.08	-37.41	43.57	-4.18	0.84
2798.00	7.95	24.00	2794.20	-45.79	55.77	-1.84	4.04
2887.00	10.37	46.57	2882.09	-49.73	66.90	6.48	4.82
2977.00	12.22	47.82	2970.34	-51.57	78.87	19.42	2.07
3066.00	14.35	46.66	3056.95	-53.73	92.76	34.42	2.41
3155.00	16.78	46.56	3142.68	-56.49	109.17	51.78	2.73
3245.00	17.66	45.98	3228.65	-59.73	127.59	71.03	1.00
3335.00	19.48	41.23	3313.96	-64.59	148.36	90.74	2.63
3424.00	22.00	42.85	3397.19	-70.69	171.75	111.86	2.90
3514.00	21.93	41.98	3480.66	-77.02	196.60	134.56	0.37
3603.00	22.08	42.28	3563.17	-83.45	221.33	156.93	0.21
3693.00	22.01	42.10	3646.59	-89.93	246.36	179.62	0.11
3782.00	22.01	42.36	3729.11	-96.30	271.06	202.04	0.11
3872.00	21.90	42.12	3812.58	-102.73	295.97	224.66	0.16
3961.00	21.68	41.94	3895.22	-109.16	320.51	246.78	0.26
4051.00	21.70	42.44	3978.85	-115.54	345.16	269.12	0.21
4141.00	21.73	42.23	4062.46	-121.84	369.77	291.54	0.09
4230.00	21.65	42.05	4145.16	-128.18	394.16	313.61	0.12
4320.00	21.66	42.12	4228.81	-134.61	418.81	335.87	0.03
4409.00	21.67	42.20	4311.52	-140.93	443.16	357.92	0.04
4499.00	21.69	42.26	4395.16	-147.29	467.78	380.27	0.03
4588.00	21.74	42.22	4477.84	-153.58	492.16	402.41	0.06
4678.00	22.13	42.38	4561.33	-159.96	517.03	425.03	0.44
4768.00	22.10	41.81	4644.70	-166.52	542.17	447.75	0.24

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4857.00	21.96	41.16	4727.21	-173.32	567.18	469.86	0.32
4947.00	21.99	41.12	4810.67	-180.39	592.54	492.02	0.04
5036.00	22.13	41.53	4893.15	-187.29	617.64	514.09	0.23
5125.00	22.22	41.40	4975.57	-194.16	642.81	536.33	0.12
5215.00	22.06	41.43	5058.93	-201.11	668.25	558.77	0.18
5304.00	22.10	40.98	5141.41	-208.09	693.42	580.81	0.20
5394.00	22.12	41.14	5224.79	-215.25	718.96	603.06	0.07
5483.00	21.95	40.16	5307.29	-222.53	744.30	624.81	0.46
5573.00	22.01	39.78	5390.74	-230.27	770.11	646.45	0.17
5662.00	22.19	39.73	5473.21	-238.08	795.85	667.86	0.20
5751.00	21.95	39.74	5555.68	-245.90	821.57	689.24	0.27
5841.00	22.11	40.24	5639.11	-253.64	847.43	710.94	0.27
5931.00	22.15	39.77	5722.48	-261.41	873.40	732.73	0.20
6020.00	22.19	39.79	5804.90	-269.23	899.21	754.22	0.05
6109.00	22.04	39.69	5887.36	-277.06	924.98	775.64	0.17
6199.00	22.23	62.17	5970.87	-278.38	945.96	801.53	9.36
6289.00	23.73	74.86	6053.78	-269.06	958.64	834.08	5.74
6378.00	26.53	93.43	6134.47	-249.61	962.14	871.28	9.36
6468.00	31.46	103.16	6213.21	-218.64	955.58	914.26	7.57
6557.00	36.45	113.00	6287.07	-177.97	939.94	961.28	8.33
6647.00	41.66	118.52	6356.96	-127.66	915.19	1012.22	6.96
6736.00	48.50	124.71	6419.79	-69.10	882.03	1065.70	9.12
6825.00	53.60	129.68	6475.75	-2.61	840.14	1120.72	7.19
6915.00	60.47	130.58	6524.69	70.89	791.48	1178.40	7.68
7004.00	67.25	133.05	6563.88	149.15	738.21	1237.88	8.01
7093.00	72.82	139.43	6594.28	232.10	677.80	1295.61	9.19
7183.00	80.32	139.41	6615.17	319.39	611.36	1352.52	8.33
7272.00	86.37	143.17	6625.49	407.68	542.42	1407.75	7.99
7362.00	89.66	142.00	6628.60	497.60	470.99	1462.39	3.88
7451.00	89.73	141.50	6629.08	586.57	401.10	1517.49	0.57
7541.00	89.49	142.08	6629.69	676.54	330.38	1573.16	0.70
7630.00	89.22	142.46	6630.69	765.52	260.00	1627.62	0.52
7719.00	89.49	143.82	6631.69	854.51	188.79	1681.00	1.56

RECEIVED
Office Of Oil and Gas

OCT 09 2026
WV Department of
Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7809.00	89.46	143.95	6632.52	944.50	116.09	1734.05	0.15
7898.00	89.83	143.81	6633.07	1033.50	44.20	1786.51	0.44
7988.00	89.66	143.79	6633.47	1123.49	-28.43	1839.66	0.19
8077.00	89.35	144.18	6634.24	1212.48	-100.41	1891.99	0.56
8167.00	89.95	144.71	6634.79	1302.46	-173.63	1944.32	0.89
8257.00	89.25	144.06	6635.42	1392.44	-246.79	1996.73	1.06
8346.00	89.99	142.41	6636.01	1481.43	-318.09	2050.00	2.03
8436.00	89.55	144.13	6636.37	1571.43	-390.21	2103.82	1.97
8525.00	89.45	143.03	6637.15	1660.42	-461.83	2156.66	1.24
8614.00	89.28	143.87	6638.13	1749.41	-533.32	2209.65	0.96
8704.00	89.95	144.57	6638.74	1839.40	-606.33	2262.27	1.08
8793.00	89.69	142.78	6639.02	1928.39	-678.03	2314.99	2.03
8883.00	88.95	142.29	6640.08	2018.38	-749.46	2369.73	0.99
8972.00	89.65	143.30	6641.17	2107.37	-820.34	2423.54	1.38
9062.00	89.72	143.34	6641.67	2197.37	-892.52	2477.30	0.09
9151.00	89.55	143.29	6642.23	2286.36	-963.89	2530.47	0.20
9241.00	89.38	143.14	6643.07	2376.36	-1035.97	2584.36	0.25
9330.00	89.25	143.23	6644.14	2465.35	-1107.21	2637.69	0.18
9420.00	88.31	140.77	6646.05	2555.30	-1178.11	2693.08	2.93
9510.00	88.74	143.35	6648.37	2645.25	-1249.06	2748.39	2.91
9599.00	88.88	142.67	6650.22	2734.23	-1320.13	2801.93	0.78
9689.00	89.21	143.36	6651.72	2824.21	-1392.01	2856.07	0.85
9778.00	88.91	143.03	6653.18	2913.20	-1463.26	2909.38	0.50
9867.00	89.05	143.48	6654.76	3002.19	-1534.57	2962.62	0.53
9957.00	89.31	142.90	6656.05	3092.18	-1606.62	3016.53	0.71
10046.00	89.45	143.52	6657.02	3181.17	-1677.89	3069.83	0.71
10136.00	88.91	143.19	6658.30	3271.16	-1750.09	3123.54	0.70
10225.00	89.14	143.33	6659.82	3360.15	-1821.40	3176.77	0.30
10314.00	89.41	142.46	6660.94	3449.14	-1892.38	3230.46	1.02
10404.00	89.21	143.43	6662.03	3539.13	-1964.19	3284.69	1.10
10493.00	89.08	143.15	6663.36	3628.12	-2035.54	3337.88	0.35
10583.00	89.35	143.10	6664.59	3718.11	-2107.52	3391.88	0.31

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10672.00	89.01	143.36	6665.86	3807.10	-2178.81	3445.15	0.48
10762.00	88.91	143.27	6667.50	3897.09	-2250.97	3498.91	0.15
10851.00	89.11	142.94	6669.03	3986.07	-2322.14	3552.34	0.43
10941.00	89.38	141.66	6670.22	4076.05	-2393.34	3607.37	1.45
11031.00	89.45	142.45	6671.14	4166.02	-2464.31	3662.71	0.88
11120.00	89.45	142.73	6671.99	4255.01	-2535.00	3716.77	0.31
11210.00	89.48	143.12	6672.83	4345.01	-2606.80	3771.03	0.43
11299.00	89.04	143.19	6673.98	4434.00	-2678.02	3824.39	0.50
11388.00	89.51	143.39	6675.11	4522.99	-2749.36	3877.59	0.57
11478.00	89.28	143.49	6676.06	4612.99	-2821.65	3931.19	0.28
11567.00	89.28	143.50	6677.18	4701.98	-2893.18	3984.14	0.01
11657.00	89.45	143.41	6678.17	4791.97	-2965.48	4037.72	0.21
11746.00	89.28	143.59	6679.16	4880.97	-3037.02	4090.66	0.28
11836.00	89.18	143.17	6680.37	4970.96	-3109.25	4144.34	0.48
11925.00	89.31	143.40	6681.54	5059.95	-3180.59	4197.54	0.30
12015.00	89.31	143.36	6682.63	5149.94	-3252.82	4251.22	0.04
12104.00	88.91	142.60	6684.01	5238.93	-3323.87	4304.80	0.96
12193.00	89.41	143.04	6685.31	5327.92	-3394.77	4358.58	0.75
12283.00	89.58	143.45	6686.11	5417.92	-3466.88	4412.44	0.49
12373.00	89.55	143.55	6686.79	5507.91	-3539.22	4465.97	0.12
12462.00	89.81	143.16	6687.29	5596.91	-3610.63	4519.09	0.53
12552.00	89.51	143.07	6687.82	5686.91	-3682.61	4573.10	0.35
12642.00	89.75	143.18	6688.40	5776.91	-3754.61	4627.11	0.29
12731.00	89.58	142.70	6688.92	5865.90	-3825.63	4680.74	0.57
12821.00	89.78	143.43	6689.43	5955.90	-3897.56	4734.83	0.84
12910.00	89.61	143.89	6689.90	6044.90	-3969.25	4787.56	0.55
13000.00	89.75	143.55	6690.40	6134.89	-4041.80	4840.82	0.41
13090.00	89.88	143.77	6690.69	6224.89	-4114.30	4894.15	0.28
13179.00	89.95	142.62	6690.83	6313.89	-4185.56	4947.47	1.29
13269.00	89.41	143.46	6691.33	6403.88	-4257.47	5001.58	1.11
13358.00	89.24	143.22	6692.38	6492.88	-4328.86	5054.72	0.33
13448.00	89.68	143.63	6693.22	6582.87	-4401.14	5108.34	0.67
13537.00	89.38	143.63	6693.95	6671.87	-4472.80	5161.12	0.34

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13627.00	89.71	143.94	6694.67	6761.86	-4545.41	5214.29	0.50
13716.00	89.48	143.34	6695.30	6850.86	-4617.08	5267.05	0.72
13806.00	89.31	142.93	6696.25	6940.85	-4689.08	5321.04	0.49
13895.00	89.38	143.21	6697.27	7029.84	-4760.22	5374.51	0.32
13985.00	89.28	143.09	6698.32	7119.84	-4832.23	5428.48	0.17
14074.00	89.48	143.83	6699.28	7208.83	-4903.73	5481.47	0.86
14164.00	89.51	143.82	6700.08	7298.82	-4976.38	5534.59	0.04
14253.00	89.34	143.27	6700.97	7387.82	-5047.96	5587.47	0.65
14343.00	89.14	143.58	6702.16	7477.81	-5120.23	5641.09	0.41
14432.00	89.51	143.17	6703.21	7566.80	-5191.65	5694.19	0.62
14522.00	89.44	143.32	6704.04	7656.80	-5263.76	5748.04	0.18
14611.00	89.41	143.65	6704.93	7745.79	-5335.28	5800.99	0.37
14701.00	89.65	142.73	6705.67	7835.79	-5407.34	5854.92	1.06
14790.00	89.61	143.20	6706.24	7924.79	-5478.38	5908.52	0.53
14880.00	89.75	142.80	6706.74	8014.78	-5550.26	5962.68	0.47
14969.00	89.44	143.33	6707.37	8103.78	-5621.39	6016.16	0.69
15059.00	89.38	143.41	6708.30	8193.78	-5693.62	6069.86	0.11
15148.00	89.65	143.53	6709.05	8282.77	-5765.13	6122.83	0.33
15238.00	90.79	145.03	6708.71	8372.75	-5838.19	6175.37	2.09
15327.00	90.18	144.00	6707.95	8461.73	-5910.66	6227.03	1.34
15417.00	90.15	143.96	6707.70	8551.72	-5983.45	6279.96	0.06
15506.00	90.18	143.53	6707.44	8640.71	-6055.22	6332.59	0.48
15596.00	89.11	143.72	6708.00	8730.71	-6127.68	6385.97	1.21
15685.00	88.81	142.64	6709.61	8819.69	-6198.92	6439.29	1.26
15774.00	90.12	143.40	6710.44	8908.69	-6270.01	6492.83	1.70
15864.00	89.81	144.13	6710.50	8998.68	-6342.60	6546.03	0.88
15953.00	90.45	143.21	6710.30	9087.68	-6414.30	6598.75	1.26
16042.00	90.52	143.52	6709.54	9176.67	-6485.72	6651.86	0.36
16132.00	89.68	143.33	6709.39	9266.67	-6557.99	6705.49	0.96
16222.00	90.15	144.41	6709.52	9356.67	-6630.68	6758.55	1.31
16311.00	90.08	143.68	6709.34	9445.66	-6702.72	6810.81	0.82
16401.00	90.22	143.32	6709.10	9535.65	-6775.07	6864.34	0.43

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16490.00	90.15	143.03	6708.82	9624.65	-6846.31	6917.68	0.34
16579.00	90.15	143.34	6708.58	9713.65	-6917.56	6971.02	0.35
16669.00	90.21	143.39	6708.30	9803.65	-6989.78	7024.72	0.09
16758.00	90.15	142.40	6708.02	9892.65	-7060.76	7078.41	1.11
16848.00	90.01	142.57	6707.90	9982.64	-7132.15	7133.22	0.24
16937.00	90.35	143.37	6707.62	10071.64	-7203.20	7186.82	0.98
17026.00	89.95	142.94	6707.38	10160.64	-7274.42	7240.18	0.66
17116.00	89.04	143.31	6708.18	10250.63	-7346.41	7294.19	1.09
17205.00	89.27	143.15	6709.49	10339.62	-7417.70	7347.46	0.31
17295.00	90.01	142.92	6710.06	10429.62	-7489.61	7401.58	0.86
17384.00	88.74	142.98	6711.03	10518.61	-7560.63	7455.19	1.43
17478.00	88.17	143.01	6713.56	10612.58	-7635.67	7511.75	0.61
17568.00	88.10	143.25	6716.49	10702.53	-7707.63	7565.72	0.28
17657.00	88.07	143.10	6719.46	10791.48	-7778.84	7619.04	0.17
17746.00	88.84	142.14	6721.86	10880.44	-7849.53	7673.05	1.38
17836.00	87.46	142.97	6724.77	10970.38	-7920.95	7727.74	1.79
17925.00	88.30	142.81	6728.06	11059.32	-7991.87	7781.40	0.96
18015.00	88.14	143.47	6730.86	11149.28	-8063.85	7835.36	0.75
18105.00	88.84	142.29	6733.23	11239.24	-8135.58	7889.65	1.52
18194.00	89.71	143.30	6734.35	11328.23	-8206.46	7943.46	1.50
18284.00	89.21	143.63	6735.20	11418.22	-8278.77	7997.04	0.67
18373.00	89.51	143.79	6736.20	11507.21	-8350.51	8049.71	0.38
18463.00	89.48	143.33	6736.99	11597.21	-8422.91	8103.17	0.51
18553.00	89.48	143.58	6737.81	11687.21	-8495.21	8156.76	0.28
18642.00	89.48	143.99	6738.61	11776.20	-8567.01	8209.34	0.46
18732.00	89.65	142.54	6739.30	11866.19	-8639.13	8263.16	1.62
18821.00	89.58	142.91	6739.90	11955.19	-8709.95	8317.07	0.42
18911.00	89.58	143.80	6740.56	12045.18	-8782.16	8370.78	0.99
19000.00	89.61	143.62	6741.18	12134.18	-8853.90	8423.46	0.21
19090.00	89.81	143.41	6741.64	12224.18	-8926.26	8476.97	0.32
19179.00	89.78	143.44	6741.96	12313.18	-8997.73	8530.00	0.05
19229.00	89.92	143.27	6742.09	12363.17	-9037.85	8559.85	0.44
19251.00	89.92	143.27	6742.12	12385.17	-9055.48	8573.00	0.00

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection
10/23/2026
