Well Location Plat

CNX Applicant / Well Operator Name	DEP ID#	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	Well # MAJ8EHSM

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8EHSM OH As Drilled_ KOP	5716.05	39.93316140	-80.57278468	6488.00
MAJ8EHSM OH As Drilled_ LP	6617.62	39.93296089	-80.56968563	8008.00
MAJ8EHSM OH As Drilled_BHL	6756.77	39.90092816	-80.53782260	22708.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1081.50	Survey #1 (OH)	GYD_CT+WIR
1189.50	22708.00	Survey #2 (OH)	MWD+IFR1+SAG+FDIR

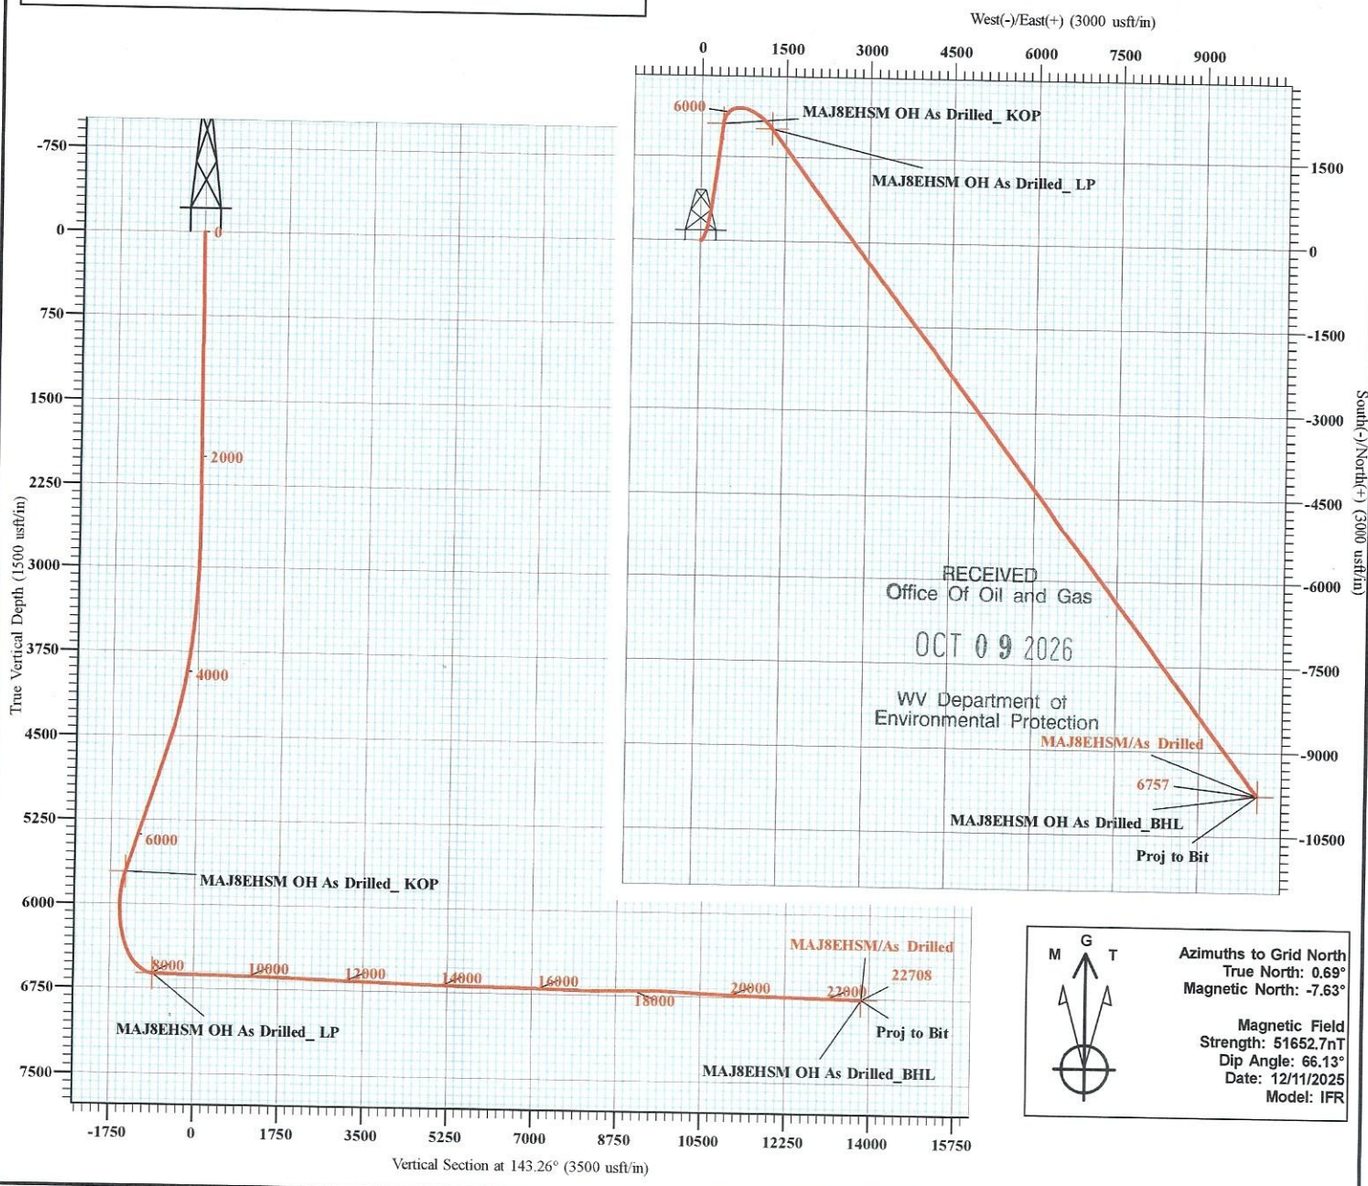

Azimuths to Grid North
True North: 0.69°
Magnetic North: -7.63°

Magnetic Field
Strength: 51652.7nT
Dip Angle: 66.13°
Date: 12/11/2025
Model: IFR

10/23/2026

CUSTOMER	**CNX Resources**	SDI JOB NO.	**OP.051149**
PROJECT	**MAJ8 EHSM**	SDI DISTRICT	**Northeast**
FIELD	**Marcellus**	SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**	Section	-
Lat/Long	**39.9275261 N, 80.5742268 W**	Township	-
Northing	**521,744.52 ft**	Range	-
Easting	**1,698,736.42 ft**		

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.927426 N, 80.5740571 W**
Northing	**521,707.46 ft**
Easting	**1,698,783.58 ft**
UWI	**47-051-02546-00-00**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.26°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-22708 ft	IFR1	11 Dec 2025	-8.32°	add 0.69°	subtract 7.63°

WELL NOTES

Gyro Surveys From 0' to 1081.5'

Superior Corrected Surveys From 1081.5' to 22686'

Survey @ 22708' Is a Porjection To The Bit at TD

OPERATORS

SDI Operator Name (Printed) SIGNATURE DATE

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.45	30.95	54.50	-0.08	0.18	0.11	0.83
104.50	0.61	64.73	104.50	-0.10	0.47	0.45	0.69
154.50	0.63	72.96	154.49	0.04	0.66	0.96	0.18
204.50	0.60	80.11	204.49	0.25	0.79	1.48	0.16
254.50	0.51	81.46	254.49	0.48	0.86	1.95	0.18
304.50	0.68	84.49	304.49	0.74	0.92	2.47	0.35
354.50	0.56	84.82	354.48	1.02	0.98	3.01	0.24
404.50	0.56	86.84	404.48	1.28	1.01	3.50	0.04
454.50	0.58	95.93	454.48	1.59	1.00	3.99	0.19
504.50	0.62	94.56	504.48	1.94	0.95	4.51	0.08
554.50	0.52	104.60	554.47	2.29	0.87	5.00	0.28
604.50	0.54	108.76	604.47	2.66	0.74	5.44	0.09
654.50	0.49	103.66	654.47	3.02	0.61	5.88	0.14
704.50	0.53	102.37	704.47	3.36	0.51	6.31	0.08
754.50	0.47	102.75	754.47	3.69	0.42	6.73	0.12
804.50	0.51	96.72	804.46	4.00	0.35	7.16	0.13
854.50	0.39	87.85	854.46	4.25	0.33	7.55	0.28
904.50	0.34	93.60	904.46	4.45	0.32	7.86	0.12
954.50	0.26	82.63	954.46	4.60	0.33	8.13	0.20
1004.50	0.12	69.60	1004.46	4.67	0.36	8.29	0.29
1054.50	0.13	91.47	1054.46	4.72	0.38	8.39	0.10
1081.50	0.17	120.41	1081.46	4.77	0.36	8.46	0.31
1189.50	0.34	296.75	1189.46	4.63	0.42	8.31	0.47
1277.50	0.73	306.79	1277.46	3.86	0.87	7.63	0.45
1362.50	0.85	309.36	1362.45	2.73	1.60	6.71	0.15
1450.50	1.05	299.95	1450.44	1.36	2.41	5.50	0.29
1538.50	0.11	351.32	1538.43	0.54	2.90	4.79	1.12
1623.50	0.33	191.90	1623.43	0.63	2.74	4.73	0.51
1710.50	0.52	168.96	1710.43	1.15	2.11	4.75	0.29
1795.50	0.57	160.87	1795.42	1.90	1.33	4.97	0.11
1883.50	0.80	170.92	1883.42	2.86	0.31	5.21	0.29
1970.50	1.01	163.38	1970.41	4.12	-1.02	5.52	0.28

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2056.50	1.17	162.12	2056.39	5.67	-2.59	6.01	0.19
2142.50	1.19	163.68	2142.37	7.33	-4.28	6.53	0.04
2209.50	1.40	157.37	2209.36	8.78	-5.70	7.04	0.38
2262.00	1.13	141.43	2261.84	9.92	-6.70	7.61	0.84
2351.00	1.73	100.71	2350.82	11.79	-7.63	9.48	1.28
2441.00	2.13	50.16	2440.77	12.70	-6.81	12.09	1.87
2530.00	3.28	54.22	2529.67	12.65	-4.27	15.43	1.31
2619.00	4.11	42.23	2618.49	12.08	-0.42	19.64	1.27
2709.00	6.35	36.59	2708.11	10.04	5.97	24.77	2.55
2798.00	8.08	34.74	2796.40	6.64	15.06	31.27	1.96
2888.00	9.95	35.50	2885.28	2.26	26.59	39.39	2.08
2977.00	10.65	27.11	2972.85	-3.71	40.17	47.61	1.86
3066.00	11.58	27.39	3060.18	-11.24	55.42	55.46	1.05
3156.00	14.86	22.25	3147.79	-21.13	74.13	63.99	3.87
3245.00	16.21	19.16	3233.54	-33.97	96.43	72.39	1.78
3335.00	17.35	18.82	3319.70	-48.60	121.00	80.84	1.27
3424.00	19.39	17.70	3404.16	-64.70	147.64	89.62	2.33
3514.00	20.94	16.18	3488.65	-83.09	177.32	98.64	1.82
3603.00	22.83	15.73	3571.23	-103.20	209.21	107.75	2.13
3693.00	24.64	14.36	3653.61	-125.62	244.20	117.14	2.10
3782.00	26.98	12.67	3733.73	-150.41	281.87	126.17	2.76
3872.00	28.55	11.57	3813.37	-178.00	322.86	134.96	1.83
3961.00	29.65	11.46	3891.13	-206.82	365.28	143.60	1.24
4050.00	31.66	12.29	3967.69	-236.81	409.68	152.95	2.31
4140.00	33.77	10.95	4043.41	-269.13	457.32	162.73	2.48
4229.00	35.77	7.95	4116.52	-304.28	507.38	171.03	2.96
4319.00	36.63	12.33	4189.16	-340.58	559.67	180.40	3.03
4408.00	39.67	7.53	4259.15	-378.33	613.79	189.80	4.77
4498.00	40.50	7.92	4328.01	-419.69	671.22	197.59	0.96
4587.00	43.09	7.83	4394.36	-461.91	729.97	205.72	2.91
4677.00	44.48	7.55	4459.33	-506.38	791.68	214.05	1.56
4766.00	46.03	8.96	4521.98	-551.07	854.24	223.13	2.07

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4856.00	45.20	7.69	4584.94	-596.50	917.87	232.45	1.37
4946.00	45.62	8.23	4648.12	-642.05	981.35	241.33	0.63
5035.00	46.19	7.20	4710.05	-687.68	1044.69	249.90	1.05
5124.00	46.26	7.04	4771.62	-734.02	1108.45	257.87	0.15
5214.00	46.13	7.18	4833.92	-780.86	1172.91	265.91	0.18
5303.00	46.12	7.25	4895.61	-827.04	1236.56	273.97	0.06
5393.00	46.19	7.24	4957.95	-873.75	1300.95	282.15	0.08
5482.00	46.18	7.05	5019.57	-920.03	1364.67	290.14	0.15
5572.00	46.27	7.28	5081.83	-966.85	1429.15	298.25	0.21
5661.00	46.18	7.17	5143.41	-1013.11	1492.90	306.33	0.13
5751.00	46.19	7.23	5205.72	-1059.87	1557.33	314.47	0.05
5840.00	46.19	7.15	5267.33	-1106.12	1621.05	322.51	0.06
5930.00	46.19	7.32	5329.63	-1152.86	1685.48	330.69	0.14
6019.00	46.14	7.31	5391.27	-1199.00	1749.16	338.86	0.06
6108.00	46.12	7.20	5452.95	-1245.16	1812.81	346.96	0.09
6198.00	46.18	7.18	5515.30	-1291.90	1877.20	355.09	0.07
6287.00	46.22	7.31	5576.90	-1338.12	1940.92	363.19	0.11
6377.00	46.24	7.30	5639.16	-1384.84	2005.39	371.45	0.02
6467.00	46.24	7.32	5701.41	-1431.56	2069.86	379.72	0.02
6556.00	42.43	11.87	5765.07	-1474.53	2131.16	390.00	5.57
6646.00	38.19	21.45	5833.75	-1509.32	2186.84	406.44	8.33
6736.00	37.57	33.49	5904.89	-1533.30	2235.69	431.79	8.23
6825.00	36.32	40.65	5976.05	-1548.24	2278.34	463.95	5.03
6915.00	36.70	54.93	6048.52	-1553.28	2314.08	503.39	9.43
7005.00	36.87	67.75	6120.71	-1545.73	2339.79	550.46	8.52
7094.00	38.76	78.55	6191.09	-1527.13	2355.45	602.54	7.73
7184.00	41.54	88.00	6259.94	-1498.05	2362.09	660.05	7.43
7273.00	45.01	94.85	6324.77	-1460.31	2360.46	720.95	6.56
7363.00	48.96	104.54	6386.23	-1412.63	2349.23	785.62	9.00
7451.00	54.43	113.31	6440.82	-1355.61	2326.69	850.74	9.98
7540.00	60.83	120.77	6488.49	-1288.21	2292.42	917.51	10.08
7629.00	66.42	123.90	6528.02	-1213.76	2249.75	984.81	7.03
7719.00	69.04	125.54	6562.13	-1134.80	2202.31	1053.25	3.36

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7808.00	74.94	134.14	6589.68	-1052.57	2148.09	1118.07	11.33
7898.00	80.16	137.93	6609.08	-965.43	2084.85	1179.03	7.11
7987.00	89.20	140.71	6617.33	-877.12	2017.71	1236.72	10.62
8077.00	89.17	143.81	6618.61	-787.16	1946.55	1291.79	3.44
8166.00	89.14	143.58	6619.92	-698.17	1874.84	1344.48	0.26
8256.00	89.14	143.89	6621.27	-608.18	1802.28	1397.71	0.34
8345.00	88.71	140.68	6622.94	-519.22	1731.90	1452.14	3.64
8435.00	89.41	143.58	6624.42	-429.26	1660.87	1507.37	3.31
8525.00	89.48	145.09	6625.29	-339.29	1587.76	1559.84	1.68
8614.00	90.01	144.43	6625.69	-250.32	1515.07	1611.20	0.95
8703.00	89.85	143.28	6625.80	-161.33	1443.20	1663.69	1.30
8793.00	89.85	142.70	6626.03	-71.33	1371.33	1717.86	0.64
8882.00	89.78	143.97	6626.32	17.67	1299.94	1771.01	1.43
8972.00	89.54	144.51	6626.85	107.66	1226.91	1823.60	0.66
9061.00	89.88	145.11	6627.30	196.62	1154.18	1874.89	0.77
9151.00	89.31	143.43	6627.94	286.60	1081.12	1927.44	1.97
9240.00	89.54	143.03	6628.83	375.60	1009.83	1980.72	0.52
9330.00	89.54	143.00	6629.56	465.59	937.94	2034.86	0.03
9419.00	89.78	143.79	6630.08	554.59	866.50	2087.93	0.93
9509.00	89.74	142.14	6630.46	644.59	794.66	2142.13	1.83
9598.00	89.14	143.36	6631.33	733.58	723.82	2196.00	1.53
9687.00	89.21	144.95	6632.61	822.55	651.69	2248.11	1.79
9777.00	89.41	143.57	6633.70	912.53	578.64	2300.68	1.55
9866.00	89.98	142.84	6634.17	1001.53	507.37	2353.98	1.04
9956.00	89.14	142.57	6634.86	1091.52	435.78	2408.51	0.98
10046.00	88.87	143.45	6636.42	1181.50	363.90	2462.66	1.02
10135.00	89.24	142.84	6637.89	1270.49	292.70	2516.03	0.80
10225.00	89.94	142.67	6638.54	1360.49	221.06	2570.50	0.80
10315.00	89.41	142.22	6639.05	1450.47	149.71	2625.35	0.77
10404.00	89.57	143.40	6639.84	1539.47	78.81	2679.15	1.34
10494.00	89.58	142.70	6640.51	1629.46	6.89	2733.25	0.78
10584.00	89.27	143.27	6641.41	1719.46	-64.97	2787.43	0.72

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10673.00	88.90	143.83	6642.83	1808.44	-136.55	2840.30	0.75
10763.00	89.34	144.51	6644.21	1898.42	-209.51	2892.97	0.90
10852.00	89.74	143.70	6644.93	1987.41	-281.60	2945.15	1.02
10942.00	89.17	142.31	6645.78	2077.40	-353.48	2999.30	1.67
11031.00	88.43	141.71	6647.65	2166.36	-423.60	3054.07	1.07
11120.00	89.04	142.92	6649.61	2255.32	-494.02	3108.47	1.52
11210.00	89.31	144.64	6650.91	2345.31	-566.62	3161.64	1.93
11299.00	89.47	143.25	6651.86	2434.29	-638.56	3214.02	1.57
11389.00	89.27	141.54	6652.85	2524.27	-709.86	3268.93	1.91
11479.00	89.37	141.84	6653.91	2614.23	-780.47	3324.72	0.35
11568.00	89.34	142.45	6654.92	2703.21	-850.74	3379.33	0.69
11658.00	89.34	142.44	6655.95	2793.20	-922.08	3434.18	0.01
11747.00	89.27	143.26	6657.03	2882.19	-993.01	3487.93	0.92
11837.00	89.34	143.24	6658.12	2972.18	-1065.12	3541.77	0.08
11926.00	88.50	142.52	6659.80	3061.16	-1136.07	3595.47	1.24
12016.00	89.21	143.37	6661.60	3151.14	-1207.88	3649.69	1.23
12105.00	89.17	142.51	6662.86	3240.13	-1278.90	3703.32	0.97
12195.00	89.24	143.01	6664.11	3330.12	-1350.54	3757.78	0.56
12284.00	89.27	142.87	6665.26	3419.11	-1421.56	3811.41	0.16
12374.00	89.37	142.79	6666.33	3509.10	-1493.27	3865.79	0.14
12463.00	89.20	142.56	6667.44	3598.09	-1564.04	3919.75	0.32
12553.00	89.34	143.82	6668.59	3688.08	-1636.09	3973.66	1.41
12642.00	89.61	142.91	6669.41	3777.07	-1707.50	4026.77	1.07
12732.00	89.17	142.39	6670.36	3867.06	-1779.04	4081.37	0.76
12821.00	89.27	143.01	6671.57	3956.05	-1849.83	4135.30	0.71
12910.00	89.27	142.93	6672.71	4045.04	-1920.88	4188.89	0.09
13000.00	89.14	142.96	6673.96	4135.03	-1992.69	4243.12	0.15
13090.00	89.27	143.26	6675.21	4225.02	-2064.67	4297.14	0.36
13179.00	89.34	143.08	6676.29	4314.01	-2135.90	4350.48	0.22
13268.00	89.24	143.21	6677.39	4403.01	-2207.11	4403.86	0.18
13358.00	89.27	142.97	6678.56	4493.00	-2279.06	4457.91	0.27
13447.00	89.24	143.66	6679.72	4581.99	-2350.43	4511.07	0.78
13536.00	89.17	142.37	6680.95	4670.98	-2421.51	4564.61	1.45

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13626.00	89.20	142.59	6682.23	4760.96	-2492.89	4619.42	0.25
13716.00	89.34	143.34	6683.38	4850.95	-2564.73	4673.62	0.85
13805.00	89.40	142.83	6684.36	4939.95	-2635.88	4727.07	0.58
13895.00	89.34	143.43	6685.35	5029.94	-2707.88	4781.07	0.67
13984.00	89.14	142.79	6686.53	5118.93	-2779.05	4834.49	0.75
14073.00	89.61	143.89	6687.50	5207.93	-2850.44	4887.62	1.34
14163.00	89.30	143.32	6688.35	5297.92	-2922.88	4941.02	0.72
14252.00	89.67	143.49	6689.15	5386.91	-2994.33	4994.08	0.46
14342.00	89.34	143.43	6689.93	5476.91	-3066.64	5047.66	0.37
14431.00	89.30	143.42	6690.99	5565.90	-3138.11	5100.69	0.05
14519.00	89.44	143.52	6691.95	5653.90	-3208.82	5153.07	0.20
14610.00	89.57	143.55	6692.74	5744.89	-3282.00	5207.15	0.15
14699.00	89.91	143.53	6693.14	5833.89	-3353.58	5260.04	0.38
14789.00	89.54	143.36	6693.58	5923.89	-3425.87	5313.64	0.45
14878.00	89.77	143.58	6694.11	6012.89	-3497.39	5366.62	0.36
14968.00	89.64	143.30	6694.58	6102.89	-3569.68	5420.22	0.34
15057.00	89.61	143.02	6695.16	6191.88	-3640.90	5473.59	0.32
15146.00	89.77	143.05	6695.64	6280.88	-3712.01	5527.10	0.18
15236.00	89.74	142.94	6696.03	6370.88	-3783.89	5581.27	0.13
15325.00	89.94	143.22	6696.27	6459.88	-3855.04	5634.73	0.39
15415.00	89.84	143.41	6696.45	6549.88	-3927.21	5688.50	0.24
15504.00	89.81	143.15	6696.72	6638.88	-3998.55	5741.71	0.29
15594.00	89.84	143.05	6696.99	6728.88	-4070.52	5795.75	0.12
15684.00	89.87	143.42	6697.22	6818.88	-4142.62	5849.62	0.41
15773.00	89.74	143.59	6697.52	6907.88	-4214.17	5902.55	0.24
15863.00	89.71	143.16	6697.96	6997.87	-4286.40	5956.24	0.48
15952.00	89.30	142.98	6698.72	7086.87	-4357.54	6009.72	0.50
16042.00	88.93	143.21	6700.11	7176.86	-4429.50	6063.75	0.48
16131.00	89.40	142.88	6701.41	7265.85	-4500.61	6117.25	0.65
16221.00	88.66	144.03	6702.94	7355.83	-4572.90	6170.84	1.52
16310.00	89.84	145.49	6704.10	7444.79	-4645.58	6222.18	2.11
16400.00	89.47	144.96	6704.64	7534.74	-4719.51	6273.51	0.72


10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16489.00	90.01	145.92	6705.05	7623.67	-4792.80	6324.00	1.24
16579.00	89.77	145.29	6705.22	7713.59	-4867.06	6374.84	0.75
16668.00	89.27	145.41	6705.96	7802.53	-4940.28	6425.44	0.58
16758.00	89.70	145.22	6706.77	7892.47	-5014.28	6476.65	0.52
16848.00	89.10	144.05	6707.72	7982.44	-5087.67	6528.74	1.46
16937.00	89.47	143.43	6708.83	8071.43	-5159.43	6581.37	0.81
17027.00	89.84	143.08	6709.37	8161.42	-5231.54	6635.22	0.57
17116.00	90.11	141.77	6709.41	8250.41	-5302.08	6689.49	1.50
17206.00	90.81	143.06	6708.68	8340.40	-5373.39	6744.38	1.63
17295.00	90.31	142.37	6707.81	8429.39	-5444.20	6798.29	0.96
17385.00	90.31	142.40	6707.33	8519.38	-5515.49	6853.22	0.03
17474.00	90.17	142.03	6706.96	8608.36	-5585.83	6907.75	0.44
17564.00	90.27	142.16	6706.61	8698.34	-5656.84	6963.04	0.18
17653.00	90.21	143.73	6706.24	8787.34	-5727.86	7016.67	1.77
17743.00	90.17	143.30	6705.94	8877.33	-5800.23	7070.18	0.48
17832.00	90.27	142.78	6705.60	8966.33	-5871.34	7123.69	0.59
17922.00	90.24	143.08	6705.20	9056.33	-5943.15	7177.94	0.33
18012.00	90.34	143.04	6704.74	9146.33	-6015.08	7232.03	0.12
18101.00	90.34	143.05	6704.21	9235.33	-6086.20	7285.54	0.01
18191.00	91.11	144.04	6703.07	9325.32	-6158.58	7339.01	1.39
18281.00	90.41	142.94	6701.88	9415.31	-6230.91	7392.55	1.45
18370.00	90.34	143.34	6701.30	9504.30	-6302.12	7445.94	0.46
18460.00	90.14	143.46	6700.92	9594.30	-6374.38	7499.60	0.26
18549.00	89.23	142.98	6701.41	9683.30	-6445.66	7552.88	1.16
18639.00	88.16	142.44	6703.46	9773.27	-6517.24	7607.39	1.33
18728.00	88.56	142.42	6706.01	9862.22	-6587.75	7661.64	0.45
18818.00	89.00	143.20	6707.92	9952.20	-6659.43	7716.03	0.99
18907.00	89.27	142.88	6709.27	10041.19	-6730.54	7769.53	0.47
18997.00	88.66	142.87	6710.89	10131.17	-6802.29	7823.84	0.68
19086.00	88.56	143.22	6713.05	10220.15	-6873.39	7877.33	0.41
19175.00	88.63	142.99	6715.23	10309.12	-6944.54	7930.75	0.27
19265.00	88.49	143.40	6717.49	10399.09	-7016.58	7984.65	0.48
19354.00	88.56	143.37	6719.79	10488.06	-7087.99	8037.71	0.09

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

DECEMBER 16 2025
SURVEY REPORT

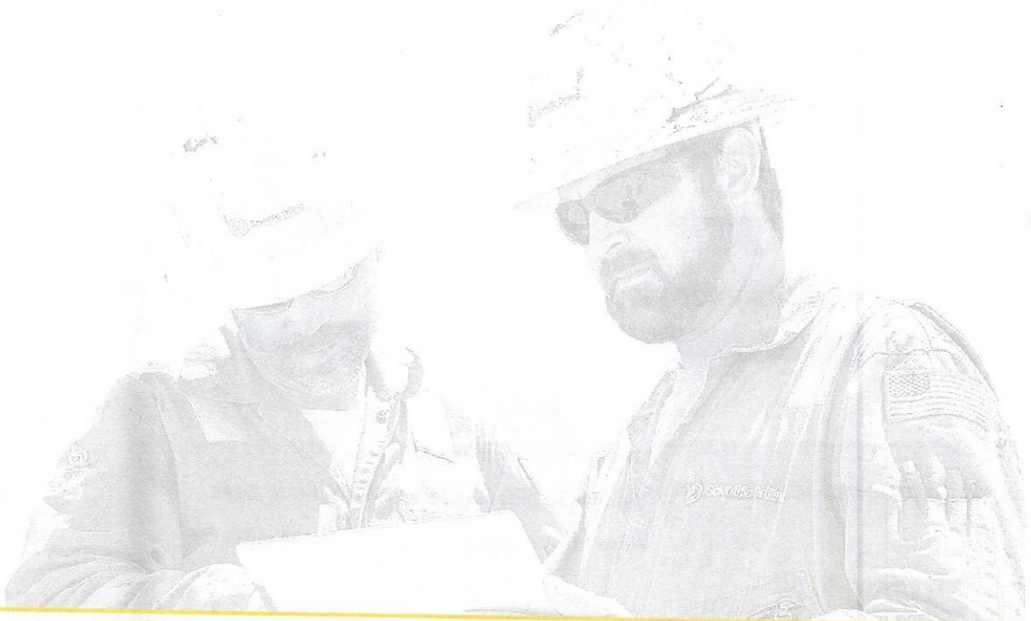

CNX RESOURCES
WELL: MAJ8 EHSM
RIG: PD 539

RECEIVED
Office Of Oil and Gas

OCT 09 2026

WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19443.00	88.60	143.07	6721.99	10577.03	-7159.25	8090.99	0.34
19533.00	88.96	143.90	6723.91	10667.01	-7231.57	8144.53	1.01
19622.00	89.54	144.36	6725.07	10755.99	-7303.69	8196.67	0.83
19712.00	89.77	145.57	6725.61	10845.95	-7377.37	8248.34	1.37
19801.00	88.29	143.38	6727.12	10934.91	-7449.79	8300.04	2.97
19891.00	88.46	142.87	6729.67	11024.87	-7521.76	8354.02	0.60
19980.00	88.63	143.04	6731.93	11113.84	-7592.77	8407.62	0.27
20070.00	89.44	143.18	6733.45	11203.83	-7664.74	8461.64	0.91
20159.00	89.47	142.99	6734.30	11292.82	-7735.90	8515.09	0.22
20248.00	89.47	143.06	6735.12	11381.82	-7806.99	8568.62	0.08
20338.00	89.50	143.17	6735.93	11471.81	-7878.98	8622.64	0.13
20427.00	89.54	143.12	6736.67	11560.81	-7950.19	8676.02	0.07
20517.00	89.54	143.16	6737.40	11650.81	-8022.20	8730.00	0.04
20606.00	89.50	142.59	6738.14	11739.80	-8093.15	8783.72	0.64
20696.00	89.57	142.78	6738.87	11829.79	-8164.73	8838.27	0.22
20785.00	89.50	142.94	6739.59	11918.79	-8235.68	8892.01	0.20
20875.00	89.50	143.08	6740.38	12008.79	-8307.56	8946.16	0.16
20964.00	89.40	143.24	6741.23	12097.78	-8378.78	8999.52	0.21
21054.00	89.50	143.23	6742.10	12187.78	-8450.88	9053.38	0.11
21143.00	89.57	143.26	6742.82	12276.77	-8522.18	9106.64	0.09
21233.00	89.40	143.34	6743.63	12366.77	-8594.34	9160.42	0.21
21322.00	89.37	143.26	6744.58	12455.76	-8665.70	9213.61	0.10
21412.00	89.60	143.13	6745.39	12545.76	-8737.75	9267.52	0.29
21501.00	89.60	143.21	6746.01	12634.76	-8808.99	9320.87	0.09
21591.00	89.50	142.86	6746.72	12724.76	-8880.90	9374.99	0.40
21681.00	89.60	142.82	6747.43	12814.75	-8952.62	9429.35	0.12
21770.00	89.54	143.21	6748.10	12903.75	-9023.71	9482.89	0.44
21860.00	89.50	143.13	6748.85	12993.74	-9095.75	9536.84	0.10
21949.00	89.54	143.21	6749.60	13082.74	-9166.98	9590.19	0.10
22039.00	89.40	143.32	6750.43	13172.74	-9239.10	9644.02	0.20
22128.00	89.33	143.11	6751.41	13261.73	-9310.38	9697.31	0.25
22217.00	89.37	143.07	6752.42	13350.72	-9381.54	9750.75	0.06

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
22307.00	89.43	143.22	6753.37	13440.72	-9453.55	9804.73	0.18
22396.00	89.43	142.92	6754.25	13529.71	-9524.69	9858.20	0.34
22485.00	89.60	142.89	6755.01	13618.71	-9595.67	9911.88	0.19
22575.00	89.60	141.24	6755.63	13708.68	-9666.65	9967.21	1.83
22664.00	89.50	141.65	6756.33	13797.64	-9736.25	10022.68	0.47
22686.00	89.40	141.81	6756.54	13819.63	-9753.52	10036.30	0.86
22708.00	89.40	141.81	6756.77	13841.62	-9770.81	10049.90	0.00

RECEIVED
Office Of Oil and Gas

OCT 09 2026

WV Department of
Environmental Protection

10/23/2026
