Well Location Plat

CNX Applicant / Well Operator Name	DEP ID#	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	**Well # MAJ8FHSM**

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8FHSM OH As Drilled_ KOP	5924.49	39.93271863	-80.56830991	6674.00
MAJ8FHSM OH As Drilled_ LP	6607.65	39.93219825	-80.56557779	7837.00
MAJ8FHSM OH As Drilled_BHL	6757.27	39.90207911	-80.53542382	21695.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1093.50	Survey #1 (OH)	GYD_CT+WIR
1189.50	2209.50	Survey #2 (OH)	MWD+IFR1+Sag
2319.00	21695.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

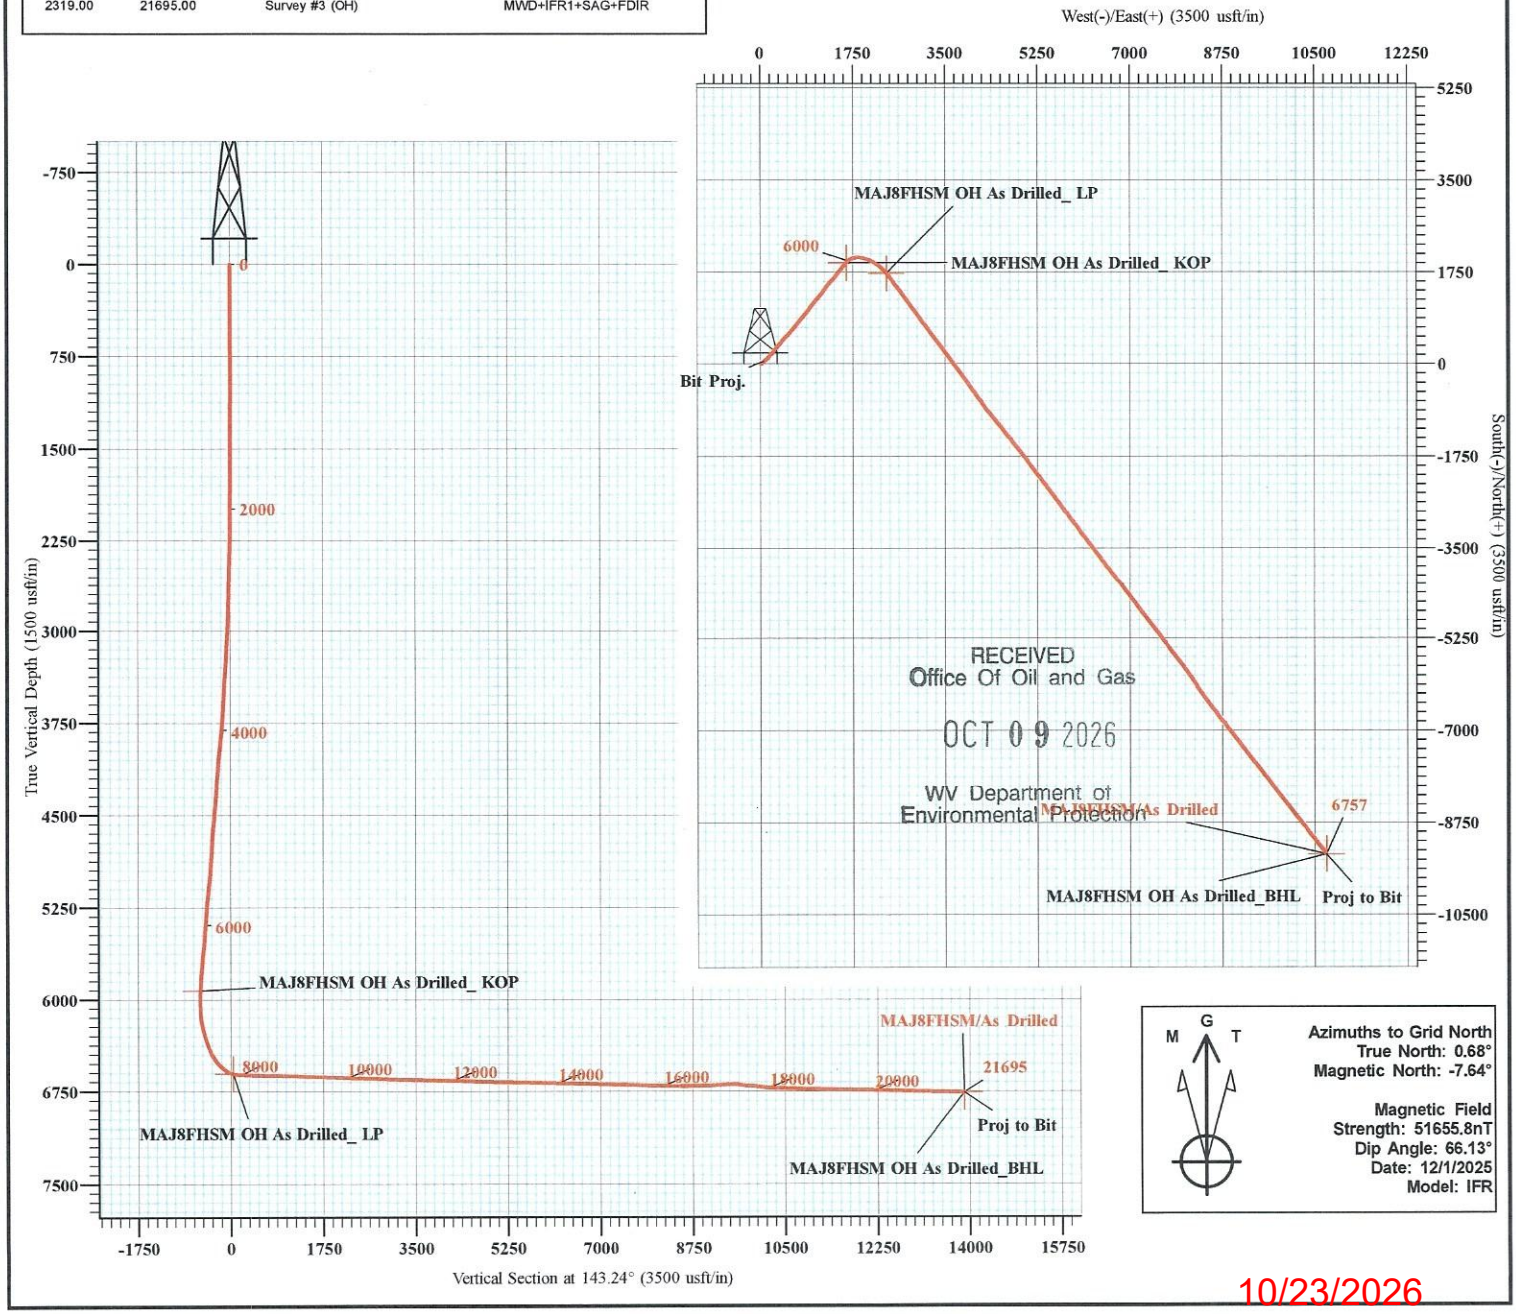

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

Azimuths to Grid North
True North: 0.68°
Magnetic North: -7.64°

Magnetic Field
Strength: 51655.8nT
Dip Angle: 66.13°
Date: 12/1/2025
Model: IFR

10/23/2026

Well Location Plat

CNX Applicant / Well Operator Name	DEP ID#	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	Well # MAJ8GHSM

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8GHSM OH As Drilled_ KOP	5996.43	39.93342361	-80.56593563	7121.00
MAJ8GHSM OH As Drilled_ LP	6615.93	39.93281133	-80.56273397	8374.00
MAJ8GHSM OH As Drilled_BHL	6703.96	39.91310832	-80.54316747	17411.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
104.50	1101.50	Survey #1 (OH)	GYD_CT+WIR
1189.50	17411.00	Survey #2 (OH)	MWD+IFR1+SAG+FDIR

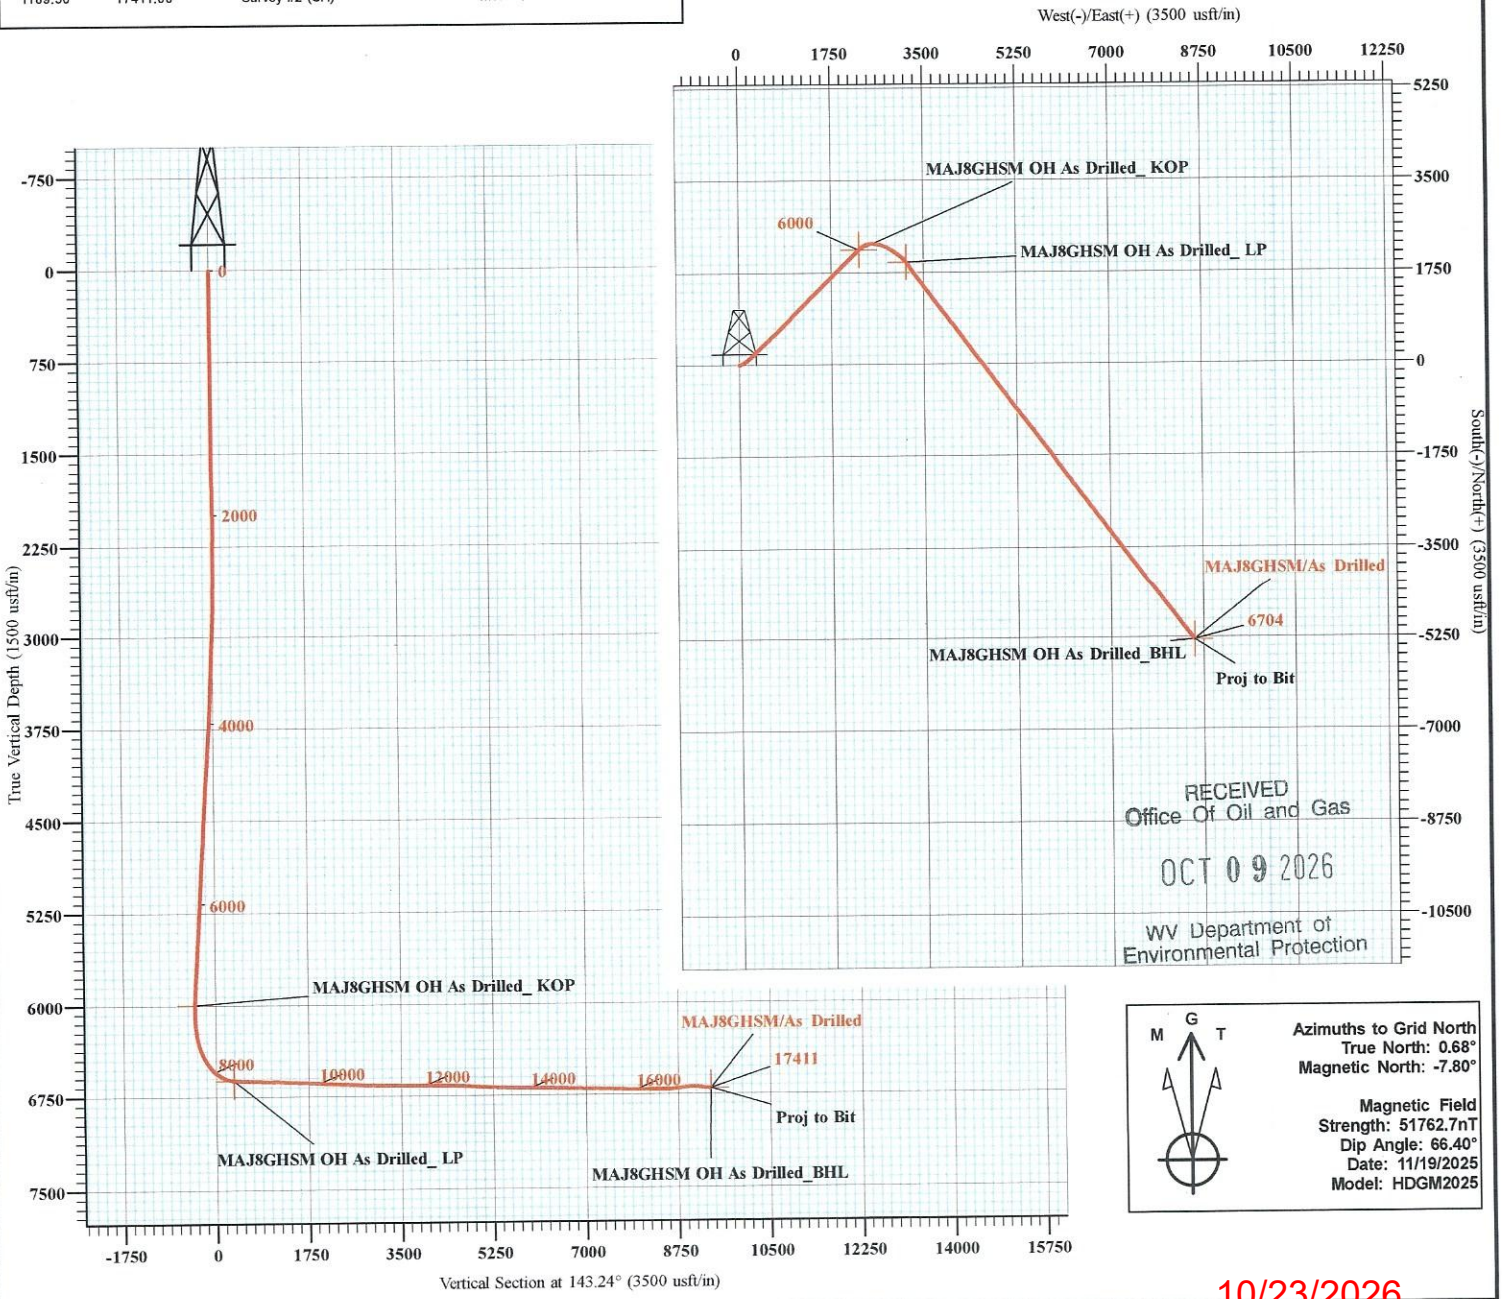


RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

Azimuths to Grid North
True North: 0.68°
Magnetic North: -7.80°

Magnetic Field
Strength: 51762.7nT
Dip Angle: 66.40°
Date: 11/19/2025
Model: HDGM2025

10/23/2026

DECEMBER 3 2025
SURVEY REPORT

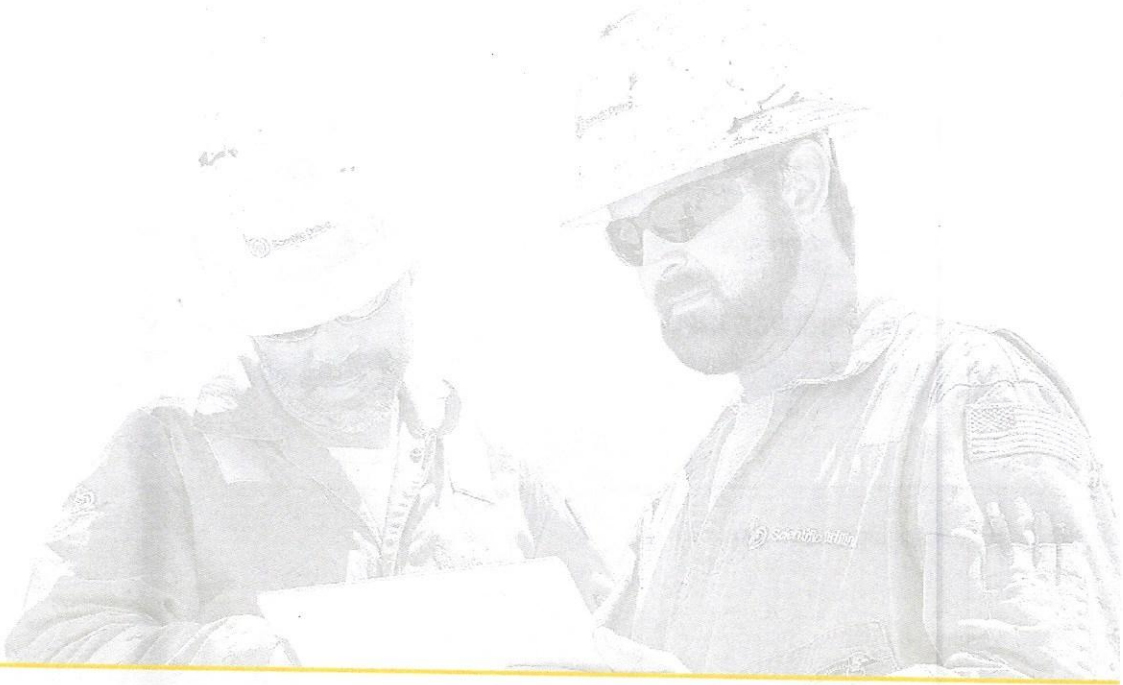

CNX RESOURCES
WELL: MAJ8FHSM
RIG: PD 539

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

CUSTOMER	**CNX RESOURCES**
PROJECT	**MAJ8FHSM**
FIELD	**Marcellus**
SDI JOB NO.	**OP.051148**
SDI DISTRICT	**Northeast**
SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad C/L**
Lat/Long	**39.9275261 N, 80.5742268 W**
Northing	**521,744.52 ft**
Easting	**1,698,736.42 ft**
Section	-
Township	-
Range	-

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.9273925 N, 80.5740006 W**
Northing	**521,695.08 ft**
Easting	**1,698,799.28 ft**
UWI	**47051025470000**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.24°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-21695 ft	IFR	01 Dec 2025	-8.32°	add 0.69°	subtract 7.63°

WELL NOTES

OPERATORS

J. GONZALEZ

SDI Operator Name (Printed) SIGNATURE DATE

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.38	18.60	54.50	-0.10	0.17	0.06	0.70
104.50	0.40	55.77	104.50	-0.19	0.43	0.25	0.50
154.50	0.42	49.10	154.50	-0.19	0.64	0.54	0.10
204.50	0.42	56.93	204.50	-0.20	0.86	0.83	0.11
254.50	0.56	68.60	254.49	-0.12	1.05	1.21	0.34
304.50	0.66	70.43	304.49	0.03	1.24	1.71	0.20
354.50	0.68	70.46	354.49	0.20	1.44	2.26	0.04
404.50	0.71	67.63	404.48	0.37	1.65	2.83	0.09
454.50	0.90	71.55	454.48	0.57	1.89	3.49	0.40
504.50	0.94	69.13	504.47	0.80	2.16	4.24	0.11
554.50	0.96	73.55	554.47	1.06	2.43	5.03	0.15
604.50	1.01	78.65	604.46	1.40	2.63	5.86	0.20
654.50	0.92	82.30	654.45	1.78	2.78	6.69	0.22
704.50	0.89	89.73	704.45	2.21	2.83	7.48	0.24
754.50	0.86	88.49	754.44	2.65	2.84	8.24	0.07
804.50	0.73	87.49	804.43	3.05	2.87	8.93	0.26
854.50	0.75	82.08	854.43	3.39	2.93	9.58	0.15
904.50	0.73	82.65	904.43	3.70	3.01	10.22	0.04
954.50	0.77	83.20	954.42	4.02	3.09	10.86	0.08
1004.50	0.78	86.17	1004.42	4.38	3.15	11.54	0.08
1054.50	0.82	86.38	1054.41	4.76	3.20	12.23	0.08
1093.50	0.80	84.53	1093.41	5.05	3.24	12.78	0.08
1189.50	0.87	66.76	1189.40	5.57	3.59	14.12	0.28
1277.50	2.24	49.50	1277.36	5.61	4.98	16.04	1.63
1363.50	4.92	43.33	1363.19	4.87	8.75	19.85	3.14
1450.50	8.31	40.60	1449.60	2.85	16.24	26.51	3.91
1538.50	10.72	44.62	1536.38	0.23	26.90	36.39	2.84
1623.50	11.94	47.76	1619.72	-1.79	38.43	48.46	1.61
1710.50	11.49	50.91	1704.91	-3.00	49.95	61.85	0.90
1795.50	11.10	53.08	1788.27	-3.37	60.20	74.96	0.68
1883.50	10.62	54.96	1874.69	-3.15	69.95	88.37	0.68
1970.50	10.17	55.79	1960.26	-2.57	78.87	101.29	0.55

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2056.50	9.82	50.91	2044.96	-2.53	87.76	113.26	1.07
2142.50	9.83	43.00	2129.70	-4.13	97.75	123.96	1.57
2209.50	9.84	40.35	2195.72	-6.43	106.30	131.56	0.68
2319.00	9.91	37.36	2303.60	-11.09	120.92	143.34	0.47
2408.00	11.62	36.72	2391.03	-15.74	134.19	153.35	1.93
2498.00	12.84	40.04	2478.98	-20.60	149.11	165.20	1.56
2587.00	14.38	42.63	2565.48	-24.89	164.82	179.05	1.86
2677.00	15.19	44.39	2652.50	-28.76	181.47	194.86	1.03
2767.00	15.43	43.51	2739.31	-32.60	198.57	211.35	0.37
2856.00	16.16	42.10	2824.95	-36.99	216.35	227.81	0.93
2946.00	21.11	36.00	2910.21	-44.22	238.77	245.74	5.90
3035.00	26.16	39.78	2991.72	-53.55	266.84	267.73	5.92
3125.00	24.99	39.03	3072.90	-62.83	296.85	292.40	1.35
3214.00	25.98	38.45	3153.24	-72.42	326.72	316.36	1.15
3303.00	31.51	38.64	3231.24	-83.27	360.18	343.03	6.22
3393.00	30.65	38.74	3308.32	-94.94	396.45	372.07	0.96
3483.00	32.16	39.83	3385.14	-106.24	432.74	401.77	1.79
3572.00	33.50	40.46	3459.92	-117.17	469.62	432.88	1.55
3661.00	35.84	43.55	3533.12	-126.99	507.20	466.78	3.29
3751.00	36.29	44.90	3605.87	-135.29	545.16	503.74	1.01
3840.00	34.58	42.85	3678.38	-143.67	582.34	539.51	2.34
3929.00	37.92	37.63	3750.16	-155.59	622.54	573.40	5.11
4019.00	41.77	40.20	3819.26	-169.80	667.36	609.65	4.65
4108.00	45.64	40.92	3883.58	-183.28	714.06	649.64	4.38
4198.00	45.92	37.92	3946.36	-198.69	763.87	690.58	2.41
4288.00	42.59	39.09	4010.81	-214.68	813.03	729.66	3.81
4377.00	38.12	39.88	4078.62	-228.39	857.50	766.28	5.06
4467.00	36.06	39.46	4150.41	-241.12	899.28	800.93	2.31
4557.00	35.94	39.30	4223.22	-253.80	940.17	834.50	0.17
4646.00	33.75	38.59	4296.26	-266.34	979.71	866.47	2.50
4736.00	32.81	38.19	4371.50	-279.00	1018.41	897.13	1.08
4825.00	35.00	36.64	4445.36	-292.55	1057.85	927.28	2.65

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4915.00	36.14	35.76	4518.57	-307.90	1100.09	958.19	1.39
5005.00	34.91	37.31	4591.82	-322.94	1142.12	989.31	1.69
5094.00	33.75	38.30	4665.31	-336.30	1181.78	1020.07	1.45
5184.00	33.46	43.12	4740.28	-347.11	1219.51	1052.53	2.98
5273.00	31.87	41.80	4815.21	-356.08	1254.94	1084.97	1.96
5363.00	32.62	38.75	4891.33	-366.86	1291.57	1115.99	1.99
5452.00	35.28	36.96	4965.15	-380.07	1330.83	1146.46	3.19
5542.00	36.04	36.41	5038.28	-395.03	1372.90	1177.81	0.92
5631.00	37.69	34.94	5109.48	-411.15	1416.28	1208.93	2.10
5721.00	38.33	35.44	5180.39	-428.32	1461.57	1240.87	0.79
5810.00	41.02	38.64	5248.90	-444.12	1506.88	1275.12	3.79
5900.00	41.83	42.92	5316.39	-456.95	1551.94	1314.01	3.27
5989.00	41.69	42.84	5382.78	-467.61	1595.38	1354.34	0.17
6079.00	40.20	40.82	5450.76	-479.26	1639.31	1393.68	2.21
6168.00	40.13	38.70	5518.78	-492.64	1683.43	1430.39	1.54
6258.00	40.08	38.74	5587.62	-507.17	1728.66	1466.66	0.06
6347.00	38.07	37.96	5656.71	-521.58	1772.65	1501.47	2.32
6437.00	35.86	37.56	5728.61	-536.02	1815.43	1534.61	2.47
6483.00	34.72	37.62	5766.16	-543.19	1836.49	1550.82	2.48
6564.00	32.89	36.75	5833.46	-555.64	1872.38	1578.07	2.34
6653.00	36.27	41.93	5906.74	-567.67	1911.35	1610.13	5.03
6743.00	35.95	46.90	5979.47	-575.81	1949.22	1647.22	3.27
6832.00	35.91	56.39	6051.59	-577.26	1981.54	1688.06	6.25
6922.00	37.92	68.83	6123.65	-568.37	2006.17	1735.91	8.58
7011.00	40.21	80.23	6192.84	-547.95	2020.95	1789.80	8.46
7101.00	43.14	92.02	6260.16	-515.43	2024.80	1849.29	9.29
7190.00	46.25	100.75	6323.48	-472.62	2017.72	1911.35	7.73
7280.00	49.15	105.47	6384.06	-421.72	2002.57	1976.13	5.04
7369.00	54.65	111.73	6438.99	-364.09	1980.12	2042.38	8.29
7459.00	60.45	117.76	6487.29	-297.35	1948.25	2111.22	8.57
7548.00	65.83	122.32	6527.50	-224.40	1908.47	2179.86	7.58
7637.00	69.45	130.40	6561.40	-145.71	1859.67	2246.02	9.33
7727.00	76.34	134.24	6587.87	-61.31	1801.77	2309.53	8.67

RECEIVED Office Of Oil and Gas
OCT 09 2025
WV Department of Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7816.00	81.64	139.24	6604.87	25.43	1738.17	2369.33	8.11
7905.00	88.04	143.23	6612.87	113.95	1669.09	2424.78	8.46
7995.00	88.31	142.67	6615.74	203.91	1597.30	2478.98	0.69
8085.00	89.12	143.76	6617.76	293.88	1525.24	2532.86	1.51
8174.00	89.42	143.33	6618.89	382.87	1453.66	2585.74	0.59
8264.00	89.12	142.90	6620.04	472.86	1381.68	2639.75	0.58
8353.00	89.58	143.70	6621.05	561.86	1310.33	2692.94	1.04
8442.00	89.82	143.67	6621.51	650.85	1238.62	2745.64	0.27
8532.00	88.91	143.57	6622.51	740.84	1166.16	2799.02	1.02
8621.00	89.68	144.01	6623.61	829.83	1094.36	2851.59	1.00
8711.00	90.35	145.17	6623.58	919.81	1021.01	2903.74	1.49
8800.00	89.21	143.38	6623.93	1008.79	948.76	2955.70	2.38
8889.00	89.48	143.64	6624.94	1097.78	877.21	3008.63	0.42
8979.00	89.24	142.93	6625.95	1187.77	805.07	3062.43	0.83
9068.00	88.81	143.52	6627.46	1276.76	733.79	3115.70	0.82
9158.00	88.94	142.60	6629.23	1366.74	661.87	3169.78	1.03
9247.00	89.51	144.14	6630.43	1455.73	590.46	3222.87	1.84
9337.00	89.58	144.68	6631.15	1545.71	517.27	3275.25	0.61
9426.00	88.88	143.05	6632.34	1634.69	445.40	3327.73	1.99
9515.00	89.55	142.48	6633.56	1723.68	374.55	3381.57	0.99
9605.00	88.91	142.63	6634.77	1813.66	303.11	3436.29	0.73
9694.00	88.98	144.06	6636.41	1902.65	231.72	3489.41	1.61
9784.00	89.42	145.07	6637.67	1992.61	158.40	3541.58	1.22
9873.00	88.68	144.39	6639.14	2081.57	85.75	3592.97	1.13
9963.00	89.08	142.90	6640.90	2171.55	13.28	3646.31	1.71
10053.00	89.05	143.09	6642.37	2261.53	-58.58	3700.47	0.21
10142.00	89.42	143.49	6643.56	2350.52	-129.92	3753.67	0.61
10232.00	89.22	143.43	6644.63	2440.52	-202.23	3807.25	0.23
10321.00	89.49	143.59	6645.63	2529.51	-273.78	3860.17	0.35
10411.00	89.62	146.06	6646.33	2619.47	-347.33	3912.01	2.75
10500.00	89.12	143.72	6647.31	2708.42	-420.13	3963.19	2.69
10590.00	89.15	143.76	6648.67	2798.40	-492.69	4016.42	0.06

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10679.00	89.42	146.20	6649.78	2887.35	-565.57	4067.48	2.76
10769.00	89.29	145.18	6650.79	2977.26	-639.90	4118.21	1.14
10858.00	89.55	145.02	6651.69	3066.21	-712.89	4169.13	0.34
10948.00	89.42	144.82	6652.50	3156.17	-786.54	4220.85	0.27
11037.00	89.05	142.58	6653.69	3245.15	-858.26	4273.53	2.55
11127.00	89.39	140.92	6654.91	3335.11	-928.93	4329.24	1.88
11217.00	88.98	141.70	6656.19	3425.05	-999.17	4385.50	0.98
11306.00	89.76	140.76	6657.17	3513.98	-1068.55	4441.22	1.37
11396.00	89.32	141.01	6657.90	3603.91	-1138.38	4498.00	0.56
11485.00	89.55	140.62	6658.77	3692.82	-1207.36	4554.23	0.51
11575.00	89.69	141.21	6659.37	3782.74	-1277.22	4610.97	0.67
11664.00	89.65	141.47	6659.88	3871.69	-1346.71	4666.57	0.30
11754.00	89.22	141.97	6660.77	3961.66	-1417.36	4722.32	0.73
11843.00	89.35	141.90	6661.88	4050.63	-1487.43	4777.19	0.17
11933.00	89.45	141.79	6662.82	4140.60	-1558.19	4832.79	0.17
12022.00	89.15	142.40	6663.91	4229.57	-1628.41	4887.46	0.76
12112.00	89.08	142.83	6665.30	4319.55	-1699.91	4942.10	0.48
12201.00	89.28	142.16	6666.57	4408.54	-1770.51	4996.28	0.79
12291.00	89.69	142.35	6667.38	4498.52	-1841.67	5051.37	0.50
12381.00	89.55	142.95	6667.98	4588.51	-1913.22	5105.97	0.68
12470.00	88.35	142.88	6669.61	4677.50	-1984.20	5159.63	1.35
12560.00	89.05	143.22	6671.65	4767.47	-2056.11	5213.71	0.86
12650.00	89.82	144.40	6672.54	4857.46	-2128.74	5266.85	1.57
12739.00	89.12	142.84	6673.36	4946.45	-2200.39	5319.64	1.92
12829.00	89.52	141.38	6674.43	5036.42	-2271.41	5374.90	1.68
12918.00	89.19	143.87	6675.43	5125.41	-2342.12	5428.92	2.82
13008.00	89.80	143.27	6676.23	5215.40	-2414.53	5482.36	0.95
13097.00	89.59	142.82	6676.70	5304.40	-2485.65	5535.87	0.56
13187.00	89.82	143.42	6677.16	5394.40	-2557.64	5589.88	0.71
13276.00	90.16	143.16	6677.18	5483.40	-2628.99	5643.08	0.48
13366.00	89.02	143.14	6677.82	5573.39	-2701.00	5697.05	1.27
13455.00	89.76	143.13	6678.77	5662.39	-2772.20	5750.45	0.83
13544.00	89.49	142.63	6679.35	5751.38	-2843.17	5804.15	0.64

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13634.00	89.49	143.12	6680.16	5841.38	-2914.92	5858.47	0.54
13723.00	89.76	143.05	6680.74	5930.37	-2986.08	5911.93	0.31
13812.00	89.02	143.90	6681.69	6019.37	-3057.60	5964.89	1.27
13902.00	89.35	143.50	6682.97	6109.35	-3130.12	6018.17	0.58
13991.00	89.59	143.49	6683.79	6198.35	-3201.66	6071.11	0.27
14081.00	89.45	143.69	6684.54	6288.35	-3274.09	6124.53	0.27
14170.00	89.52	142.58	6685.34	6377.34	-3345.29	6177.92	1.25
14260.00	89.49	143.76	6686.12	6467.34	-3417.32	6231.87	1.31
14349.00	89.99	142.93	6686.52	6556.33	-3488.72	6285.00	1.09
14439.00	89.25	143.05	6687.12	6646.33	-3560.58	6339.17	0.83
14528.00	89.32	143.32	6688.23	6735.32	-3631.83	6392.50	0.31
14617.00	89.42	144.43	6689.21	6824.31	-3703.71	6444.97	1.25
14707.00	89.36	142.60	6690.17	6914.30	-3776.07	6498.48	2.03
14796.00	89.19	142.32	6691.29	7003.28	-3846.63	6552.70	0.37
14886.00	89.12	143.01	6692.62	7093.27	-3918.18	6607.28	0.77
14975.00	89.49	143.53	6693.70	7182.26	-3989.51	6660.50	0.72
15065.00	89.02	142.75	6694.87	7272.25	-4061.51	6714.48	1.01
15155.00	89.86	142.97	6695.75	7362.25	-4133.25	6768.82	0.96
15244.00	89.69	144.56	6696.10	7451.24	-4205.03	6821.42	1.80
15333.00	89.79	143.39	6696.50	7540.23	-4277.01	6873.77	1.32
15423.00	89.62	143.89	6696.97	7630.23	-4349.49	6927.12	0.59
15512.00	88.65	143.18	6698.31	7719.21	-4421.05	6980.01	1.35
15602.00	88.89	143.75	6700.24	7809.19	-4493.35	7033.58	0.69
15691.00	89.25	143.36	6701.69	7898.18	-4564.94	7086.44	0.60
15781.00	88.92	143.29	6703.13	7988.17	-4637.11	7140.19	0.37
15870.00	89.32	143.27	6704.49	8077.16	-4708.44	7193.40	0.45
15960.00	89.19	142.06	6705.66	8167.14	-4779.99	7247.97	1.35
16050.00	90.40	143.41	6705.98	8257.13	-4851.62	7302.46	2.01
16139.00	89.22	142.31	6706.28	8346.13	-4922.56	7356.20	1.81
16229.00	90.53	142.78	6706.48	8436.12	-4994.00	7410.93	1.55
16318.00	89.09	142.53	6706.77	8525.11	-5064.76	7464.92	1.64
16408.00	90.60	142.98	6707.01	8615.11	-5136.40	7519.38	1.75

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16497.00	90.60	142.52	6706.08	8704.10	-5207.24	7573.25	0.52
16586.00	90.70	143.25	6705.07	8793.09	-5278.20	7626.95	0.83
16676.00	90.46	143.43	6704.16	8883.08	-5350.40	7680.69	0.33
16765.00	90.13	142.45	6703.70	8972.08	-5421.42	7734.32	1.16
16854.00	91.24	143.13	6702.64	9061.07	-5492.29	7788.14	1.46
16944.00	92.21	142.78	6699.93	9151.03	-5564.09	7842.33	1.15
17033.00	92.11	143.20	6696.58	9239.96	-5635.11	7895.87	0.48
17123.00	92.51	142.31	6692.95	9329.88	-5706.70	7950.29	1.08
17212.00	91.07	143.87	6690.17	9418.84	-5777.82	8003.71	2.38
17302.00	88.85	140.77	6690.23	9508.81	-5849.04	8058.71	4.24
17391.00	87.71	144.38	6692.90	9597.75	-5919.67	8112.77	4.25
17480.00	85.39	144.92	6698.26	9686.55	-5992.13	8164.16	2.68
17569.00	88.18	149.36	6703.25	9775.17	-6066.75	8212.36	5.88
17659.00	89.02	148.88	6705.45	9864.67	-6143.96	8258.54	1.07
17748.00	87.24	146.15	6708.36	9953.37	-6218.99	8306.30	3.66
17837.00	86.77	143.88	6713.01	10042.20	-6291.80	8357.26	2.60
17927.00	86.60	144.26	6718.21	10132.03	-6364.56	8409.98	0.46
18016.00	87.74	143.55	6722.60	10220.92	-6436.38	8462.35	1.51
18106.00	90.26	143.81	6724.18	10310.89	-6508.88	8515.64	2.81
18195.00	89.66	142.92	6724.24	10399.89	-6580.30	8568.75	1.21
18284.00	89.79	142.76	6724.66	10488.89	-6651.23	8622.51	0.23
18374.00	88.69	142.71	6725.86	10578.88	-6722.84	8677.00	1.22
18464.00	89.06	142.35	6727.63	10668.85	-6794.26	8731.74	0.57
18553.00	89.73	142.06	6728.57	10757.83	-6864.58	8786.28	0.82
18642.00	88.89	141.66	6729.64	10846.80	-6934.58	8841.24	1.05
18732.00	89.12	142.43	6731.20	10936.77	-7005.53	8896.58	0.89
18821.00	89.43	142.19	6732.33	11025.75	-7075.95	8950.99	0.44
18911.00	89.69	142.35	6733.02	11115.73	-7147.13	9006.07	0.34
19000.00	89.66	142.65	6733.52	11204.72	-7217.74	9060.24	0.34
19090.00	90.60	143.17	6733.32	11294.72	-7289.53	9114.52	1.19
19180.00	88.86	142.74	6733.74	11384.71	-7361.36	9168.74	1.99
19269.00	88.86	142.53	6735.51	11473.69	-7432.08	9222.74	0.24
19359.00	89.39	142.39	6736.89	11563.67	-7503.44	9277.57	0.61

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19449.00	90.84	140.96	6736.71	11653.63	-7574.04	9333.38	2.26
19538.00	89.66	141.83	6736.32	11742.58	-7643.59	9388.91	1.65
19628.00	89.19	142.35	6737.22	11832.56	-7714.59	9444.20	0.78
19717.00	89.56	142.53	6738.19	11921.55	-7785.14	9498.45	0.46
19807.00	89.63	141.87	6738.83	12011.53	-7856.25	9553.61	0.74
19896.00	89.36	141.70	6739.61	12100.50	-7926.17	9608.67	0.36
19986.00	89.39	142.40	6740.59	12190.47	-7997.14	9664.01	0.78
20076.00	89.39	142.20	6741.55	12280.45	-8068.35	9719.05	0.22
20165.00	89.39	142.33	6742.50	12369.44	-8138.73	9773.51	0.15
20255.00	89.43	142.31	6743.43	12459.42	-8209.95	9828.52	0.05
20345.00	89.56	142.30	6744.22	12549.40	-8281.16	9883.55	0.14
20434.00	89.33	142.22	6745.08	12638.39	-8351.54	9938.02	0.27
20524.00	89.49	142.11	6746.01	12728.37	-8422.62	9993.22	0.22
20613.00	89.33	143.14	6746.93	12817.35	-8493.34	10047.25	1.17
20703.00	89.53	141.85	6747.82	12907.34	-8564.73	10102.04	1.45
20792.00	89.49	141.70	6748.58	12996.31	-8634.65	10157.10	0.17
20882.00	89.36	142.10	6749.49	13086.28	-8705.47	10212.63	0.47
20972.00	89.53	142.18	6750.36	13176.26	-8776.52	10267.87	0.21
21061.00	89.79	142.10	6750.89	13265.24	-8846.79	10322.49	0.31
21151.00	89.22	141.84	6751.66	13355.21	-8917.67	10377.93	0.70
21240.00	89.56	142.19	6752.61	13444.19	-8987.82	10432.71	0.55
21329.00	89.26	142.28	6753.53	13533.17	-9058.17	10487.21	0.35
21419.00	89.56	141.80	6754.45	13623.14	-9129.13	10542.57	0.63
21508.00	89.69	142.08	6755.04	13712.12	-9199.20	10597.43	0.35
21598.00	89.32	142.06	6755.81	13802.10	-9270.19	10652.75	0.41
21673.00	89.73	142.29	6756.44	13877.08	-9329.43	10698.74	0.63
21695.00	89.73	142.29	6756.54	13899.08	-9346.83	10712.20	0.00

10/23/2026
