Well Location Plat

CNX Applicant / Well Operator Name	DEP ID#	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	Well # MAJ8HHSM

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8HHSM OH As Drilled_KOP	6166.86	39.921419	-80.586043	7854.00
MAJ8HHSM OH As Drilled_LP	6626.20	39.918869	-80.585948	9017.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1070.50	Survey #1 (OH)	GYD_CT+WIR
1208.50	2208.50	Survey #2 (OH)	MWD+IFR1+SAG+FDIR
2285.00	21401.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

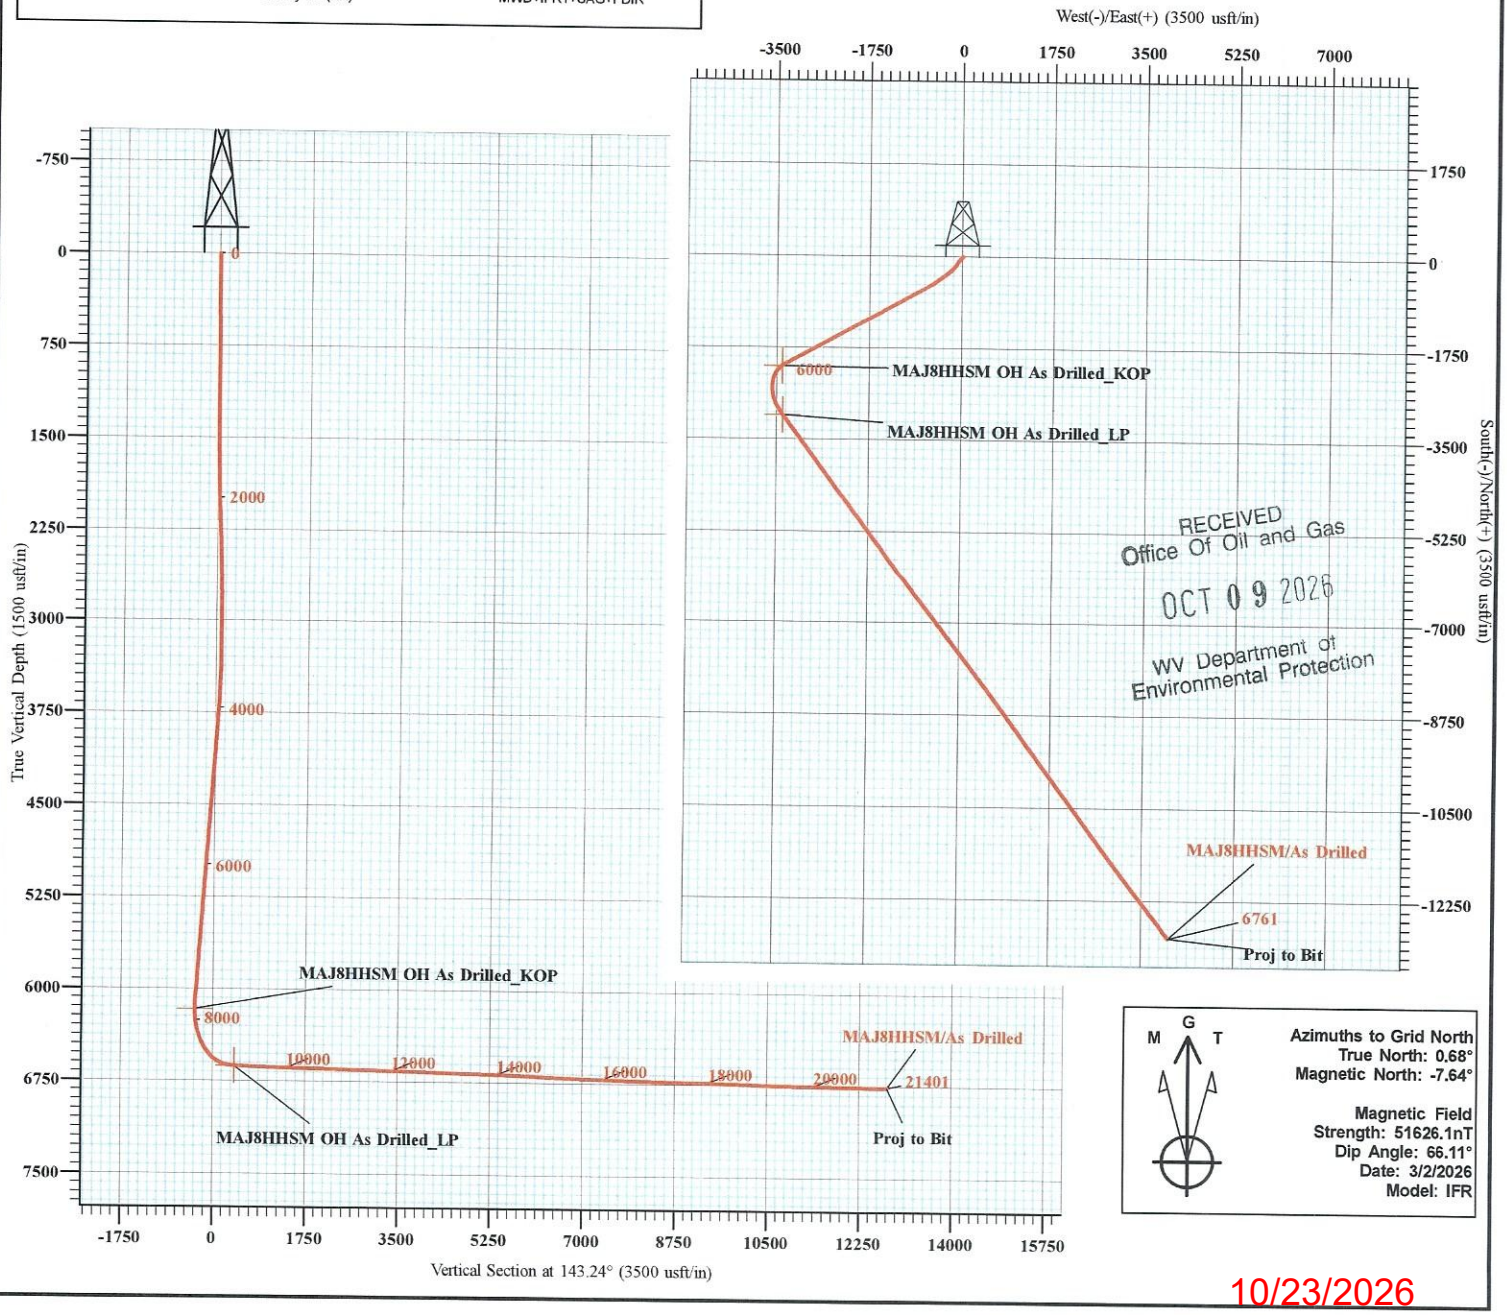


RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

Azimuths to Grid North
True North: 0.68°
Magnetic North: -7.64°

Magnetic Field
Strength: 51626.1nT
Dip Angle: 66.11°
Date: 3/2/2026
Model: IFR

10/23/2026

MARCH 3 2026
SURVEY REPORT

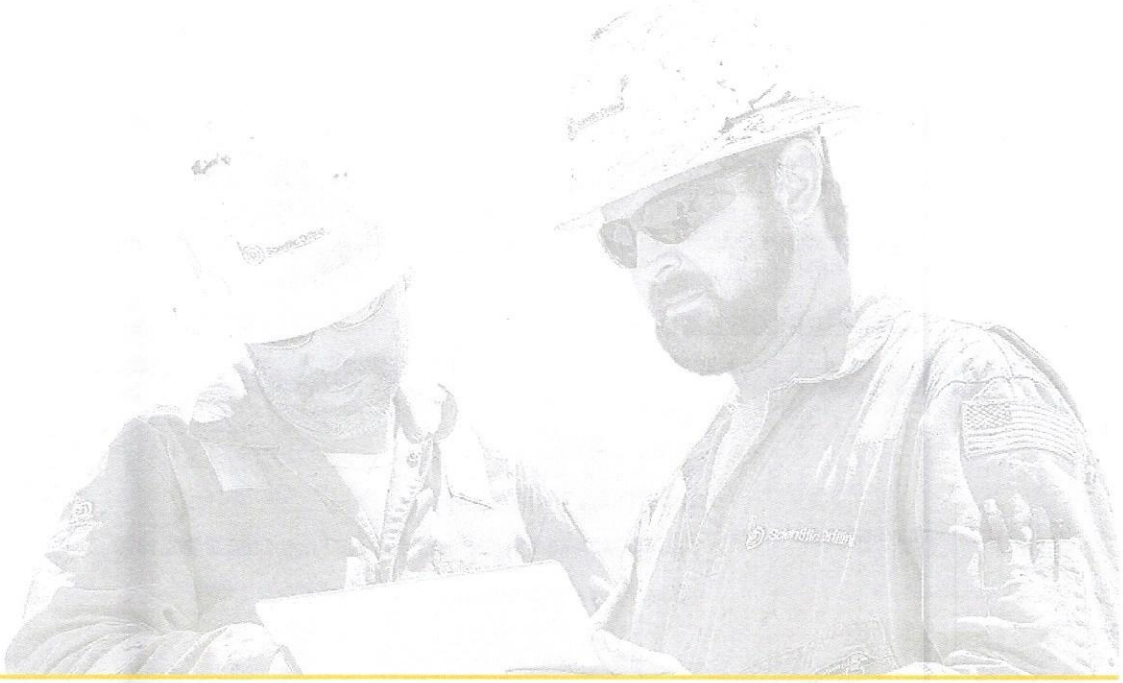

CNX RESOURCES
WELL: MAJ8 HHSM
RIG: PRECISION DRILLING 539

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

CUSTOMER	**CNX Resources**	SDI JOB NO.	**OP.052254**
PROJECT	**MAJ8 HHSM**	SDI DISTRICT	**Northeast**
FIELD	**Marcellus**	SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**	Section	-
Lat/Long	**39.9275261 N, 80.5742268 W**	Township	-
Northing	**521,744.52 ft**	Range	-
Easting	**1,698,736.42 ft**		

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.9273155 N, 80.5739875 W**
Northing	**521,666.99 ft**
Easting	**1,698,802.6 ft**
UWI	**47-051-02549**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.24°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-21401 ft	IFR1	02 Mar 2026	-8.32°	add 0.69°	subtract 7.63°

SDI Operator Name (Printed) SIGNATURE DATE

WELL NOTES

Gyro Surveys From 0' To 1070.5'

Superior MSA MWD Corrected Surveys From 1208.5' To 21379'

Survey At 21401' Is A Projection To The Bit

OPERATORS

D. LAMBERT, J. WITKOWSKI

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.22	178.47	54.50	0.09	-0.10	0.00	0.40
104.50	0.32	171.60	104.50	0.29	-0.34	0.03	0.21
154.50	0.16	112.82	154.50	0.47	-0.50	0.11	0.55
204.50	0.41	100.33	204.50	0.66	-0.56	0.35	0.51
254.50	0.35	108.53	254.50	0.92	-0.64	0.67	0.16
304.50	0.45	117.85	304.50	1.22	-0.78	0.99	0.24
354.50	0.43	96.68	354.49	1.53	-0.90	1.35	0.33
404.50	0.43	96.85	404.49	1.79	-0.94	1.72	0.00
454.50	0.54	95.69	454.49	2.07	-0.99	2.14	0.22
504.50	0.43	104.56	504.49	2.38	-1.06	2.56	0.27
554.50	0.46	117.23	554.49	2.71	-1.20	2.92	0.21
604.50	0.42	108.81	604.49	3.04	-1.35	3.27	0.15
654.50	0.41	120.46	654.49	3.35	-1.50	3.60	0.17
704.50	0.47	148.79	704.48	3.72	-1.76	3.86	0.45
754.50	0.54	140.62	754.48	4.16	-2.12	4.12	0.20
804.50	0.33	154.52	804.48	4.54	-2.43	4.33	0.47
854.50	0.26	130.32	854.48	4.79	-2.64	4.48	0.28
904.50	0.21	118.45	904.48	4.98	-2.75	4.64	0.14
954.50	0.07	115.35	954.48	5.09	-2.81	4.75	0.28
1004.50	0.25	84.58	1004.48	5.18	-2.81	4.89	0.39
1054.50	0.21	82.98	1054.48	5.28	-2.79	5.09	0.08
1070.50	0.17	82.92	1070.48	5.31	-2.79	5.14	0.25
1208.50	0.19	106.70	1208.48	5.59	-2.83	5.56	0.06
1295.50	0.58	211.95	1295.48	5.87	-3.24	5.47	0.75
1382.50	2.28	221.43	1382.45	6.38	-4.91	4.09	1.97
1468.50	4.52	223.71	1468.29	7.29	-8.64	0.61	2.61
1556.50	7.34	226.59	1555.81	8.52	-15.02	-5.87	3.22
1642.50	9.59	226.64	1640.87	9.98	-23.71	-15.07	2.62
1728.50	11.71	224.21	1725.38	12.17	-34.89	-26.36	2.52
1814.50	14.05	220.28	1809.21	15.88	-49.11	-39.20	2.90
1901.50	14.79	218.49	1893.47	21.08	-65.86	-52.94	0.99
1989.50	15.20	218.62	1978.48	26.85	-83.66	-67.13	0.47

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2076.50	15.49	216.77	2062.37	33.02	-101.88	-81.20	0.65
2161.50	15.71	215.73	2144.24	39.70	-120.31	-94.72	0.42
2208.50	15.85	214.40	2189.47	43.69	-130.77	-102.06	0.83
2285.00	15.69	212.08	2263.09	50.80	-148.16	-113.45	0.85
2374.00	15.86	218.32	2348.75	58.27	-167.90	-127.39	1.91
2463.00	17.90	218.53	2433.91	64.88	-188.14	-143.45	2.29
2553.00	20.63	221.08	2518.86	71.73	-210.92	-162.49	3.17
2642.00	22.57	222.82	2601.61	78.12	-235.27	-184.40	2.30
2732.00	23.08	226.21	2684.56	83.41	-260.14	-208.88	1.57
2821.00	24.27	229.25	2766.08	86.82	-284.16	-235.33	1.92
2911.00	26.75	233.54	2847.30	88.00	-308.27	-265.64	3.43
3001.00	28.16	233.13	2927.16	87.93	-333.05	-298.92	1.58
3090.00	29.98	233.51	3004.95	87.87	-358.88	-333.60	2.06
3179.00	30.89	232.69	3081.68	87.98	-385.95	-369.65	1.12
3269.00	33.18	233.41	3157.97	88.13	-414.64	-407.81	2.58
3358.00	34.88	233.09	3231.73	88.13	-444.44	-447.71	1.92
3448.00	36.83	234.44	3304.67	87.63	-475.59	-490.24	2.34
3537.00	39.11	236.49	3374.83	85.48	-506.60	-535.35	2.93
3627.00	41.05	238.10	3443.69	81.36	-537.90	-584.11	2.44
3716.00	42.45	238.93	3510.09	75.91	-568.84	-634.65	1.69
3806.00	43.69	239.47	3575.84	69.52	-600.31	-687.44	1.44
3895.00	45.03	240.64	3639.47	62.13	-631.36	-741.36	1.76
3985.00	46.66	241.61	3702.16	53.27	-662.53	-797.91	1.97
4075.00	48.59	240.79	3762.82	44.07	-694.57	-856.16	2.25
4164.00	50.69	240.89	3820.45	35.10	-727.61	-915.38	2.36
4254.00	50.67	240.84	3877.48	25.86	-761.51	-976.20	0.05
4343.00	50.67	240.95	3933.88	16.69	-794.99	-1036.35	0.10
4433.00	50.65	241.35	3990.94	7.11	-828.58	-1097.32	0.34
4522.00	50.75	241.23	4047.31	-2.53	-861.67	-1157.72	0.15
4612.00	50.70	241.21	4104.28	-12.21	-895.21	-1218.79	0.06
4701.00	50.63	240.97	4160.69	-21.61	-928.49	-1279.05	0.22
4791.00	50.70	241.03	4217.74	-31.01	-962.24	-1339.93	0.10

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4880.00	50.73	241.24	4274.09	-40.47	-995.49	-1400.26	0.18
4970.00	50.69	241.16	4331.08	-50.12	-1029.05	-1461.30	0.08
5060.00	50.66	241.16	4388.11	-59.71	-1062.63	-1522.29	0.03
5149.00	50.62	240.92	4444.56	-69.05	-1095.95	-1582.49	0.21
5239.00	50.62	241.15	4501.66	-78.48	-1129.64	-1643.36	0.20
5328.00	50.70	241.10	4558.08	-87.93	-1162.88	-1703.63	0.10
5418.00	50.63	240.96	4615.12	-97.36	-1196.59	-1764.53	0.14
5504.00	50.44	241.20	4669.79	-106.42	-1228.70	-1822.65	0.31
5596.00	50.46	241.19	4728.37	-116.23	-1262.88	-1884.81	0.02
5686.00	50.37	241.17	4785.72	-125.82	-1296.32	-1945.58	0.10
5775.00	50.36	241.08	4842.49	-135.22	-1329.42	-2005.60	0.08
5865.00	50.40	241.12	4899.88	-144.70	-1362.92	-2066.29	0.06
5954.00	50.44	241.02	4956.59	-154.04	-1396.10	-2126.33	0.10
6044.00	50.44	241.22	5013.91	-163.56	-1429.61	-2187.08	0.17
6133.00	50.49	241.43	5070.56	-173.21	-1462.55	-2247.31	0.19
6223.00	50.52	241.11	5127.80	-182.91	-1495.93	-2308.21	0.28
6312.00	50.39	241.00	5184.47	-192.24	-1529.15	-2368.26	0.17
6402.00	50.44	241.28	5241.82	-201.78	-1562.63	-2429.01	0.25
6491.00	50.46	240.98	5298.50	-211.20	-1595.76	-2489.10	0.26
6581.00	50.44	241.21	5355.81	-220.68	-1629.30	-2549.85	0.20
6670.00	50.40	241.16	5412.51	-230.16	-1662.36	-2609.95	0.06
6760.00	50.45	241.26	5469.85	-239.78	-1695.77	-2670.75	0.10
6849.00	50.43	241.18	5526.53	-249.31	-1728.81	-2730.89	0.07
6939.00	50.45	241.19	5583.85	-258.90	-1762.25	-2791.68	0.02
7028.00	50.41	241.29	5640.55	-268.45	-1795.26	-2851.83	0.10
7117.00	50.45	241.48	5697.24	-278.17	-1828.12	-2912.05	0.17
7207.00	50.35	240.94	5754.61	-287.78	-1861.51	-2972.83	0.48
7296.00	50.46	241.27	5811.33	-297.17	-1894.65	-3032.87	0.31
7386.00	50.40	241.00	5868.66	-306.70	-1928.14	-3093.63	0.24
7475.00	50.41	241.00	5925.39	-315.96	-1961.39	-3153.61	0.01
7565.00	50.50	240.83	5982.69	-325.22	-1995.13	-3214.26	0.18
7654.00	50.46	241.20	6039.32	-334.51	-2028.40	-3274.32	0.32
7744.00	50.45	241.18	6096.62	-344.11	-2061.85	-3335.13	0.02

RECEIVED Office Of Oil and Gas OCT 09 2026 WV Department of Environmental Protection 10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7833.00	50.29	235.64	6153.41	-350.29	-2097.72	-3393.48	4.80
7922.00	49.89	227.12	6210.57	-348.09	-2140.25	-3446.74	7.35
8012.00	50.97	217.59	6267.98	-334.97	-2191.44	-3493.35	8.25
8101.00	52.94	209.19	6322.89	-311.15	-2249.91	-3531.80	7.75
8190.00	54.96	200.30	6375.33	-276.82	-2315.17	-3561.80	8.39
8280.00	57.91	191.17	6425.16	-231.16	-2387.25	-3582.01	9.06
8369.00	61.41	183.89	6470.15	-176.18	-2463.32	-3591.97	8.08
8459.00	65.20	177.93	6510.61	-112.54	-2543.65	-3593.18	7.26
8549.00	69.37	170.45	6545.39	-41.38	-2626.14	-3584.70	8.95
8638.00	73.26	164.59	6573.92	35.43	-2708.39	-3566.45	7.61
8728.00	77.32	157.21	6596.80	118.31	-2790.55	-3537.94	9.12
8817.00	82.03	153.19	6612.75	203.93	-2869.98	-3501.21	6.91
8907.00	86.35	145.66	6621.88	292.87	-2946.99	-3455.69	9.61
8996.00	88.70	143.27	6625.72	381.75	-3019.33	-3404.02	3.76
9085.00	89.07	142.92	6627.45	470.73	-3090.49	-3350.59	0.57
9175.00	88.90	143.83	6629.05	560.72	-3162.70	-3296.91	1.03
9265.00	88.97	143.89	6630.72	650.70	-3235.37	-3243.84	0.10
9354.00	88.54	142.80	6632.65	739.67	-3306.76	-3190.72	1.32
9444.00	88.87	144.34	6634.69	829.65	-3379.15	-3137.29	1.75
9533.00	89.18	142.54	6636.20	918.63	-3450.62	-3084.28	2.05
9623.00	88.64	144.34	6637.91	1008.61	-3522.90	-3030.68	2.09
9712.00	89.44	142.73	6639.40	1097.59	-3594.46	-2977.80	2.02
9802.00	89.41	143.76	6640.31	1187.59	-3666.56	-2923.95	1.14
9891.00	90.01	144.24	6640.76	1276.58	-3738.56	-2871.63	0.86
9981.00	89.41	143.08	6641.21	1366.57	-3811.06	-2818.30	1.45
10070.00	89.51	142.42	6642.05	1455.56	-3881.90	-2764.44	0.75
10159.00	89.17	144.37	6643.08	1544.55	-3953.34	-2711.37	2.22
10249.00	89.84	143.71	6643.86	1634.54	-4026.18	-2658.52	1.04
10338.00	88.94	143.22	6644.80	1723.53	-4097.69	-2605.55	1.15
10428.00	89.88	143.85	6645.73	1813.53	-4170.06	-2552.06	1.26
10517.00	89.34	143.54	6646.34	1902.52	-4241.78	-2499.37	0.70
10606.00	89.68	144.00	6647.10	1991.51	-4313.57	-2446.77	0.64

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10696.00	89.78	143.24	6647.52	2081.51	-4386.03	-2393.38	0.85
10785.00	89.98	144.42	6647.71	2170.50	-4457.87	-2340.86	1.34
10875.00	88.90	141.48	6648.59	2260.49	-4529.69	-2286.64	3.48
10965.00	88.90	142.81	6650.31	2350.45	-4600.74	-2231.42	1.48
11054.00	89.51	144.66	6651.55	2439.43	-4672.49	-2178.79	2.19
11144.00	89.41	143.75	6652.40	2529.42	-4745.48	-2126.15	1.02
11233.00	89.17	142.87	6653.50	2618.41	-4816.85	-2072.98	1.02
11323.00	89.58	142.47	6654.48	2708.40	-4888.40	-2018.41	0.64
11412.00	89.54	142.74	6655.17	2797.39	-4959.11	-1964.36	0.31
11502.00	89.57	143.04	6655.86	2887.39	-5030.88	-1910.06	0.33
11591.00	89.47	145.17	6656.61	2976.37	-5102.97	-1857.88	2.40
11681.00	89.54	143.98	6657.39	3066.34	-5176.31	-1805.72	1.32
11770.00	89.07	144.94	6658.47	3155.31	-5248.72	-1753.99	1.20
11860.00	88.94	143.31	6660.03	3245.28	-5321.63	-1701.26	1.82
11949.00	89.74	142.94	6661.06	3334.28	-5392.82	-1647.85	0.99
12039.00	89.41	143.49	6661.72	3424.27	-5464.90	-1593.96	0.71
12128.00	89.37	143.92	6662.67	3513.26	-5536.63	-1541.28	0.49
12217.00	89.95	142.87	6663.20	3602.26	-5608.07	-1488.21	1.35
12307.00	89.51	144.02	6663.62	3692.26	-5680.37	-1434.61	1.37
12396.00	89.11	144.00	6664.69	3781.24	-5752.37	-1382.32	0.45
12485.00	89.04	143.89	6666.13	3870.22	-5824.32	-1329.94	0.15
12575.00	89.37	142.96	6667.38	3960.21	-5896.59	-1276.32	1.10
12665.00	88.94	143.92	6668.71	4050.20	-5968.87	-1222.71	1.17
12754.00	89.21	143.37	6670.14	4139.19	-6040.53	-1169.96	0.69
12844.00	89.57	144.01	6671.10	4229.18	-6113.05	-1116.67	0.82
12934.00	89.34	142.64	6671.96	4319.17	-6185.23	-1062.92	1.54
13023.00	89.14	144.19	6673.14	4408.16	-6256.69	-1009.88	1.76
13113.00	89.20	143.35	6674.44	4498.15	-6329.28	-956.70	0.94
13202.00	89.24	143.77	6675.65	4587.14	-6400.87	-903.84	0.47
13292.00	89.67	142.12	6676.51	4677.13	-6472.69	-849.61	1.89
13382.00	89.41	142.14	6677.23	4767.11	-6543.73	-794.36	0.29
13471.00	89.27	143.02	6678.26	4856.10	-6614.41	-740.29	1.00
13561.00	89.17	142.73	6679.48	4946.09	-6686.16	-685.97	0.34

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13650.00	89.34	142.42	6680.64	5035.07	-6756.84	-631.89	0.40
13740.00	89.20	142.07	6681.79	5125.05	-6827.99	-576.79	0.42
13829.00	89.44	142.44	6682.84	5214.03	-6898.36	-522.31	0.50
13919.00	89.21	142.13	6683.90	5304.01	-6969.55	-467.26	0.43
14008.00	89.47	142.50	6684.93	5393.00	-7039.98	-412.85	0.51
14098.00	88.70	142.38	6686.37	5482.98	-7111.31	-358.00	0.87
14187.00	89.17	143.43	6688.02	5571.96	-7182.29	-304.33	1.29
14277.00	89.44	142.04	6689.11	5661.94	-7253.91	-249.84	1.57
14366.00	88.97	142.63	6690.35	5750.92	-7324.35	-195.46	0.85
14456.00	89.07	142.36	6691.89	5840.90	-7395.74	-140.68	0.32
14545.00	88.87	143.10	6693.49	5929.89	-7466.55	-86.79	0.86
14635.00	89.21	142.19	6694.99	6019.87	-7538.08	-32.19	1.08
14724.00	88.84	142.64	6696.51	6108.84	-7608.60	22.09	0.65
14814.00	89.00	142.42	6698.21	6198.82	-7680.02	76.83	0.30
14903.00	89.21	142.65	6699.60	6287.80	-7750.65	130.96	0.35
14993.00	89.37	143.37	6700.71	6377.80	-7822.53	185.10	0.82
15082.00	89.11	142.96	6701.89	6466.79	-7893.76	238.46	0.55
15172.00	89.07	142.85	6703.32	6556.77	-7965.54	292.73	0.13
15262.00	89.04	142.57	6704.81	6646.76	-8037.13	347.25	0.31
15351.00	88.94	142.45	6706.37	6735.74	-8107.74	401.41	0.18
15440.00	89.00	142.68	6707.97	6824.72	-8178.39	455.50	0.27
15530.00	89.24	142.43	6709.36	6914.70	-8249.84	510.21	0.39
15619.00	89.34	143.38	6710.46	7003.69	-8320.82	563.89	1.07
15709.00	89.21	143.29	6711.60	7093.68	-8393.01	617.63	0.18
15798.00	89.21	144.13	6712.82	7182.67	-8464.74	670.30	0.94
15888.00	89.31	143.27	6713.99	7272.66	-8537.27	723.57	0.96
15977.00	89.31	143.16	6715.06	7361.65	-8608.54	776.86	0.12
16066.00	89.14	143.68	6716.26	7450.64	-8680.00	829.90	0.61
16156.00	89.44	144.38	6717.38	7540.63	-8752.84	882.76	0.85
16245.00	89.44	143.83	6718.25	7629.61	-8824.93	934.93	0.62
16335.00	89.47	143.79	6719.10	7719.60	-8897.56	988.07	0.06
16424.00	89.47	144.25	6719.93	7808.59	-8969.58	1040.36	0.52

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16514.00	89.14	143.78	6721.02	7898.58	-9042.40	1093.24	0.64
16604.00	89.34	143.48	6722.21	7988.57	-9114.86	1146.60	0.40
16693.00	89.17	143.55	6723.37	8077.56	-9186.41	1199.52	0.21
16782.00	89.51	143.70	6724.40	8166.55	-9258.07	1252.30	0.42
16871.00	89.27	143.85	6725.34	8255.54	-9329.86	1304.89	0.32
16961.00	89.31	143.94	6726.46	8345.53	-9402.57	1357.92	0.11
17050.00	89.54	143.45	6727.35	8434.52	-9474.29	1410.61	0.61
17140.00	89.47	143.67	6728.13	8524.52	-9546.69	1464.07	0.26
17229.00	89.81	143.61	6728.69	8613.51	-9618.36	1516.83	0.39
17319.00	89.54	143.76	6729.20	8703.51	-9690.88	1570.13	0.34
17408.00	89.47	143.61	6729.97	8792.50	-9762.59	1622.84	0.19
17498.00	89.47	143.72	6730.80	8882.49	-9835.09	1676.16	0.12
17587.00	89.58	143.18	6731.54	8971.49	-9906.58	1729.16	0.62
17677.00	89.61	143.28	6732.17	9061.49	-9978.67	1783.03	0.12
17766.00	89.54	143.80	6732.83	9150.48	-10050.25	1835.92	0.59
17856.00	89.41	143.71	6733.66	9240.48	-10122.83	1889.13	0.18
17945.00	89.47	143.50	6734.53	9329.47	-10194.47	1941.94	0.25
18035.00	89.21	143.76	6735.56	9419.46	-10266.93	1995.30	0.41
18125.00	89.51	143.47	6736.57	9509.45	-10339.38	2048.69	0.46
18214.00	89.44	143.73	6737.39	9598.45	-10411.01	2101.50	0.30
18304.00	89.44	143.99	6738.27	9688.44	-10483.69	2154.57	0.29
18393.00	89.41	143.54	6739.16	9777.43	-10555.48	2207.18	0.51
18483.00	89.24	143.83	6740.22	9867.42	-10627.99	2260.48	0.37
18572.00	89.57	143.85	6741.14	9956.41	-10699.84	2312.99	0.37
18661.00	89.27	143.82	6742.04	10045.40	-10771.69	2365.50	0.34
18751.00	89.41	143.81	6743.08	10135.39	-10844.33	2418.64	0.16
18840.00	89.37	143.54	6744.03	10224.38	-10916.03	2471.35	0.31
18930.00	89.20	143.75	6745.15	10314.38	-10988.50	2524.70	0.30
19020.00	89.20	143.27	6746.41	10404.37	-11060.85	2578.22	0.53
19109.00	89.20	143.49	6747.65	10493.36	-11132.28	2631.30	0.25
19199.00	89.47	143.81	6748.70	10583.35	-11204.76	2684.64	0.47
19288.00	89.61	144.06	6749.41	10672.34	-11276.70	2737.03	0.32
19378.00	89.61	142.85	6750.02	10762.33	-11349.00	2790.62	1.34

RECEIVED Office Of Oil and Gas
OCT 9 2026
WV Department of Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19467.00	89.67	142.82	6750.58	10851.33	-11419.92	2844.39	0.08
19556.00	89.54	142.68	6751.19	10940.32	-11490.77	2898.26	0.21
19646.00	89.54	142.80	6751.92	11030.32	-11562.40	2952.74	0.13
19736.00	89.77	142.75	6752.46	11120.31	-11634.06	3007.19	0.26
19825.00	89.64	142.52	6752.92	11209.31	-11704.79	3061.20	0.30
19915.00	89.57	142.96	6753.54	11299.30	-11776.42	3115.69	0.50
20004.00	89.47	142.94	6754.28	11388.30	-11847.45	3169.31	0.11
20094.00	89.54	142.92	6755.06	11478.29	-11919.26	3223.56	0.08
20183.00	89.61	142.91	6755.72	11567.29	-11990.26	3277.22	0.08
20273.00	89.07	142.32	6756.76	11657.28	-12061.76	3331.87	0.89
20362.00	89.91	142.50	6757.55	11746.26	-12132.28	3386.15	0.97
20452.00	89.77	142.99	6757.80	11836.26	-12203.92	3440.64	0.57
20541.00	89.81	142.61	6758.13	11925.26	-12274.81	3494.44	0.43
20631.00	89.87	142.47	6758.38	12015.25	-12346.25	3549.18	0.17
20720.00	89.91	142.84	6758.55	12104.24	-12417.00	3603.17	0.42
20810.00	89.84	142.62	6758.75	12194.24	-12488.62	3657.67	0.26
20899.00	89.97	141.88	6758.89	12283.23	-12558.99	3712.16	0.84
20989.00	89.87	142.56	6759.02	12373.21	-12630.13	3767.30	0.76
21078.00	89.70	142.69	6759.35	12462.20	-12700.85	3821.32	0.24
21168.00	89.67	142.83	6759.85	12552.20	-12772.50	3875.78	0.16
21257.00	89.91	142.54	6760.17	12641.20	-12843.28	3929.74	0.42
21347.00	89.71	142.70	6760.47	12731.19	-12914.80	3984.37	0.28
21379.00	89.77	142.52	6760.62	12763.19	-12940.22	4003.80	0.59
21401.00	89.77	142.52	6760.71	12785.19	-12957.68	4017.19	0.00

10/23/2026
