Well Location Plat

CNX Applicant / Well Operator Name	**DEP ID#**	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	**Well #** **MAJ8KHSM**

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8KHSM OH As Drilled KOP	5928.92	39.92507328	-80.58312595	6759.00
MAJ8KHSM OH As Drilled LP	6607.79	39.92271351	-80.58307747	8011.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1088.50	Survey #1 (OH)	GYD_CT+WIR
1208.50	2208.50	Survey #2 (OH)	MWD+IFR1+Sag
2263.00	19681.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

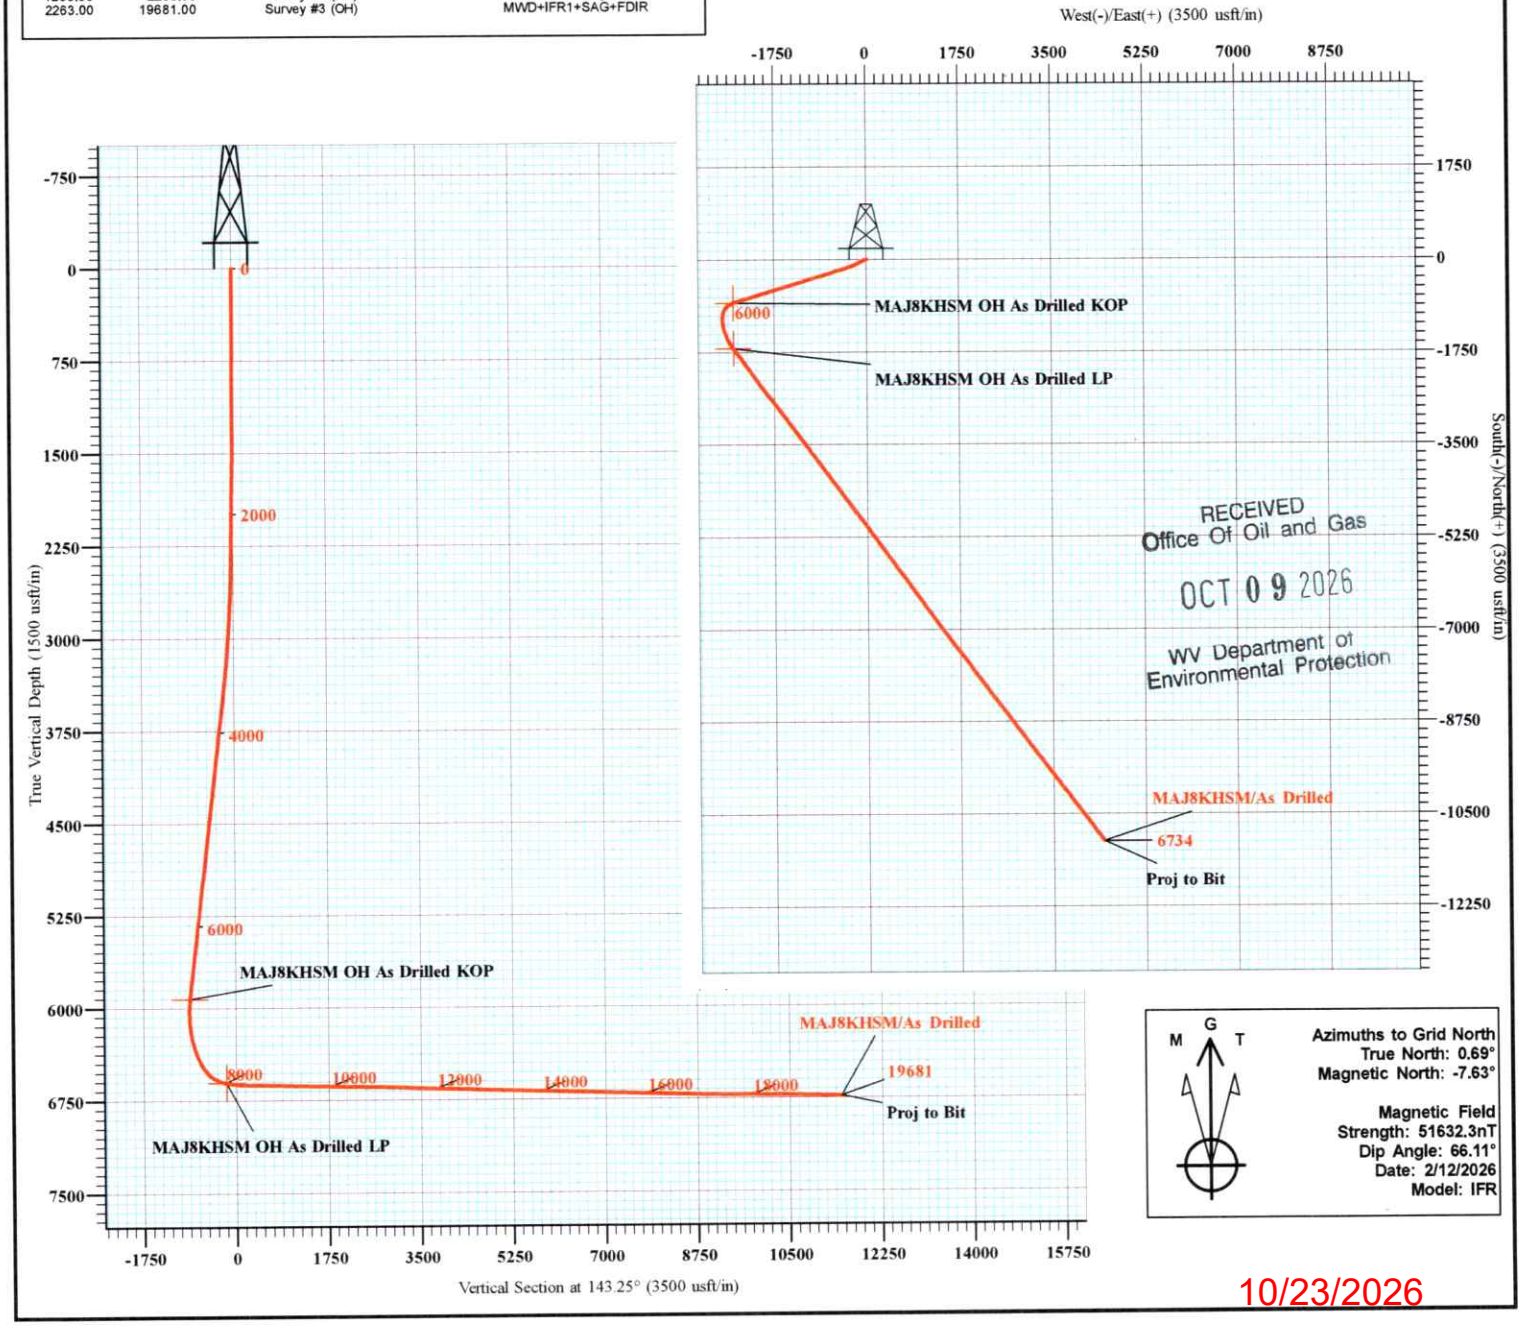


RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

Azimuths to Grid North
True North: 0.69°
Magnetic North: -7.63°

Magnetic Field
Strength: 51632.3nT
Dip Angle: 66.11°
Date: 2/12/2026
Model: IFR

10/23/2026

FEBRUARY 15 2026
SURVEY REPORT

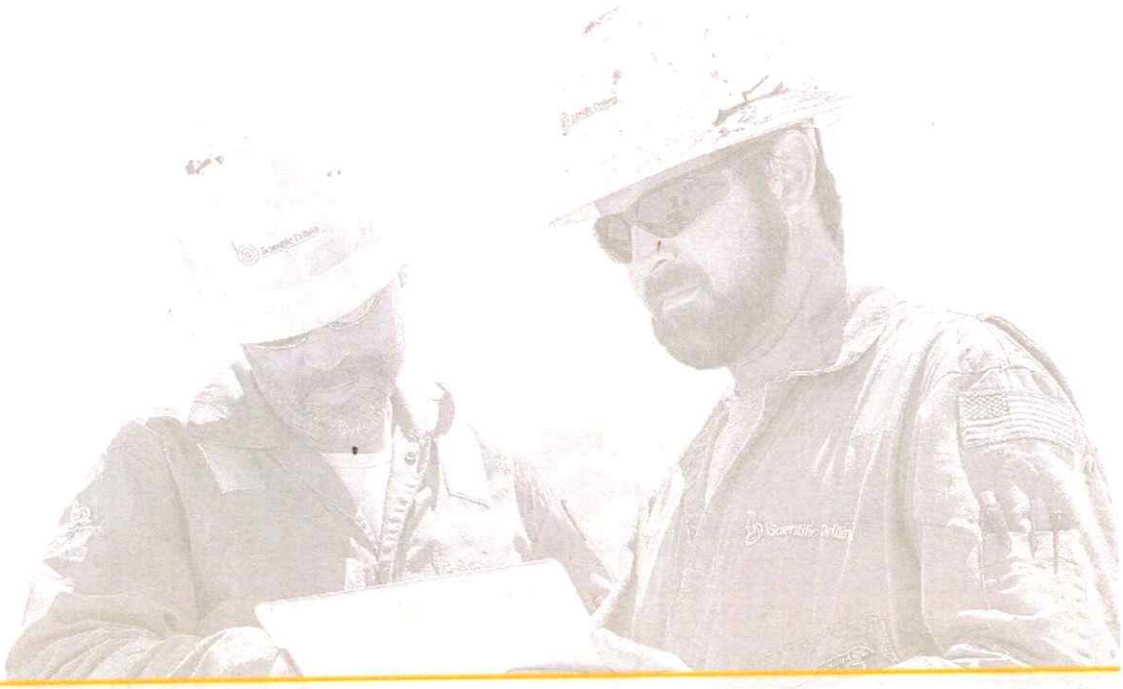

CNX RESOURCES
WELL: MAJ8 KHSM
RIG: PRECISION DRILLING 539

RECEIVED
Office Of Oil and Gas
OCT 09 2025
WV Department of
Environmental Protection

10/23/2026

CUSTOMER	**CNX RESOURCES**	SDI JOB NO.	**OP.051520**
PROJECT	**MAJ8 KHSM**	SDI DISTRICT	**Northeast**
FIELD	**Marcellus**	SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**	Section	-
Lat/Long	**39.9275261 N, 80.5742268 W**	Township	-
Northing	**521,744.52 ft**	Range	-
Easting	**1,698,736.42 ft**		

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.9273825 N, 80.5741006 W**
Northing	**521,691.76 ft**
Easting	**1,698,771.19 ft**
UWI	**47-051-02551**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.25°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-19681 ft	IFR1	12 Feb 2026	-8.32°	add 0.69°	subtract 7.63°

SDI Operator Name (Printed) SIGNATURE DATE

WELL NOTES

Gyro Surveys From 0' To 1088.5'

Superior MSA MWD Corrected Surveys From 1208.5' To 19659'

Survey At 19681' Is A Projection To The Bit

OPERATORS

D. BARKER, J. WITKOWSKI

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.23	283.80	54.50	-0.08	0.03	-0.11	0.42
104.50	0.23	312.05	104.50	-0.26	0.12	-0.28	0.22
154.50	0.15	319.26	154.50	-0.42	0.23	-0.40	0.17
204.50	0.05	27.26	204.50	-0.50	0.30	-0.43	0.28
254.50	0.07	33.39	254.50	-0.52	0.35	-0.40	0.04
304.50	0.17	57.82	304.50	-0.52	0.41	-0.32	0.22
354.50	0.09	55.62	354.50	-0.52	0.47	-0.23	0.16
404.50	0.12	111.25	404.50	-0.47	0.48	-0.15	0.20
454.50	0.24	72.75	454.50	-0.39	0.49	0.00	0.33
504.50	0.30	78.73	504.50	-0.30	0.55	0.23	0.13
554.50	0.20	98.10	554.50	-0.18	0.56	0.45	0.26
604.50	0.27	99.17	604.50	-0.04	0.53	0.65	0.14
654.50	0.33	102.17	654.50	0.16	0.48	0.91	0.12
704.50	0.19	120.50	704.50	0.34	0.41	1.12	0.32
754.50	0.13	81.73	754.50	0.45	0.37	1.25	0.24
804.50	0.30	117.61	804.50	0.59	0.32	1.42	0.42
854.50	0.27	106.76	854.49	0.80	0.23	1.65	0.12
904.50	0.22	71.19	904.49	0.93	0.22	1.85	0.31
954.50	0.30	52.54	954.49	0.96	0.33	2.05	0.23
1004.50	0.37	65.23	1004.49	0.99	0.48	2.30	0.20
1054.50	0.35	59.05	1054.49	1.04	0.63	2.57	0.09
1088.50	0.37	79.50	1088.49	1.10	0.70	2.77	0.38
1208.50	0.47	33.86	1208.49	1.10	1.18	3.43	0.28
1295.50	0.93	326.43	1295.48	0.28	2.06	3.23	1.00
1382.50	2.01	283.31	1382.46	-1.59	3.00	1.36	1.70
1468.50	3.78	263.92	1468.34	-4.20	3.05	-2.93	2.32
1556.50	6.01	254.82	1556.02	-7.37	1.54	-10.26	2.68
1642.50	8.03	251.36	1641.37	-10.89	-1.56	-20.30	2.40
1728.50	9.77	248.65	1726.33	-14.70	-6.14	-32.79	2.08
1814.50	11.09	246.81	1810.91	-18.58	-12.05	-47.19	1.58
1901.50	12.22	245.62	1896.11	-22.51	-19.15	-63.26	1.33
1989.50	13.13	243.51	1981.97	-26.29	-27.45	-80.69	1.16

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2076.50	13.65	243.68	2066.60	-29.90	-36.41	-98.74	0.60
2161.50	13.87	243.78	2149.16	-33.58	-45.36	-116.87	0.26
2208.50	14.22	242.35	2194.76	-35.52	-50.53	-127.04	1.05
2263.00	14.27	239.75	2247.58	-37.34	-57.02	-138.77	1.18
2352.00	13.70	236.88	2333.95	-39.25	-68.30	-157.07	1.01
2441.00	15.75	242.45	2420.02	-41.85	-79.65	-176.61	2.80
2531.00	17.65	245.23	2506.22	-46.64	-91.02	-199.83	2.29
2620.00	19.61	247.15	2590.56	-53.03	-102.47	-225.85	2.31
2710.00	21.54	251.19	2674.82	-61.74	-113.66	-255.41	2.66
2800.00	22.93	251.37	2758.12	-72.29	-124.59	-287.66	1.55
2889.00	23.17	251.15	2840.02	-83.06	-135.79	-320.66	0.29
2979.00	24.76	249.39	2922.26	-93.74	-148.14	-355.06	1.94
3068.00	28.73	250.37	3001.72	-105.22	-161.90	-392.67	4.49
3157.00	29.62	249.92	3079.43	-117.83	-176.63	-433.47	1.03
3247.00	31.29	252.83	3157.01	-132.04	-191.17	-476.70	2.48
3336.00	33.90	253.47	3231.99	-148.37	-205.06	-522.58	2.96
3426.00	35.85	253.41	3305.82	-166.13	-219.72	-571.91	2.17
3515.00	37.14	252.95	3377.37	-184.17	-235.04	-622.57	1.48
3605.00	37.88	252.87	3448.76	-202.61	-251.15	-674.95	0.82
3694.00	37.91	253.23	3518.99	-221.12	-267.09	-727.24	0.25
3784.00	37.85	253.22	3590.03	-240.00	-283.03	-780.15	0.07
3874.00	37.91	253.20	3661.07	-258.87	-299.00	-833.06	0.07
3963.00	37.87	253.30	3731.30	-277.56	-314.75	-885.40	0.08
4053.00	37.82	253.34	3802.37	-296.51	-330.60	-938.29	0.06
4142.00	37.76	253.24	3872.71	-315.20	-346.28	-990.53	0.10
4232.00	37.71	253.18	3943.88	-334.00	-362.19	-1043.26	0.07
4321.00	37.77	253.48	4014.26	-352.70	-377.82	-1095.44	0.22
4411.00	37.77	253.33	4085.41	-371.69	-393.57	-1148.27	0.10
4500.00	37.56	253.51	4155.86	-390.45	-409.08	-1200.39	0.27
4590.00	37.44	253.00	4227.26	-409.19	-424.87	-1252.86	0.37
4680.00	37.34	252.90	4298.77	-427.61	-440.89	-1305.11	0.13
4769.00	37.97	253.08	4369.23	-445.98	-456.80	-1357.10	0.72

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4859.00	38.57	253.27	4439.89	-464.97	-472.93	-1410.46	0.68
4948.00	38.77	253.28	4509.38	-484.02	-488.93	-1463.72	0.22
5038.00	37.86	252.88	4579.99	-502.95	-505.17	-1517.10	1.05
5127.00	38.84	253.66	4649.79	-521.85	-521.06	-1569.98	1.23
5217.00	38.79	253.58	4719.91	-541.49	-536.97	-1624.11	0.08
5307.00	38.59	253.30	4790.16	-560.91	-553.01	-1678.03	0.30
5396.00	38.68	253.44	4859.68	-580.02	-568.91	-1731.27	0.14
5485.00	38.67	253.62	4929.16	-599.30	-584.68	-1784.61	0.13
5575.00	38.80	253.51	4999.37	-618.85	-600.61	-1838.62	0.16
5664.00	38.53	253.53	5068.86	-638.11	-616.39	-1891.94	0.30
5753.00	38.53	253.35	5138.48	-657.25	-632.19	-1945.08	0.13
5843.00	38.54	253.43	5208.89	-676.55	-648.21	-1998.81	0.06
5932.00	38.59	253.37	5278.47	-695.67	-664.07	-2051.98	0.07
6022.00	38.52	253.51	5348.86	-715.03	-680.05	-2105.75	0.12
6111.00	38.49	253.36	5418.50	-734.15	-695.85	-2158.86	0.11
6201.00	38.53	253.20	5488.93	-753.34	-711.97	-2212.53	0.12
6290.00	37.34	253.36	5559.12	-772.08	-727.71	-2264.93	1.35
6380.00	38.25	253.58	5630.24	-791.14	-743.40	-2317.80	1.03
6469.00	38.11	253.47	5700.20	-810.20	-759.01	-2370.55	0.17
6559.00	38.14	253.58	5771.00	-829.46	-774.76	-2423.84	0.08
6648.00	37.06	253.46	5841.52	-848.27	-790.17	-2475.91	1.22
6738.00	38.73	252.19	5912.54	-866.78	-806.50	-2528.72	2.05
6827.00	38.67	245.56	5982.02	-881.75	-826.53	-2580.56	4.66
6917.00	38.42	232.00	6052.54	-887.15	-855.43	-2628.28	9.38
7006.00	38.63	220.46	6122.26	-880.39	-893.65	-2668.16	8.07
7096.00	39.16	208.75	6192.40	-862.36	-940.00	-2700.10	8.18
7185.00	42.31	197.27	6259.93	-833.06	-993.33	-2722.55	9.12
7274.00	46.21	188.14	6323.72	-792.64	-1053.82	-2736.01	8.38
7364.00	51.73	178.77	6382.86	-740.77	-1121.43	-2739.85	9.96
7453.00	55.45	175.35	6435.68	-681.25	-1192.93	-2736.13	5.20
7543.00	60.36	169.46	6483.52	-614.68	-1268.42	-2725.96	7.78
7632.00	66.34	161.35	6523.47	-541.07	-1345.24	-2705.80	10.55
7722.00	71.74	158.21	6555.66	-460.53	-1424.05	-2676.73	6.83

RECEIVED
Office of Oil and Gas
OCT 1 9
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7811.00	77.22	152.98	6579.48	-376.82	-1502.06	-2641.28	8.36
7900.00	80.78	149.13	6596.47	-290.29	-1578.47	-2599.00	5.83
7990.00	86.45	144.60	6606.48	-201.08	-1653.31	-2550.13	8.04
8079.00	86.19	143.16	6612.19	-112.28	-1725.05	-2497.77	1.64
8169.00	86.12	143.30	6618.23	-22.48	-1796.98	-2444.02	0.17
8258.00	88.77	143.93	6622.19	66.42	-1868.55	-2391.28	3.06
8348.00	89.45	144.24	6623.59	156.40	-1941.43	-2338.49	0.83
8437.00	89.68	143.26	6624.27	245.39	-2013.20	-2285.87	1.13
8527.00	88.74	144.23	6625.51	335.38	-2085.77	-2232.65	1.50
8616.00	89.95	143.83	6626.53	424.36	-2157.79	-2180.38	1.43
8706.00	89.85	144.26	6626.68	514.36	-2230.65	-2127.54	0.49
8795.00	89.72	144.03	6627.02	603.34	-2302.78	-2075.41	0.30
8885.00	89.52	143.44	6627.61	693.34	-2375.35	-2022.17	0.69
8974.00	89.68	143.04	6628.23	782.34	-2446.65	-1968.91	0.48
9064.00	88.94	141.61	6629.32	872.31	-2517.87	-1913.91	1.79
9153.00	89.18	143.14	6630.78	961.29	-2588.35	-1859.59	1.74
9247.00	89.53	140.92	6631.84	1055.26	-2662.44	-1801.76	2.39
9337.00	89.53	141.97	6632.58	1145.21	-2732.82	-1745.67	1.17
9426.00	89.50	141.70	6633.33	1234.18	-2802.79	-1690.67	0.31
9516.00	89.57	143.67	6634.06	1324.17	-2874.37	-1636.12	2.19
9605.00	89.43	143.47	6634.84	1413.16	-2945.97	-1583.27	0.27
9695.00	89.40	143.35	6635.75	1503.16	-3018.23	-1529.63	0.14
9784.00	89.47	143.36	6636.63	1592.15	-3089.64	-1476.51	0.08
9874.00	89.44	142.74	6637.49	1682.15	-3161.56	-1422.41	0.69
9964.00	89.57	143.49	6638.27	1772.14	-3233.54	-1368.40	0.85
10053.00	89.54	143.19	6638.96	1861.14	-3304.93	-1315.26	0.34
10142.00	89.88	143.08	6639.41	1950.14	-3376.14	-1261.86	0.40
10232.00	89.61	143.39	6639.81	2040.14	-3448.23	-1208.00	0.46
10321.00	88.87	142.45	6640.99	2129.13	-3519.23	-1154.34	1.34
10410.00	89.77	143.86	6642.05	2218.12	-3590.45	-1100.98	1.88
10500.00	89.77	143.50	6642.41	2308.11	-3662.96	-1047.67	0.40
10589.00	89.64	143.38	6642.86	2397.11	-3734.45	-994.66	0.20

10/23/2026

MD ft	INC deg	AZIM deg	TVD ft	VS ft	+N/-S ft	+E/-W ft	DLS °/100ft
10679.00	90.51	143.77	6642.75	2487.11	-3806.86	-941.22	1.06
10768.00	89.61	143.52	6642.65	2576.11	-3878.54	-888.46	1.05
10858.00	89.57	143.89	6643.30	2666.10	-3951.08	-835.19	0.41
10947.00	89.34	143.40	6644.14	2755.09	-4022.75	-782.43	0.61
11037.00	89.17	142.57	6645.31	2845.08	-4094.61	-728.26	0.94
11126.00	89.07	143.22	6646.68	2934.07	-4165.58	-674.57	0.74
11216.00	89.51	143.55	6647.80	3024.06	-4237.81	-620.90	0.61
11305.00	89.47	142.76	6648.59	3113.06	-4309.03	-567.53	0.89
11395.00	89.24	143.23	6649.60	3203.05	-4380.90	-513.37	0.58
11484.00	88.67	142.67	6651.23	3292.04	-4451.92	-459.75	0.90
11574.00	89.24	143.83	6652.87	3382.02	-4524.02	-405.91	1.44
11663.00	89.17	143.90	6654.10	3471.01	-4595.89	-353.43	0.11
11753.00	89.24	143.65	6655.35	3560.99	-4668.49	-300.25	0.29
11842.00	89.41	143.19	6656.40	3649.99	-4739.95	-247.22	0.55
11932.00	88.90	143.12	6657.73	3739.98	-4811.97	-193.26	0.57
12021.00	89.04	142.70	6659.33	3828.96	-4882.95	-139.59	0.50
12111.00	89.54	142.54	6660.44	3918.95	-4954.46	-84.96	0.58
12200.00	89.71	143.56	6661.02	4007.94	-5025.58	-31.46	1.16
12290.00	89.21	144.00	6661.87	4097.93	-5098.19	21.72	0.74
12379.00	89.68	144.54	6662.73	4186.92	-5170.43	73.69	0.80
12468.00	88.67	142.97	6664.02	4275.90	-5242.20	126.30	2.10
12558.00	89.37	144.25	6665.55	4365.88	-5314.63	179.69	1.62
12647.00	89.14	144.42	6666.71	4454.86	-5386.94	231.57	0.32
12732.00	89.17	143.14	6667.97	4539.84	-5455.50	281.79	1.51
12827.00	89.27	142.22	6669.26	4634.83	-5531.04	339.38	0.97
12923.00	89.85	143.77	6670.00	4730.82	-5607.70	397.16	1.72
13006.00	89.34	143.53	6670.58	4813.82	-5674.55	446.35	0.68
13096.00	89.17	143.04	6671.75	4903.81	-5746.69	500.15	0.58
13185.00	89.07	144.00	6673.12	4992.80	-5818.24	553.06	1.08
13275.00	89.01	143.62	6674.63	5082.78	-5890.87	606.19	0.43
13364.00	89.38	143.29	6675.88	5171.77	-5962.36	659.18	0.56
13454.00	89.07	142.56	6677.10	5261.76	-6034.16	713.44	0.88
13543.00	89.44	144.53	6678.25	5350.75	-6105.73	766.31	2.25

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13633.00	89.24	143.08	6679.29	5440.73	-6178.36	819.46	1.63
13723.00	89.71	143.99	6680.11	5530.73	-6250.74	872.94	1.14
13812.00	89.41	144.29	6680.80	5619.71	-6322.86	925.08	0.48
13901.00	89.34	144.03	6681.77	5708.70	-6395.01	977.19	0.30
13991.00	88.87	143.50	6683.17	5798.68	-6467.59	1030.38	0.79
14080.00	89.41	143.83	6684.51	5887.67	-6539.28	1083.10	0.71
14170.00	89.17	143.67	6685.63	5977.66	-6611.85	1136.32	0.32
14260.00	88.97	143.85	6687.09	6067.64	-6684.43	1189.52	0.30
14349.00	89.51	143.15	6688.27	6156.63	-6755.97	1242.45	0.99
14528.00	89.31	144.02	6690.11	6335.62	-6900.01	1348.70	0.50
14618.00	89.64	143.94	6690.93	6425.61	-6972.80	1401.63	0.38
14707.00	89.54	143.56	6691.57	6514.60	-7044.57	1454.25	0.44
14797.00	89.17	143.87	6692.58	6604.59	-7117.11	1507.51	0.54
14886.00	89.61	142.62	6693.53	6693.59	-7188.41	1560.76	1.49
14976.00	88.87	142.15	6694.73	6783.57	-7259.70	1615.69	0.97
15065.00	89.37	142.40	6696.09	6872.54	-7330.09	1670.14	0.63
15155.00	89.31	142.45	6697.13	6962.53	-7401.41	1725.02	0.09
15244.00	89.64	143.10	6697.95	7051.52	-7472.28	1778.85	0.82
15333.00	89.11	142.04	6698.92	7140.51	-7542.94	1832.94	1.33
15423.00	89.54	144.14	6699.98	7230.50	-7614.90	1886.99	2.38
15513.00	89.21	142.78	6700.96	7320.49	-7687.20	1940.57	1.55
15602.00	89.37	144.23	6702.06	7409.48	-7758.74	1993.49	1.64
15691.00	88.70	142.29	6703.56	7498.46	-7830.05	2046.72	2.31
15781.00	89.64	143.86	6704.86	7588.45	-7901.99	2100.78	2.03
15870.00	89.24	142.51	6705.73	7677.44	-7973.23	2154.11	1.58
15960.00	89.44	143.01	6706.77	7767.43	-8044.88	2208.57	0.60
16049.00	89.34	143.37	6707.72	7856.43	-8116.13	2261.89	0.42
16139.00	89.51	143.69	6708.62	7946.42	-8188.50	2315.39	0.40
16228.00	89.64	142.46	6709.28	8035.42	-8259.65	2368.85	1.39
16317.00	89.31	142.65	6710.10	8124.40	-8330.30	2422.96	0.43
16407.00	89.17	142.85	6711.29	8214.39	-8401.94	2477.43	0.27
16497.00	89.44	142.50	6712.38	8304.38	-8473.50	2532.00	0.49

10/23/2026

MD ft	INC deg	AZIM deg	TVD ft	VS ft	+N/-S ft	+E/-W ft	DLS °/100ft
16586.00	89.21	142.62	6713.43	8393.37	-8544.16	2586.10	0.29
16676.00	89.37	142.81	6714.55	8483.36	-8615.76	2640.62	0.28
16765.00	89.24	142.54	6715.63	8572.35	-8686.53	2694.58	0.34
16854.00	89.54	143.86	6716.57	8661.34	-8757.79	2747.89	1.52
16944.00	89.41	142.55	6717.40	8751.33	-8829.86	2801.79	1.46
17033.00	89.21	143.22	6718.47	8840.33	-8900.82	2855.49	0.79
17123.00	89.64	143.99	6719.37	8930.32	-8973.26	2908.89	0.98
17212.00	90.18	142.47	6719.51	9019.32	-9044.55	2962.16	1.81
17301.00	89.58	142.56	6719.70	9108.31	-9115.17	3016.32	0.68
17391.00	89.71	142.64	6720.26	9198.30	-9186.67	3070.98	0.17
17480.00	89.61	141.84	6720.78	9287.28	-9257.03	3125.48	0.91
17570.00	89.88	142.90	6721.19	9377.27	-9328.31	3180.43	1.22
17659.00	89.58	142.40	6721.60	9466.26	-9399.05	3234.43	0.66
17749.00	89.78	142.66	6722.11	9556.26	-9470.48	3289.18	0.36
17838.00	89.68	142.60	6722.53	9645.25	-9541.21	3343.19	0.13
17928.00	89.71	142.65	6723.01	9735.24	-9612.73	3397.83	0.06
18018.00	89.84	142.58	6723.36	9825.24	-9684.25	3452.47	0.16
18107.00	89.74	142.16	6723.69	9914.23	-9754.73	3506.81	0.49
18197.00	89.81	142.87	6724.04	10004.22	-9826.15	3561.58	0.79
18286.00	89.98	142.57	6724.20	10093.21	-9896.96	3615.49	0.39
18376.00	89.91	142.78	6724.29	10183.21	-9968.53	3670.06	0.25
18466.00	89.64	142.46	6724.64	10273.20	-10040.05	3724.70	0.47
18555.00	89.88	142.16	6725.01	10362.19	-10110.47	3779.11	0.43
18644.00	89.58	142.98	6725.43	10451.18	-10181.15	3833.20	0.98
18734.00	89.04	143.07	6726.52	10541.17	-10253.04	3887.33	0.61
18823.00	89.64	142.59	6727.54	10630.16	-10323.96	3941.10	0.86
18913.00	89.68	143.23	6728.08	10720.16	-10395.75	3995.37	0.71
19002.00	89.58	142.95	6728.65	10809.16	-10466.91	4048.82	0.33
19092.00	89.41	143.02	6729.45	10899.15	-10538.77	4103.00	0.20
19182.00	89.48	142.25	6730.32	10989.14	-10610.29	4157.62	0.86
19271.00	89.58	142.30	6731.05	11078.13	-10680.69	4212.07	0.13
19360.00	89.61	143.15	6731.68	11167.12	-10751.50	4265.97	0.96
19450.00	89.64	142.81	6732.27	11257.12	-10823.36	4320.16	0.38

RECEIVED
Office Of Oil & Gas
OCT 09
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19539.00	89.64	143.21	6732.82	11346.12	-10894.45	4373.71	0.45
19629.00	89.54	142.81	6733.47	11436.11	-10966.33	4427.86	0.46
19659.00	89.61	142.85	6733.69	11466.11	-10990.24	4445.98	0.27
19681.00	89.61	142.85	6733.84	11488.11	-11007.77	4459.27	0.00

10/23/2026
