Well Location Plat

CNX Applicant / Well Operator Name	DEP ID#	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	Well # MAJ8LHSM

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8LHSM OH As Drilled_ KOP	5696.63	39.92784529	-80.58240546	6402.00
MAJ8LHSM OH As Drilled_ LP	6610.12	39.92569499	-80.58265391	7832.00
MAJ8LHSM OH As Drilled_BHL	6701.73	39.89796761	-80.55513724	20545.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1060.50	Survey #1 (OH)	GYD_CT+WIR
1205.50	2209.50	Survey #2 (OH)	MWD+IFR1+Sag
2263.00	20545.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

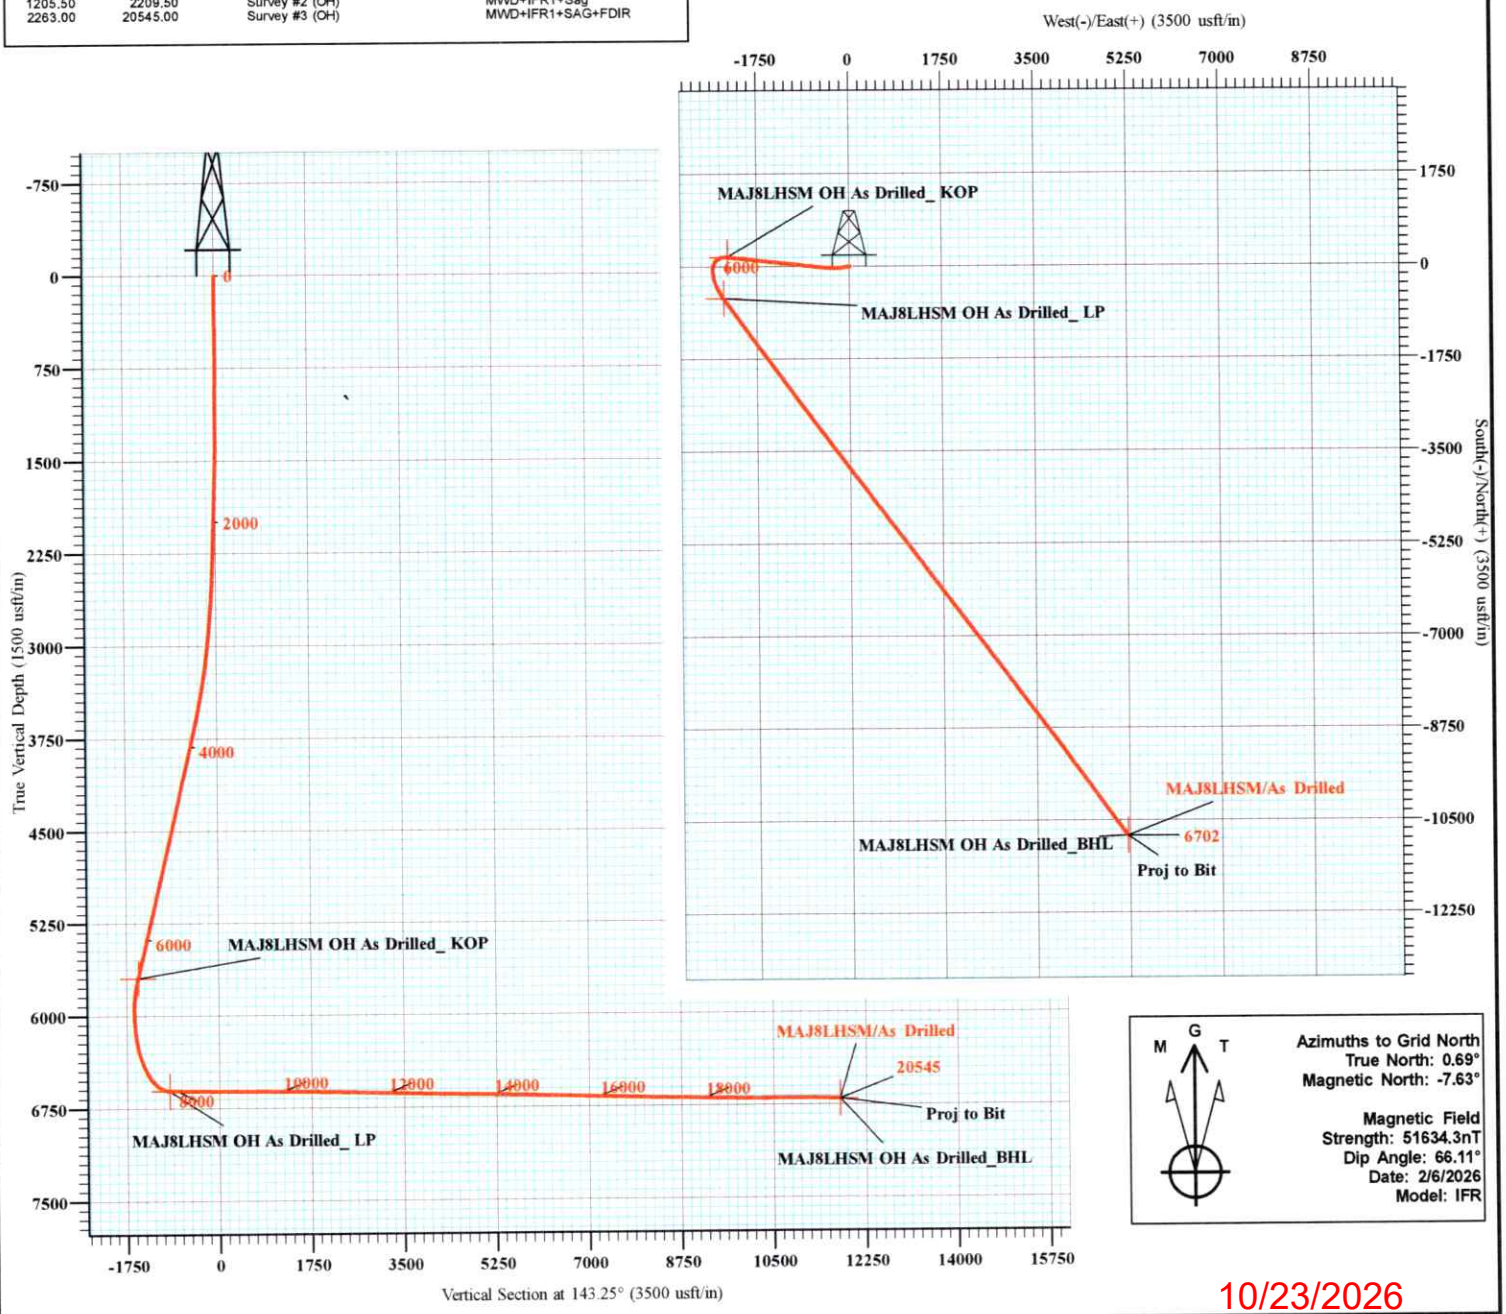


Azimuths to Grid North
True North: 0.69°
Magnetic North: -7.63°

Magnetic Field
Strength: 51634.3nT
Dip Angle: 66.11°
Date: 2/6/2026
Model: IFR

10/23/2026

FEBRUARY 8 2026
SURVEY REPORT

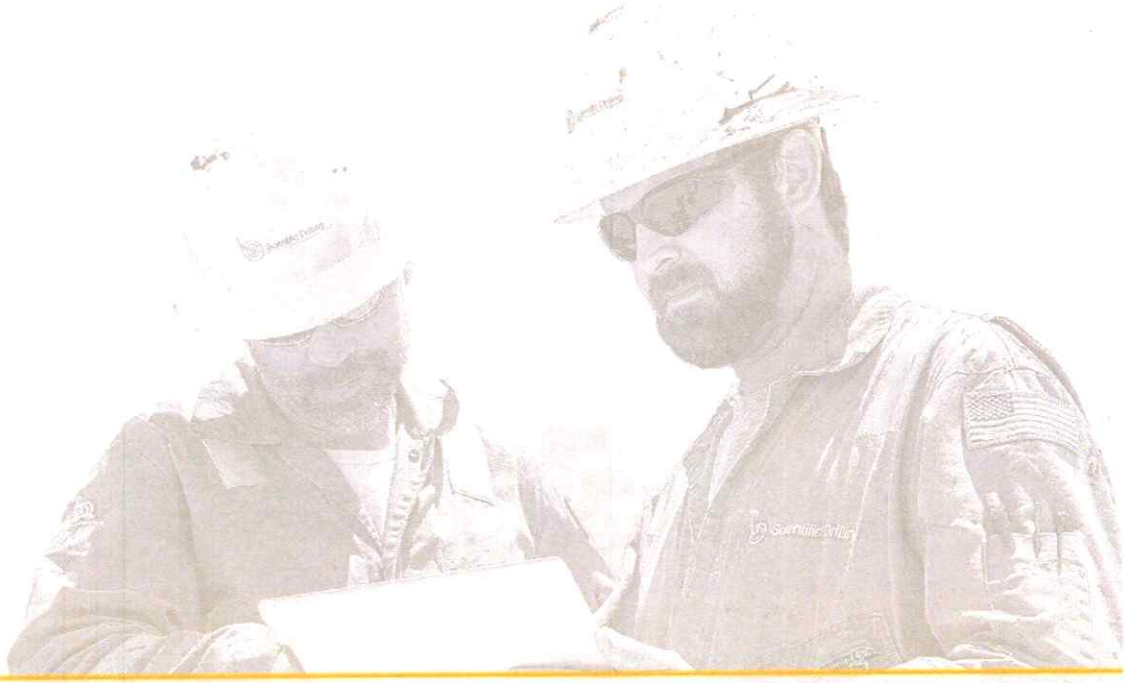

CNX RESOURCES
WELL: MAJ8LHSM
RIG: PRECISION DRILLING 539

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

CUSTOMER	**CNX RESOURCES**	SDI JOB NO.	**OP.051519**
PROJECT	**MAJ8 LHSM**	SDI DISTRICT	**Northeast**
FIELD	**Marcellus**	SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**	Section	-
Lat/Long	**39.9275261 N, 80.5742268 W**	Township	-
Northing	**521,744.52 ft**	Range	-
Easting	**1,698,736.42 ft**		

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.9274159 N, 80.5741571 W**
Northing	**521,704.14 ft**
Easting	**1,698,755.49 ft**
UWI	**47-051-02552**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.25°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-20545 ft	IFR1	06 Feb 2026	-8.32°	add 0.69°	subtract 7.63°

WELL NOTES

Gyro Surveys: 0 - 1160.5'.
Superior MSA MWD Corrected Surveys: 1205.5' - 20518'.
Survey @ 20545' is a Projection to Bit.

OPERATORS

J. GONZALEZ, T. SOLLEY

SDI Operator Name (Printed) SIGNATURE DATE

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.11	98.75	54.50	0.04	-0.01	0.05	0.20
104.50	0.18	138.41	104.50	0.15	-0.07	0.15	0.24
154.50	0.20	97.26	154.50	0.29	-0.14	0.29	0.27
204.50	0.41	115.04	204.50	0.51	-0.23	0.54	0.46
254.50	0.51	112.15	254.50	0.86	-0.39	0.91	0.21
304.50	0.53	106.03	304.50	1.23	-0.54	1.34	0.12
354.50	0.53	103.11	354.49	1.59	-0.65	1.78	0.05
404.50	0.72	111.78	404.49	2.04	-0.82	2.30	0.42
454.50	0.70	97.67	454.49	2.52	-0.98	2.89	0.35
504.50	0.75	113.69	504.48	3.02	-1.15	3.50	0.42
554.50	0.83	108.64	554.48	3.60	-1.40	4.14	0.21
604.50	0.69	111.81	604.47	4.15	-1.63	4.76	0.29
654.50	0.81	123.20	654.47	4.74	-1.93	5.34	0.38
704.50	0.71	120.86	704.46	5.36	-2.29	5.90	0.21
754.50	0.64	90.26	754.46	5.82	-2.45	6.44	0.73
804.50	0.54	95.94	804.46	6.14	-2.47	6.96	0.23
854.50	0.44	118.23	854.46	6.48	-2.59	7.36	0.43
904.50	0.39	97.78	904.46	6.77	-2.70	7.70	0.31
954.50	0.21	106.98	954.45	6.96	-2.75	7.96	0.37
1004.50	0.50	105.02	1004.45	7.21	-2.83	8.25	0.58
1054.50	0.39	95.15	1054.45	7.49	-2.91	8.63	0.27
1060.50	0.40	89.16	1060.45	7.52	-2.91	8.67	0.71
1205.50	0.51	327.52	1205.45	7.17	-2.35	8.83	0.55
1293.50	2.09	303.78	1293.42	5.27	-1.13	7.29	1.86
1379.50	3.95	285.58	1379.30	1.45	0.54	3.13	2.41
1465.50	5.58	271.68	1465.01	-3.50	1.45	-3.90	2.31
1553.50	6.95	261.90	1552.48	-8.71	0.83	-13.45	1.97
1639.50	7.95	258.35	1637.75	-13.73	-1.11	-24.42	1.28
1726.50	9.08	255.46	1723.79	-18.88	-4.04	-36.96	1.39
1811.50	9.28	258.42	1807.71	-24.33	-7.10	-50.17	0.60
1899.50	9.78	262.21	1894.49	-30.96	-9.54	-64.53	0.91
1986.50	10.48	260.04	1980.14	-38.11	-11.91	-79.64	0.92

RECEIVED
Office Of Oil and Gas
OCT
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2073.50	10.30	261.38	2065.71	-45.34	-14.45	-95.12	0.35
2159.50	9.43	262.95	2150.44	-52.46	-16.46	-109.72	1.06
2209.50	9.41	260.40	2199.76	-56.35	-17.65	-117.81	0.84
2352.00	9.42	256.98	2340.34	-66.36	-22.22	-140.66	0.39
2441.00	10.90	261.75	2427.95	-73.31	-25.07	-156.09	1.91
2531.00	12.54	265.42	2516.07	-82.57	-27.07	-174.25	2.00
2620.00	14.60	267.30	2602.58	-94.00	-28.37	-195.09	2.37
2710.00	17.13	269.28	2689.15	-108.15	-29.07	-219.67	2.87
2800.00	18.13	270.57	2774.92	-124.43	-29.09	-246.93	1.19
2889.00	19.37	270.68	2859.19	-141.80	-28.78	-275.54	1.39
2979.00	20.21	270.91	2943.88	-160.37	-28.36	-306.00	0.94
3068.00	22.65	271.42	3026.72	-180.35	-27.69	-338.51	2.75
3157.00	24.18	272.87	3108.39	-202.57	-26.35	-373.85	1.84
3247.00	26.94	274.13	3189.57	-227.67	-23.96	-412.60	3.13
3336.00	28.82	274.73	3268.24	-255.08	-20.74	-454.09	2.14
3426.00	30.67	275.58	3346.38	-284.91	-16.72	-498.56	2.11
3515.00	32.73	276.11	3422.10	-316.56	-11.95	-545.08	2.34
3605.00	33.96	276.62	3497.28	-350.37	-6.46	-594.25	1.40
3694.00	35.62	276.41	3570.37	-385.18	-0.70	-644.70	1.87
3784.00	37.03	275.59	3642.88	-421.36	4.86	-697.72	1.66
3874.00	36.68	276.03	3714.89	-457.87	10.33	-751.42	0.49
3963.00	38.67	276.40	3785.33	-494.94	16.22	-805.49	2.25
4053.00	38.46	276.64	3855.70	-533.40	22.59	-861.23	0.29
4142.00	38.36	276.45	3925.44	-571.32	28.89	-916.17	0.17
4232.00	38.45	276.72	3995.97	-609.69	35.31	-971.71	0.21
4321.00	38.37	276.35	4065.71	-647.60	41.60	-1026.64	0.27
4411.00	38.57	276.37	4136.17	-685.86	47.80	-1082.29	0.22
4500.00	38.16	276.32	4205.95	-723.60	53.91	-1137.19	0.46
4590.00	38.64	276.80	4276.48	-761.95	60.29	-1192.73	0.63
4680.00	38.54	276.38	4346.83	-800.48	66.74	-1248.49	0.31
4769.00	38.38	276.22	4416.52	-838.26	72.81	-1303.51	0.21
4859.00	38.32	276.06	4487.10	-876.27	78.78	-1359.03	0.13

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4948.00	37.77	276.44	4557.19	-913.68	84.75	-1413.56	0.67
5038.00	38.53	276.55	4627.97	-951.76	91.04	-1468.79	0.85
5127.00	38.10	276.36	4697.80	-989.54	97.25	-1523.62	0.50
5217.00	38.81	276.17	4768.28	-1027.72	103.35	-1579.26	0.80
5307.00	38.54	276.05	4838.54	-1065.98	109.34	-1635.18	0.31
5396.00	37.87	276.47	4908.48	-1103.52	115.34	-1689.90	0.81
5485.00	38.82	276.53	4978.28	-1141.36	121.59	-1744.76	1.07
5575.00	37.89	276.39	5048.85	-1179.59	127.88	-1800.25	1.04
5664.00	37.61	276.32	5119.22	-1216.83	133.91	-1854.40	0.32
5753.00	38.56	276.19	5189.28	-1254.27	139.89	-1908.97	1.07
5843.00	38.49	276.40	5259.69	-1292.53	146.03	-1964.69	0.16
5932.00	37.83	276.17	5329.66	-1330.06	152.05	-2019.35	0.76
6022.00	38.76	276.40	5400.30	-1368.12	158.16	-2074.79	1.05
6111.00	38.78	276.26	5469.69	-1406.19	164.31	-2130.18	0.10
6201.00	38.90	276.46	5539.79	-1444.76	170.56	-2186.27	0.19
6290.00	38.71	276.10	5609.15	-1482.82	176.66	-2241.71	0.33
6380.00	38.65	276.29	5679.40	-1521.14	182.73	-2297.63	0.15
6469.00	37.12	273.57	5749.65	-1557.49	187.45	-2352.07	2.54
6559.00	34.33	259.17	5822.84	-1586.22	184.36	-2404.20	9.82
6648.00	32.61	248.60	5897.14	-1603.55	170.89	-2451.22	6.82
6738.00	31.83	232.86	5973.42	-1609.82	147.67	-2492.80	9.34
6827.00	33.15	225.58	6048.51	-1606.41	116.45	-2528.90	4.63
6917.00	32.38	207.16	6124.39	-1592.49	77.69	-2557.55	11.08
7006.00	33.42	198.69	6199.15	-1568.09	33.24	-2576.29	5.30
7096.00	37.71	188.16	6272.41	-1534.49	-17.55	-2588.16	8.29
7185.00	42.97	178.82	6340.29	-1490.47	-74.92	-2591.40	8.99
7274.00	49.77	173.07	6401.69	-1436.24	-139.07	-2586.67	8.95
7364.00	53.40	168.59	6457.62	-1373.74	-208.63	-2575.37	5.61
7453.00	60.00	161.59	6506.50	-1304.74	-280.36	-2556.09	9.90
7543.00	66.41	159.51	6547.05	-1228.07	-356.05	-2529.32	7.41
7632.00	72.52	152.13	6578.30	-1146.81	-431.94	-2495.13	10.36
7722.00	79.31	146.76	6600.20	-1060.10	-507.01	-2450.75	9.51
7811.00	88.47	146.44	6609.66	-971.85	-580.81	-2402.08	10.30

RECEIVED
Office of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7900.00	90.79	143.01	6610.24	-882.90	-653.45	-2350.70	4.65
7990.00	90.45	143.58	6609.26	-792.91	-725.60	-2296.91	0.74
8079.00	90.12	143.07	6608.82	-703.91	-796.98	-2243.75	0.68
8168.00	89.28	144.85	6609.29	-614.92	-868.94	-2191.39	2.21
8258.00	89.61	143.65	6610.16	-524.94	-941.97	-2138.81	1.38
8347.00	89.75	142.83	6610.66	-435.94	-1013.28	-2085.55	0.93
8437.00	89.51	144.42	6611.24	-345.95	-1085.74	-2032.18	1.79
8527.00	89.98	143.22	6611.64	-255.96	-1158.38	-1979.05	1.43
8616.00	89.68	144.34	6611.90	-166.96	-1230.18	-1926.46	1.30
8706.00	90.22	145.50	6611.98	-77.00	-1303.83	-1874.74	1.42
8795.00	89.85	144.41	6611.93	11.96	-1376.69	-1823.63	1.29
8885.00	89.41	143.41	6612.51	101.95	-1449.42	-1770.62	1.21
8974.00	89.31	143.29	6613.50	190.94	-1520.82	-1717.50	0.18
9064.00	89.99	144.34	6614.05	280.93	-1593.45	-1664.36	1.39
9153.00	89.68	142.75	6614.31	369.93	-1665.04	-1611.48	1.82
9243.00	89.58	144.25	6614.89	459.92	-1737.38	-1557.95	1.67
9332.00	89.99	144.22	6615.22	548.91	-1809.60	-1505.93	0.46
9422.00	89.55	144.14	6615.58	638.90	-1882.57	-1453.26	0.50
9511.00	89.85	143.34	6616.05	727.89	-1954.33	-1400.62	0.96
9601.00	89.55	143.56	6616.52	817.89	-2026.63	-1347.03	0.41
9690.00	89.75	144.85	6617.07	906.87	-2098.82	-1294.97	1.47
9780.00	89.78	143.83	6617.43	996.85	-2171.94	-1242.51	1.13
9869.00	89.88	144.07	6617.70	1085.85	-2243.90	-1190.13	0.29
9959.00	90.02	143.44	6617.78	1175.84	-2316.48	-1136.92	0.72
10048.00	89.75	143.41	6617.96	1264.84	-2387.96	-1083.89	0.31
10137.00	89.52	144.06	6618.52	1353.84	-2459.72	-1031.24	0.77
10227.00	89.99	143.47	6618.91	1443.83	-2532.31	-978.05	0.84
10316.00	90.02	142.36	6618.90	1532.83	-2603.31	-924.38	1.25
10406.00	89.68	143.62	6619.14	1622.83	-2675.17	-870.21	1.45
10495.00	89.58	143.08	6619.71	1711.82	-2746.57	-817.08	0.62
10674.00	89.38	143.21	6621.34	1890.82	-2889.80	-709.72	0.13
10764.00	89.99	144.17	6621.83	1980.81	-2962.32	-656.43	1.26

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10853.00	89.25	142.72	6622.42	2069.80	-3033.81	-603.43	1.83
10943.00	89.65	142.51	6623.28	2159.79	-3105.31	-548.78	0.50
11032.00	89.65	142.82	6623.83	2248.79	-3176.08	-494.81	0.35
11122.00	89.58	144.15	6624.43	2338.78	-3248.41	-441.26	1.48
11211.00	89.38	144.06	6625.24	2427.77	-3320.50	-389.08	0.25
11301.00	89.79	143.47	6625.89	2517.76	-3393.09	-335.88	0.80
11390.00	89.65	142.66	6626.33	2606.76	-3464.23	-282.40	0.92
11480.00	88.78	142.02	6627.56	2696.74	-3535.47	-227.42	1.20
11569.00	88.68	142.18	6629.53	2785.70	-3605.68	-172.76	0.21
11659.00	89.52	142.71	6630.95	2875.68	-3677.02	-117.91	1.10
11748.00	89.82	143.16	6631.46	2964.68	-3748.04	-64.27	0.61
11838.00	89.89	142.63	6631.69	3054.67	-3819.82	-9.98	0.59
11927.00	89.55	142.58	6632.12	3143.67	-3890.52	44.07	0.39
12017.00	89.25	142.41	6633.06	3233.65	-3961.92	98.86	0.38
12106.00	89.22	142.92	6634.25	3322.64	-4032.67	152.84	0.57
12195.00	89.12	143.26	6635.54	3411.63	-4103.83	206.28	0.40
12285.00	89.65	143.28	6636.51	3501.63	-4175.96	260.10	0.59
12374.00	89.42	142.84	6637.23	3590.62	-4247.09	313.59	0.56
12463.00	88.81	142.35	6638.60	3679.60	-4317.78	367.64	0.88
12553.00	89.52	142.77	6639.92	3769.59	-4389.23	422.35	0.92
12643.00	89.89	142.71	6640.38	3859.58	-4460.86	476.84	0.42
12732.00	89.65	142.41	6640.74	3948.58	-4531.52	530.94	0.43
12822.00	89.55	142.49	6641.37	4038.56	-4602.88	585.79	0.14
12912.00	89.59	143.09	6642.04	4128.56	-4674.55	640.22	0.67
13001.00	89.48	143.01	6642.76	4217.56	-4745.67	693.71	0.15
13091.00	89.35	142.80	6643.68	4307.55	-4817.46	747.99	0.27
13181.00	89.75	141.69	6644.39	4397.53	-4888.61	803.10	1.31
13270.00	89.79	142.45	6644.75	4486.51	-4958.81	857.80	0.86
13360.00	89.78	143.21	6645.08	4576.51	-5030.53	912.18	0.84
13449.00	89.55	143.06	6645.60	4665.50	-5101.73	965.57	0.31
13539.00	89.45	142.67	6646.39	4755.50	-5173.48	1019.90	0.45
13628.00	89.62	142.61	6647.11	4844.49	-5244.21	1073.91	0.20
13718.00	89.28	143.04	6647.98	4934.48	-5315.92	1128.29	0.61

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13807.00	89.11	143.13	6649.23	5023.48	-5387.07	1181.74	0.22
13897.00	89.99	143.24	6649.93	5113.47	-5459.12	1235.67	0.99
13986.00	89.55	142.84	6650.29	5202.47	-5530.24	1289.18	0.67
14076.00	89.25	142.91	6651.23	5292.46	-5601.99	1343.50	0.34
14165.00	90.05	143.32	6651.78	5381.46	-5673.17	1396.91	1.01
14255.00	89.45	142.77	6652.17	5471.46	-5745.09	1451.02	0.90
14345.00	89.62	142.97	6652.90	5561.45	-5816.84	1505.34	0.29
14434.00	89.62	142.94	6653.49	5650.45	-5887.88	1558.96	0.03
14523.00	88.98	143.21	6654.58	5739.44	-5959.02	1612.42	0.78
14613.00	89.42	142.28	6655.83	5829.43	-6030.65	1666.90	1.14
14702.00	89.58	143.29	6656.61	5918.42	-6101.52	1720.72	1.15
14792.00	88.31	143.08	6658.27	6008.40	-6173.56	1774.65	1.43
14881.00	89.48	142.50	6659.98	6097.38	-6244.43	1828.46	1.47
14971.00	89.35	142.95	6660.90	6187.37	-6316.04	1882.96	0.52
15061.00	89.42	143.19	6661.87	6277.37	-6387.98	1937.03	0.28
15150.00	89.35	143.12	6662.82	6366.36	-6459.20	1990.40	0.11
15240.00	89.62	143.04	6663.63	6456.36	-6531.15	2044.46	0.31
15329.00	89.28	142.91	6664.49	6545.35	-6602.20	2098.05	0.41
15418.00	89.41	142.28	6665.50	6634.34	-6672.89	2152.11	0.72
15508.00	89.75	142.91	6666.16	6724.33	-6744.38	2206.78	0.80
15597.00	89.31	142.57	6666.89	6813.33	-6815.22	2260.66	0.62
15687.00	89.28	142.77	6668.00	6903.31	-6886.77	2315.23	0.22
15776.00	88.84	142.84	6669.46	6992.30	-6957.66	2369.03	0.50
15866.00	89.48	143.32	6670.78	7082.29	-7029.61	2423.08	0.89
15955.00	89.65	143.01	6671.46	7171.29	-7100.84	2476.44	0.40
16044.00	89.52	143.04	6672.10	7260.28	-7171.94	2529.97	0.15
16134.00	89.21	142.88	6673.10	7350.28	-7243.77	2584.18	0.39
16223.00	89.45	142.99	6674.14	7439.27	-7314.78	2637.82	0.30
16313.00	89.38	143.14	6675.06	7529.26	-7386.72	2691.89	0.18
16402.00	89.48	142.89	6675.94	7618.26	-7457.81	2745.44	0.30
16492.00	89.52	143.35	6676.73	7708.25	-7529.79	2799.45	0.51
16582.00	89.52	142.73	6677.48	7798.25	-7601.71	2853.56	0.69

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16671.00	89.55	142.90	6678.21	7887.24	-7672.61	2907.35	0.19
16760.00	89.15	142.94	6679.22	7976.24	-7743.61	2961.00	0.45
16850.00	89.38	142.89	6680.37	8066.23	-7815.40	3015.27	0.26
16939.00	89.45	142.87	6681.28	8155.22	-7886.36	3068.98	0.08
17029.00	89.45	143.43	6682.14	8245.22	-7958.38	3122.95	0.62
17118.00	89.52	143.16	6682.94	8334.21	-8029.73	3176.14	0.31
17207.00	89.48	143.43	6683.72	8423.21	-8101.08	3229.33	0.31
17297.00	89.58	143.08	6684.46	8513.21	-8173.19	3283.17	0.40
17386.00	89.45	143.16	6685.21	8602.20	-8244.38	3336.58	0.17
17476.00	89.62	143.23	6685.94	8692.20	-8316.44	3390.50	0.20
17565.00	89.45	143.10	6686.66	8781.20	-8387.67	3443.86	0.24
17655.00	89.78	143.22	6687.27	8871.19	-8459.70	3497.82	0.39
17744.00	89.58	142.79	6687.77	8960.19	-8530.78	3551.37	0.53
17834.00	89.48	143.15	6688.50	9050.19	-8602.62	3605.57	0.42
17924.00	89.28	143.07	6689.48	9140.18	-8674.60	3659.59	0.24
18013.00	89.21	142.95	6690.65	9229.17	-8745.68	3713.14	0.16
18103.00	89.48	143.12	6691.68	9319.17	-8817.59	3767.25	0.35
18192.00	89.25	143.00	6692.67	9408.16	-8888.72	3820.74	0.29
18282.00	89.48	142.52	6693.66	9498.15	-8960.36	3875.20	0.59
18372.00	89.48	143.96	6694.48	9588.15	-9032.46	3929.06	1.60
18461.00	89.78	144.17	6695.05	9677.13	-9104.52	3981.29	0.41
18550.00	89.92	144.06	6695.29	9766.12	-9176.63	4033.45	0.20
18639.00	89.68	143.91	6695.60	9855.12	-9248.62	4085.78	0.32
18729.00	89.78	143.50	6696.02	9945.11	-9321.16	4139.06	0.47
18818.00	89.99	143.82	6696.20	10034.11	-9392.85	4191.80	0.43
18908.00	89.85	143.75	6696.33	10124.11	-9465.46	4244.97	0.17
18998.00	89.75	144.09	6696.64	10214.10	-9538.20	4297.97	0.39
19087.00	90.29	143.90	6696.61	10303.09	-9610.19	4350.29	0.64
19177.00	90.19	144.05	6696.23	10393.08	-9682.98	4403.22	0.20
19266.00	89.95	143.95	6696.12	10482.07	-9754.98	4455.54	0.29
19356.00	90.26	144.04	6695.96	10572.07	-9827.79	4508.44	0.36
19445.00	90.52	144.36	6695.35	10661.05	-9899.97	4560.50	0.46
19535.00	90.15	144.15	6694.83	10751.04	-9973.02	4613.08	0.47

RECEIVED
Office Of Oil and Gas
OCT 0 8 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19624.00	90.02	143.57	6694.69	10840.03	-10044.89	4665.57	0.67
19713.00	90.22	144.33	6694.51	10929.02	-10116.85	4717.94	0.88
19803.00	90.39	144.72	6694.03	11019.00	-10190.14	4770.17	0.47
19892.00	89.72	142.99	6693.94	11107.99	-10262.01	4822.67	2.08
19982.00	88.64	143.18	6695.23	11197.98	-10333.96	4876.72	1.22
20071.00	89.28	144.11	6696.85	11286.96	-10405.62	4929.46	1.27
20160.00	89.55	144.07	6697.76	11375.95	-10477.70	4981.66	0.31
20250.00	88.95	144.03	6698.93	11465.93	-10550.55	5034.49	0.67
20339.00	89.58	143.74	6700.08	11554.92	-10622.44	5086.95	0.78
20429.00	89.65	144.49	6700.68	11644.90	-10695.36	5139.70	0.84
20518.00	89.38	143.74	6701.43	11733.89	-10767.46	5191.87	0.90
20545.00	89.38	143.74	6701.73	11760.89	-10789.23	5207.83	0.00

10/23/2026
