Well Location Plat

CNX Applicant / Well Operator Name	DEP ID#	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	Well # MAJ8NHSM

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8NHSM OH As Drilled_ KOP	5730.54	39.92902204	-80.57847887	5949.00
MAJ8NHSM OH As Drilled_ LP	6623.96	39.92717325	-80.57742990	7290.00
MAJ8NHSM OH As Drilled_BHL	6745.76	39.89894844	-80.54937089	20240.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1094.50	Survey #1 (OH)	GYD_CT+WIR
1189.50	2209.50	Survey #2 (OH)	MWD+IFR1+SAG+FDIR
2347.00	20240.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

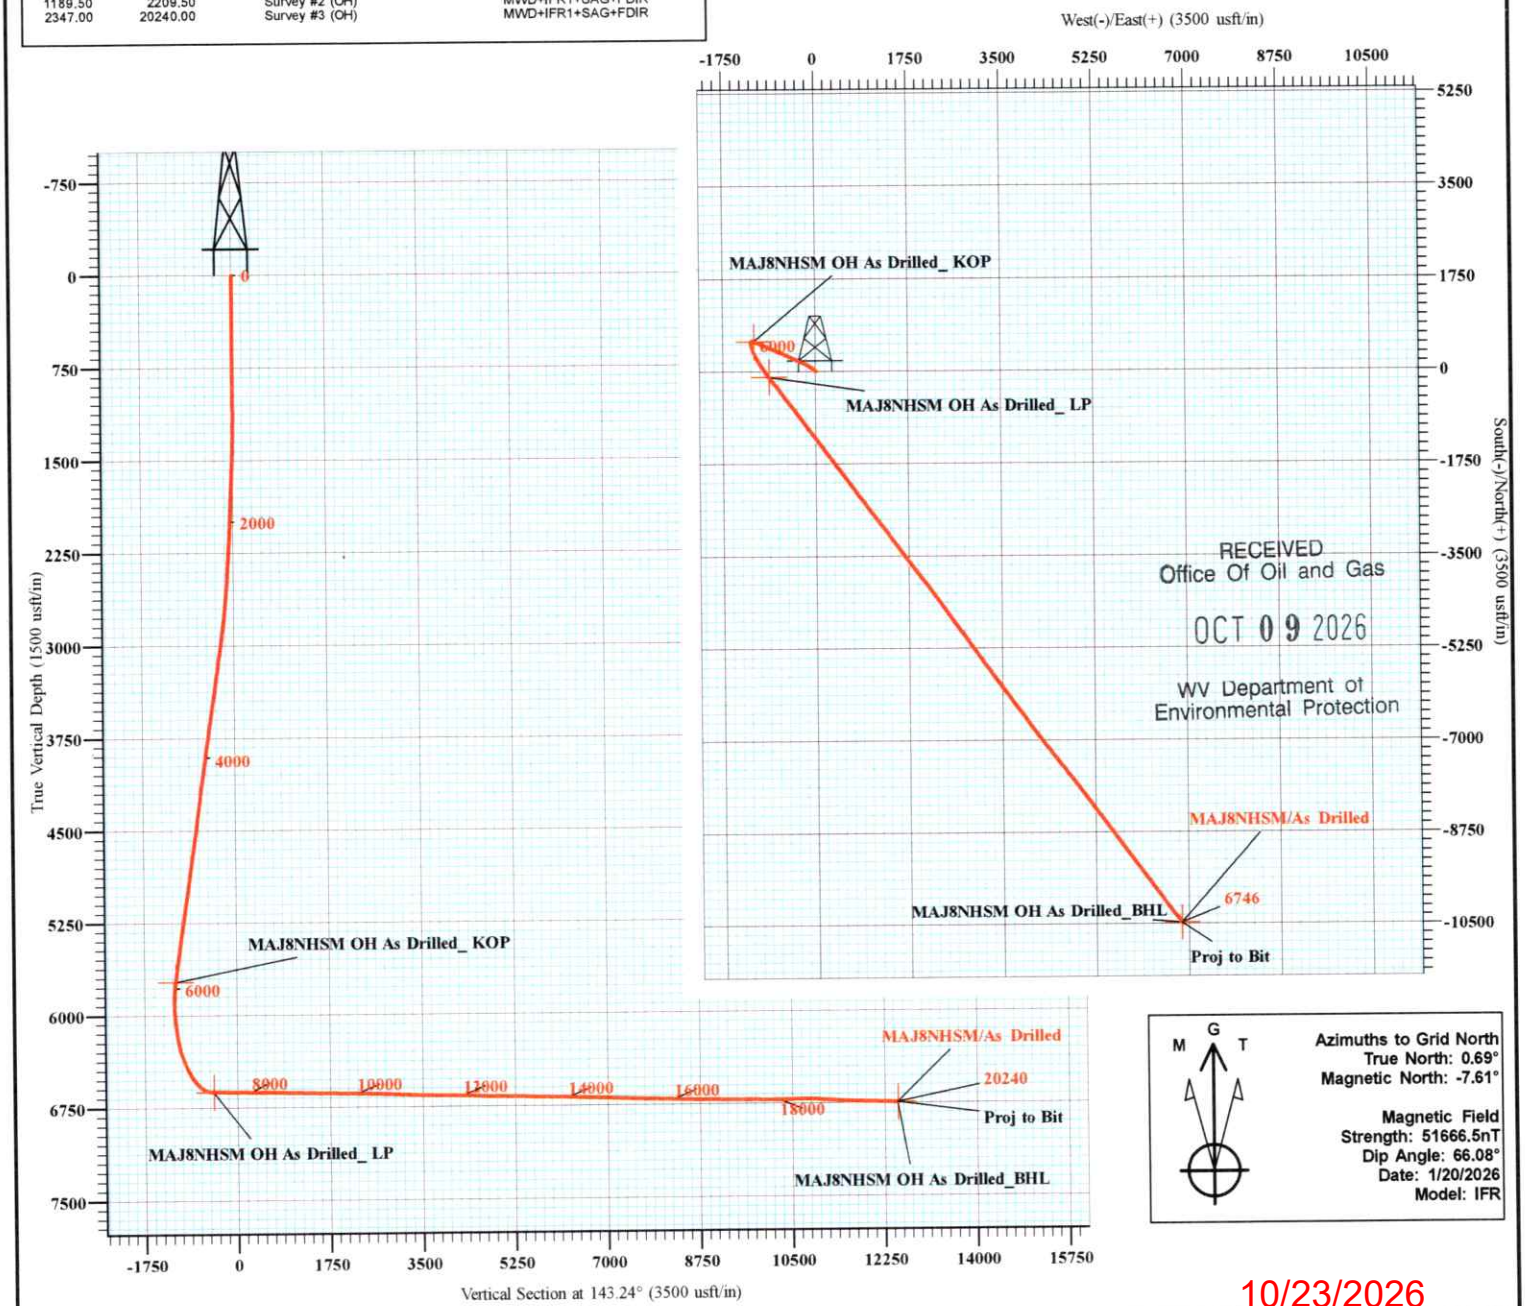


RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

Azimuths to Grid North
True North: 0.69°
Magnetic North: -7.61°

Magnetic Field
Strength: 51666.5nT
Dip Angle: 66.08°
Date: 1/20/2026
Model: IFR

10/23/2026

JANUARY 21 2026
SURVEY REPORT

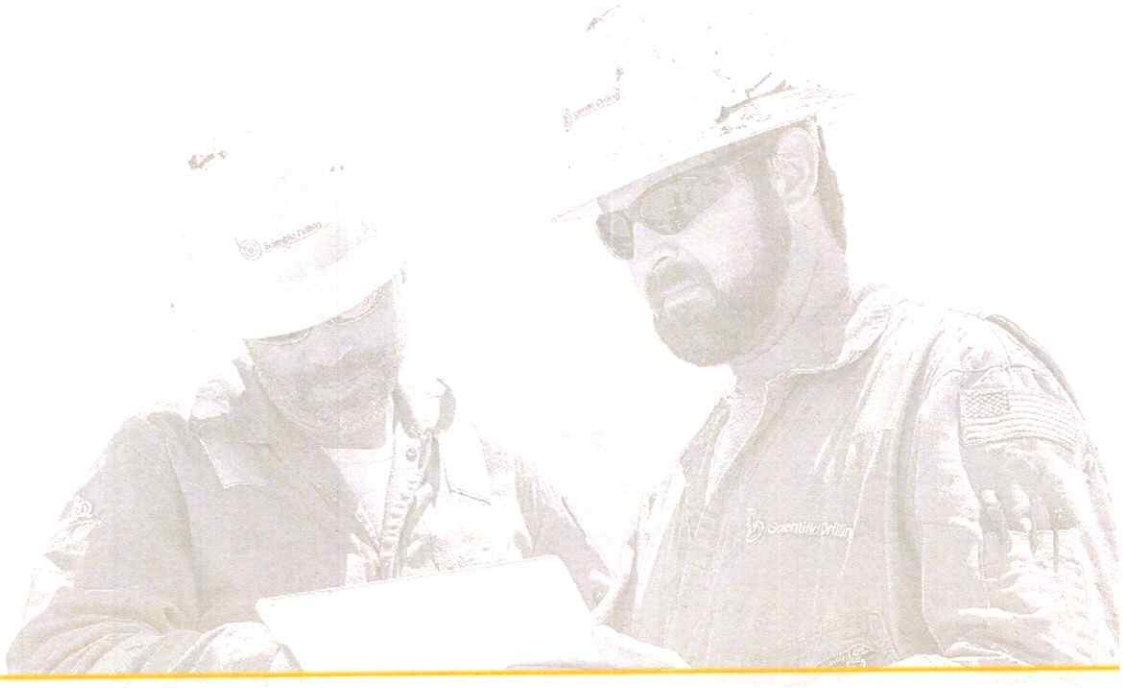

CNX RESOURCES
WELL: MAJ8 NHSM
RIG: PRECISION DRILLING 539

RECEIVED
Office Of Oil and Gas

OCT 09 2026

WV Department of
Environmental Protection

10/23/2026

CUSTOMER	**CNX Resources**	SDI JOB NO.	**OP.051517**
PROJECT	**MAJ8 NHSM**	SDI DISTRICT	**Northeast**
FIELD	**Marcellus**	SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**	Section	-
Lat/Long	**39.927526 N, 80.574227 W**	Township	-
Northing	**521,744.52 ft**	Range	-
Easting	**1,698,736.42 ft**		

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.927483 N, 80.57427 W**
Northing	**521,728.81 ft**
Easting	**1,698,724.04 ft**
UWI	**47-051-02554**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.24°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-20240 ft	IFR1	20 Jan 2026	-8.30°	add 0.69°	subtract 7.61°

WELL NOTES

Gyro Surveys From 0' To 1094.5'

Superior MSA MWD Corrected Surveys From 1189.5' To 20218'

Survey At 20240' Is A Projection To The Bit

OPERATORS

D. BARKER, J. WITKOWSKI

SDI Operator Name (Printed) SIGNATURE DATE

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.46	253.51	54.50	-0.08	-0.06	-0.21	0.84
104.50	0.54	278.85	104.50	-0.31	-0.08	-0.64	0.47
154.50	0.07	214.52	154.50	-0.47	-0.07	-0.89	1.03
204.50	0.06	201.63	204.50	-0.45	-0.12	-0.91	0.04
254.50	0.14	203.18	254.50	-0.40	-0.20	-0.95	0.16
304.50	0.14	153.90	304.50	-0.31	-0.31	-0.94	0.23
354.50	0.08	134.29	354.50	-0.22	-0.39	-0.89	0.14
404.50	0.14	81.46	404.50	-0.16	-0.41	-0.81	0.22
454.50	0.23	62.93	454.50	-0.11	-0.35	-0.66	0.21
504.50	0.30	110.07	504.50	0.02	-0.35	-0.44	0.44
554.50	0.21	120.50	554.50	0.21	-0.44	-0.24	0.20
604.50	0.31	153.12	604.49	0.43	-0.61	-0.10	0.35
654.50	0.26	139.49	654.49	0.67	-0.82	0.03	0.17
704.50	0.34	134.11	704.49	0.93	-1.01	0.21	0.17
754.50	0.18	151.12	754.49	1.16	-1.18	0.36	0.35
804.50	0.22	132.23	804.49	1.33	-1.31	0.47	0.15
854.50	0.32	116.79	854.49	1.55	-1.44	0.66	0.25
904.50	0.20	107.99	904.49	1.75	-1.53	0.87	0.25
954.50	0.34	102.08	954.49	1.93	-1.59	1.10	0.29
1004.50	0.29	104.10	1004.49	2.14	-1.65	1.37	0.10
1054.50	0.32	94.43	1054.49	2.33	-1.69	1.63	0.12
1094.50	0.17	118.07	1094.49	2.46	-1.73	1.79	0.44
1189.50	0.31	59.03	1189.49	2.61	-1.66	2.14	0.28
1277.50	1.55	339.22	1277.48	1.49	-0.43	1.92	1.73
1362.50	3.00	330.95	1362.41	-1.82	2.59	0.43	1.74
1450.50	4.41	320.52	1450.22	-7.48	7.22	-2.84	1.77
1537.50	5.73	314.47	1536.88	-15.12	12.84	-8.07	1.63
1623.50	6.70	312.97	1622.37	-24.30	19.27	-14.80	1.14
1710.50	6.23	310.62	1708.82	-33.90	25.80	-22.10	0.62
1795.50	5.31	307.14	1793.39	-42.18	31.18	-28.73	1.16
1883.50	5.88	306.55	1880.97	-50.41	36.32	-35.60	0.65
1970.50	6.67	306.75	1967.45	-59.52	42.00	-43.23	0.91

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2056.50	7.42	305.06	2052.80	-69.58	48.18	-51.78	0.90
2141.50	7.41	306.36	2137.09	-80.04	54.58	-60.68	0.20
2209.50	7.13	309.17	2204.54	-88.33	59.85	-67.49	0.67
2347.00	9.93	302.65	2340.51	-107.71	71.63	-84.09	2.15
2436.00	9.87	301.76	2428.18	-121.99	79.79	-97.03	0.18
2526.00	9.86	302.63	2516.85	-136.39	88.00	-110.08	0.17
2616.00	11.78	303.51	2605.25	-152.25	97.23	-124.23	2.14
2705.00	12.94	303.87	2692.19	-170.20	107.80	-140.08	1.31
2795.00	15.74	299.16	2779.38	-190.86	119.37	-159.11	3.37
2884.00	19.07	296.57	2864.29	-214.88	131.76	-182.67	3.84
2973.00	20.85	295.35	2947.94	-241.87	145.04	-209.99	2.05
3063.00	20.74	295.82	3032.08	-270.17	158.84	-238.81	0.22
3152.00	20.83	294.58	3115.29	-298.05	172.29	-267.38	0.50
3242.00	20.93	294.98	3199.38	-326.25	185.73	-296.50	0.19
3331.00	20.79	294.91	3282.54	-354.15	199.10	-325.24	0.16
3421.00	20.80	294.57	3366.68	-382.23	212.47	-354.26	0.13
3510.00	20.83	294.70	3449.87	-410.00	225.65	-383.01	0.06
3600.00	20.84	294.62	3533.99	-438.11	239.01	-412.10	0.03
3689.00	20.84	294.27	3617.16	-465.86	252.11	-440.92	0.14
3779.00	20.67	294.68	3701.32	-493.81	265.32	-469.95	0.25
3869.00	21.03	294.51	3785.43	-521.92	278.66	-499.08	0.41
3958.00	20.57	294.26	3868.63	-549.61	291.71	-527.86	0.53
4048.00	20.47	294.23	3952.92	-577.20	304.66	-556.63	0.11
4137.00	20.61	294.24	4036.26	-604.51	317.48	-585.10	0.16
4227.00	20.68	293.99	4120.48	-632.23	330.44	-614.06	0.13
4317.00	19.68	294.31	4204.95	-659.36	343.14	-642.39	1.12
4406.00	20.20	293.45	4288.62	-685.81	355.43	-670.15	0.67
4496.00	20.90	293.59	4372.89	-713.25	368.03	-699.12	0.78
4585.00	20.76	294.09	4456.07	-740.82	380.83	-728.06	0.25
4675.00	20.43	293.61	4540.32	-768.40	393.63	-757.02	0.41
4764.00	21.35	293.82	4623.47	-796.02	406.39	-786.07	1.04
4854.00	21.19	293.96	4707.34	-824.48	419.61	-815.92	0.19

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4943.00	21.22	293.36	4790.31	-852.47	432.53	-845.41	0.25
5033.00	20.24	293.13	4874.49	-880.06	445.11	-874.68	1.09
5122.00	21.48	293.75	4957.65	-907.56	457.72	-903.75	1.42
5212.00	21.22	293.72	5041.47	-936.08	470.91	-933.75	0.29
5301.00	21.12	293.23	5124.47	-963.98	483.71	-963.23	0.23
5390.00	21.19	293.38	5207.47	-991.82	496.42	-992.73	0.10
5480.00	21.16	293.29	5291.39	-1020.00	509.29	-1022.58	0.05
5569.00	21.18	293.61	5374.39	-1047.89	522.08	-1052.06	0.13
5659.00	21.09	293.88	5458.33	-1076.14	535.15	-1081.77	0.15
5748.00	20.63	293.69	5541.50	-1103.73	547.93	-1110.77	0.52
5838.00	18.89	293.32	5626.20	-1130.15	560.07	-1138.67	1.94
5927.00	20.86	293.37	5709.89	-1156.38	572.06	-1166.45	2.21
6017.00	15.89	274.33	5795.35	-1178.41	579.36	-1193.48	8.59
6106.00	11.91	247.96	5881.81	-1188.76	576.83	-1214.17	8.30
6196.00	11.92	210.68	5970.00	-1187.56	565.33	-1227.54	8.41
6285.00	15.86	185.17	6056.46	-1174.97	545.29	-1233.33	8.08
6375.00	20.89	171.89	6141.88	-1151.71	517.13	-1232.18	7.24
6464.00	28.18	164.37	6222.81	-1118.13	481.12	-1224.26	8.90
6554.00	36.03	159.23	6299.00	-1072.78	435.83	-1209.13	9.23
6643.00	43.06	154.16	6367.61	-1017.70	383.93	-1186.57	8.69
6733.00	46.91	154.18	6431.25	-955.25	326.68	-1158.85	4.28
6822.00	54.42	150.81	6487.64	-887.36	265.73	-1127.00	8.93
6912.00	61.90	149.84	6535.08	-811.53	199.36	-1089.15	8.36
7001.00	67.98	147.81	6572.77	-731.33	130.44	-1047.41	7.14
7090.00	75.06	147.99	6600.96	-647.26	58.97	-1002.58	7.96
7180.00	83.06	143.73	6618.03	-559.08	-14.06	-953.01	10.03
7269.00	89.52	143.02	6623.79	-470.31	-85.30	-900.05	7.30
7359.00	89.59	142.99	6624.49	-380.31	-157.18	-845.89	0.08
7448.00	89.29	141.40	6625.36	-291.34	-227.49	-791.34	1.82
7538.00	90.23	143.23	6625.73	-201.35	-298.71	-736.33	2.29
7627.00	90.13	143.17	6625.45	-112.35	-369.98	-683.01	0.13
7716.00	91.24	144.23	6624.39	-23.37	-441.70	-630.33	1.72
7806.00	88.62	143.38	6624.50	66.62	-514.32	-577.19	3.06

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection
10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7895.00	88.69	142.08	6626.59	155.59	-585.12	-523.31	1.46
7984.00	89.23	142.33	6628.20	244.56	-655.44	-468.77	0.67
8074.00	89.83	142.62	6628.94	334.55	-726.82	-413.96	0.74
8164.00	89.96	142.72	6629.11	424.55	-798.38	-359.38	0.18
8253.00	90.23	144.59	6628.96	513.54	-870.06	-306.64	2.12
8343.00	89.83	143.39	6628.91	603.53	-942.86	-253.72	1.41
8432.00	88.99	142.85	6629.83	692.52	-1014.05	-200.32	1.12
8522.00	89.76	143.68	6630.81	782.52	-1086.17	-146.49	1.26
8611.00	89.63	143.30	6631.29	871.51	-1157.70	-93.54	0.45
8701.00	89.83	142.45	6631.71	961.51	-1229.46	-39.22	0.97
8790.00	89.23	143.01	6632.44	1050.50	-1300.28	14.67	0.92
8880.00	89.06	143.22	6633.78	1140.49	-1372.26	68.69	0.30
8969.00	89.33	143.58	6635.03	1229.48	-1443.70	121.75	0.51
9059.00	89.39	143.10	6636.04	1319.48	-1515.90	175.48	0.54
9148.00	89.26	143.40	6637.09	1408.47	-1587.20	228.72	0.37
9238.00	89.33	143.23	6638.19	1498.46	-1659.37	282.49	0.20
9327.00	89.66	143.40	6638.98	1587.46	-1730.74	335.66	0.42
9417.00	89.76	143.34	6639.43	1677.46	-1802.97	389.35	0.13
9506.00	89.96	142.96	6639.65	1766.46	-1874.18	442.73	0.48
9596.00	89.49	143.71	6640.08	1856.46	-1946.38	496.47	0.98
9686.00	90.00	144.06	6640.48	1946.45	-2019.08	549.52	0.69
9775.00	89.97	144.16	6640.51	2035.44	-2091.18	601.69	0.12
9864.00	89.76	142.21	6640.72	2124.43	-2162.43	655.02	2.20
9953.00	89.83	143.86	6641.04	2213.43	-2233.54	708.53	1.86
10043.00	88.72	143.16	6642.17	2303.42	-2305.89	762.05	1.46
10132.00	89.19	142.04	6643.80	2392.40	-2376.58	816.10	1.36
10222.00	89.80	143.92	6644.59	2482.39	-2448.43	870.28	2.20
10311.00	88.82	144.19	6645.66	2571.37	-2520.48	922.52	1.14
10400.00	89.06	142.51	6647.31	2660.35	-2591.86	975.64	1.91
10490.00	89.70	143.09	6648.28	2750.35	-2663.55	1030.05	0.96
10580.00	89.23	142.00	6649.12	2840.33	-2734.99	1084.77	1.32
10669.00	89.33	142.24	6650.24	2929.31	-2805.23	1139.42	0.29

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10759.00	88.79	142.23	6651.72	3019.28	-2876.37	1194.53	0.60
10848.00	88.86	142.44	6653.54	3108.25	-2946.81	1248.90	0.25
10938.00	89.36	142.69	6654.94	3198.24	-3018.26	1303.60	0.62
11027.00	89.53	143.03	6655.80	3287.23	-3089.20	1357.33	0.43
11117.00	89.06	142.91	6656.91	3377.22	-3161.05	1411.53	0.54
11206.00	89.33	142.77	6658.16	3466.21	-3231.97	1465.28	0.34
11296.00	89.23	142.84	6659.29	3556.20	-3303.66	1519.69	0.14
11385.00	89.53	142.58	6660.26	3645.19	-3374.46	1573.60	0.45
11474.00	90.23	142.66	6660.44	3734.18	-3445.18	1627.64	0.79
11564.00	89.29	143.06	6660.82	3824.18	-3516.92	1681.97	1.14
11654.00	89.23	143.50	6661.98	3914.17	-3589.06	1735.78	0.49
11743.00	89.86	143.45	6662.69	4003.17	-3660.57	1788.75	0.71
11832.00	89.36	142.69	6663.29	4092.17	-3731.72	1842.22	1.02
11922.00	89.56	142.74	6664.14	4182.16	-3803.32	1896.74	0.23
12011.00	89.80	142.95	6664.64	4271.15	-3874.25	1950.49	0.36
12100.00	89.76	141.58	6664.98	4360.14	-3944.64	2004.96	1.54
12190.00	88.99	141.55	6665.96	4450.09	-4015.13	2060.90	0.86
12279.00	89.29	141.95	6667.30	4539.05	-4085.01	2115.99	0.56
12369.00	88.62	144.26	6668.94	4629.03	-4156.97	2170.01	2.67
12459.00	88.86	144.41	6670.92	4718.99	-4230.07	2222.47	0.31
12549.00	89.33	144.32	6672.34	4808.96	-4303.21	2274.90	0.53
12638.00	89.43	144.53	6673.30	4897.94	-4375.60	2326.68	0.26
12728.00	90.10	144.24	6673.67	4987.92	-4448.76	2379.09	0.81
12818.00	90.03	144.70	6673.57	5077.90	-4522.00	2431.39	0.52
12907.00	89.59	145.54	6673.87	5166.85	-4595.01	2482.28	1.07
12997.00	89.49	143.72	6674.59	5256.82	-4668.40	2534.38	2.03
13086.00	89.36	143.76	6675.48	5345.81	-4740.16	2587.01	0.15
13176.00	89.36	143.64	6676.49	5435.80	-4812.69	2640.29	0.13
13265.00	88.79	142.93	6677.92	5524.79	-4884.02	2693.49	1.02
13355.00	89.53	144.41	6679.24	5614.77	-4956.52	2746.80	1.84
13444.00	88.99	143.77	6680.39	5703.76	-5028.59	2799.00	0.94
13534.00	90.33	145.22	6680.93	5793.73	-5101.86	2851.26	2.19
13623.00	89.83	144.95	6680.80	5882.68	-5174.84	2902.20	0.64

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13713.00	89.76	144.11	6681.12	5972.66	-5248.13	2954.43	0.94
13802.00	89.39	145.15	6681.78	6061.63	-5320.70	3005.94	1.24
13892.00	88.99	144.19	6683.06	6151.59	-5394.12	3057.98	1.16
13981.00	88.99	144.43	6684.63	6240.56	-5466.39	3109.90	0.27
14071.00	89.59	144.34	6685.74	6330.53	-5539.55	3162.30	0.67
14160.00	89.46	144.27	6686.48	6419.52	-5611.83	3214.23	0.17
14250.00	89.09	143.87	6687.62	6509.50	-5684.70	3267.04	0.61
14339.00	89.02	143.74	6689.09	6598.48	-5756.51	3319.59	0.17
14429.00	89.56	143.92	6690.20	6688.47	-5829.16	3372.70	0.63
14518.00	89.22	144.17	6691.15	6777.46	-5901.20	3424.95	0.47
14608.00	89.49	143.22	6692.16	6867.45	-5973.72	3478.24	1.10
14698.00	89.19	143.68	6693.20	6957.44	-6046.02	3531.83	0.61
14787.00	89.29	143.54	6694.38	7046.43	-6117.66	3584.63	0.19
14877.00	89.16	143.27	6695.60	7136.42	-6189.91	3638.28	0.33
14966.00	89.52	143.31	6696.62	7225.41	-6261.25	3691.47	0.41
15055.00	89.19	143.67	6697.62	7314.41	-6332.78	3744.42	0.55
15145.00	89.22	143.12	6698.87	7404.40	-6405.02	3798.08	0.61
15234.00	89.42	142.94	6699.93	7493.39	-6476.13	3851.60	0.30
15324.00	89.16	143.82	6701.04	7583.38	-6548.35	3905.28	1.02
15413.00	89.29	143.59	6702.25	7672.37	-6620.08	3957.96	0.30
15503.00	89.26	143.18	6703.39	7762.36	-6692.31	4011.64	0.46
15592.00	89.39	142.90	6704.43	7851.36	-6763.42	4065.14	0.35
15682.00	89.69	142.86	6705.16	7941.35	-6835.19	4119.46	0.34
15771.00	89.52	142.88	6705.77	8030.35	-6906.14	4173.18	0.19
15860.00	89.39	142.55	6706.62	8119.34	-6976.95	4227.09	0.40
15950.00	89.52	142.35	6707.47	8209.33	-7048.30	4281.94	0.27
16039.00	89.19	142.69	6708.47	8298.32	-7118.92	4336.09	0.53
16129.00	89.42	142.40	6709.57	8388.30	-7190.36	4390.82	0.41
16218.00	89.22	142.59	6710.62	8477.29	-7260.96	4445.00	0.31
16308.00	89.32	142.48	6711.77	8567.27	-7332.39	4499.74	0.17
16398.00	89.42	142.19	6712.76	8657.26	-7403.63	4554.73	0.34
16487.00	89.32	142.32	6713.74	8746.24	-7474.00	4609.21	0.18

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16576.00	89.19	142.47	6714.89	8835.22	-7544.50	4663.51	0.22
16666.00	89.86	142.19	6715.64	8925.21	-7615.74	4718.51	0.81
16755.00	89.76	142.00	6715.94	9014.19	-7685.96	4773.19	0.24
16845.00	89.59	142.64	6716.45	9104.17	-7757.19	4828.20	0.74
16934.00	89.86	142.11	6716.87	9193.16	-7827.68	4882.53	0.67
17023.00	89.73	142.39	6717.19	9282.15	-7898.05	4937.02	0.35
17113.00	90.03	143.57	6717.38	9372.15	-7969.91	4991.21	1.35
17202.00	89.86	143.20	6717.47	9461.15	-8041.34	5044.29	0.46
17292.00	89.73	143.26	6717.79	9551.15	-8113.44	5098.16	0.16
17381.00	90.43	142.97	6717.66	9640.14	-8184.62	5151.58	0.85
17471.00	90.16	143.66	6717.20	9730.14	-8256.80	5205.35	0.82
17560.00	89.22	143.52	6717.68	9819.14	-8328.42	5258.17	1.07
17650.00	89.09	142.60	6719.01	9909.13	-8400.35	5312.26	1.03
17740.00	89.76	143.13	6719.91	9999.12	-8472.09	5366.58	0.95
17829.00	90.09	143.47	6720.03	10088.12	-8543.45	5419.77	0.53
17919.00	90.23	143.31	6719.78	10178.12	-8615.69	5473.45	0.24
18008.00	90.23	143.26	6719.42	10267.12	-8687.04	5526.65	0.06
18098.00	90.23	142.98	6719.06	10357.12	-8759.03	5580.66	0.31
18188.00	90.26	143.23	6718.67	10447.12	-8831.00	5634.70	0.28
18277.00	90.70	143.16	6717.93	10536.11	-8902.26	5688.01	0.50
18366.00	90.90	143.34	6716.69	10625.10	-8973.56	5741.26	0.30
18456.00	90.43	143.51	6715.64	10715.10	-9045.84	5794.88	0.56
18545.00	89.93	143.77	6715.36	10804.09	-9117.51	5847.65	0.63
18635.00	88.95	143.85	6716.24	10894.08	-9190.14	5900.79	1.09
18724.00	87.84	143.39	6718.73	10983.05	-9261.76	5953.55	1.35
18814.00	88.62	143.22	6721.51	11073.00	-9333.89	6007.31	0.89
18904.00	88.25	143.22	6723.97	11162.97	-9405.95	6061.17	0.41
18993.00	88.35	143.50	6726.61	11251.93	-9477.33	6114.26	0.33
19082.00	88.11	143.40	6729.36	11340.89	-9548.80	6167.24	0.29
19172.00	88.15	143.41	6732.30	11430.84	-9621.01	6220.87	0.05
19261.00	89.22	142.63	6734.34	11519.81	-9692.09	6274.39	1.49
19351.00	89.09	143.53	6735.67	11609.80	-9764.04	6328.44	1.01
19440.00	89.22	143.20	6736.98	11698.79	-9835.45	6381.55	0.40

RECEIVED
Office Of Oil and Gas
OCT 09 2026
10/23/2026
WV Department of
Environmental Protection

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19529.00	89.22	143.28	6738.19	11787.78	-9906.74	6434.80	0.09
19619.00	89.49	143.44	6739.20	11877.78	-9978.95	6488.51	0.35
19708.00	89.76	143.36	6739.79	11966.77	-10050.40	6541.57	0.32
19797.00	89.32	143.36	6740.50	12055.77	-10121.81	6594.69	0.49
19887.00	89.25	143.28	6741.63	12145.76	-10193.99	6648.44	0.12
19976.00	89.25	142.94	6742.79	12234.76	-10265.16	6701.86	0.38
20066.00	89.42	142.87	6743.83	12324.75	-10336.94	6756.14	0.20
20155.00	89.39	143.29	6744.76	12413.74	-10408.09	6809.60	0.47
20218.00	89.29	142.18	6745.48	12476.73	-10458.23	6847.75	1.77
20240.00	89.29	142.18	6745.76	12498.73	-10475.60	6861.23	0.00

10/23/2026
