Well Location Plat

CNX Applicant / Well Operator Name	DEP ID#	MAJ8 Pad C/L Marshall County, WV (NAD27) GL 1190.7 & 18' KB @ 1208.70usft	Well # MAJ8JHSM

WELL PLAN

Operator Name: **CNX RESOURCES**


Well/Farm Name: **MAJ8 Pad C/L**

Name	TVD	Latitude	Longitude	TMD
MAJ8JHSM OH As Drilled KOP	6025.14	39.92402073	-80.58513330	7298.00
MAJ8JHSM OH As Drilled LP	6624.47	39.92049380	-80.58425669	8993.00

SURVEY PROGRAM

Date: 2025-10-02T00:00:00 Validated: Yes Version:

Depth From	Depth To	Survey/Plan	Tool
54.50	1074.50	Survey #1 (OH)	GYD_CT+WIR
1208.50	2208.50	Survey #2 (OH)	MWD+IFR1+Sag
2263.00	20223.00	Survey #3 (OH)	MWD+IFR1+SAG+FDIR

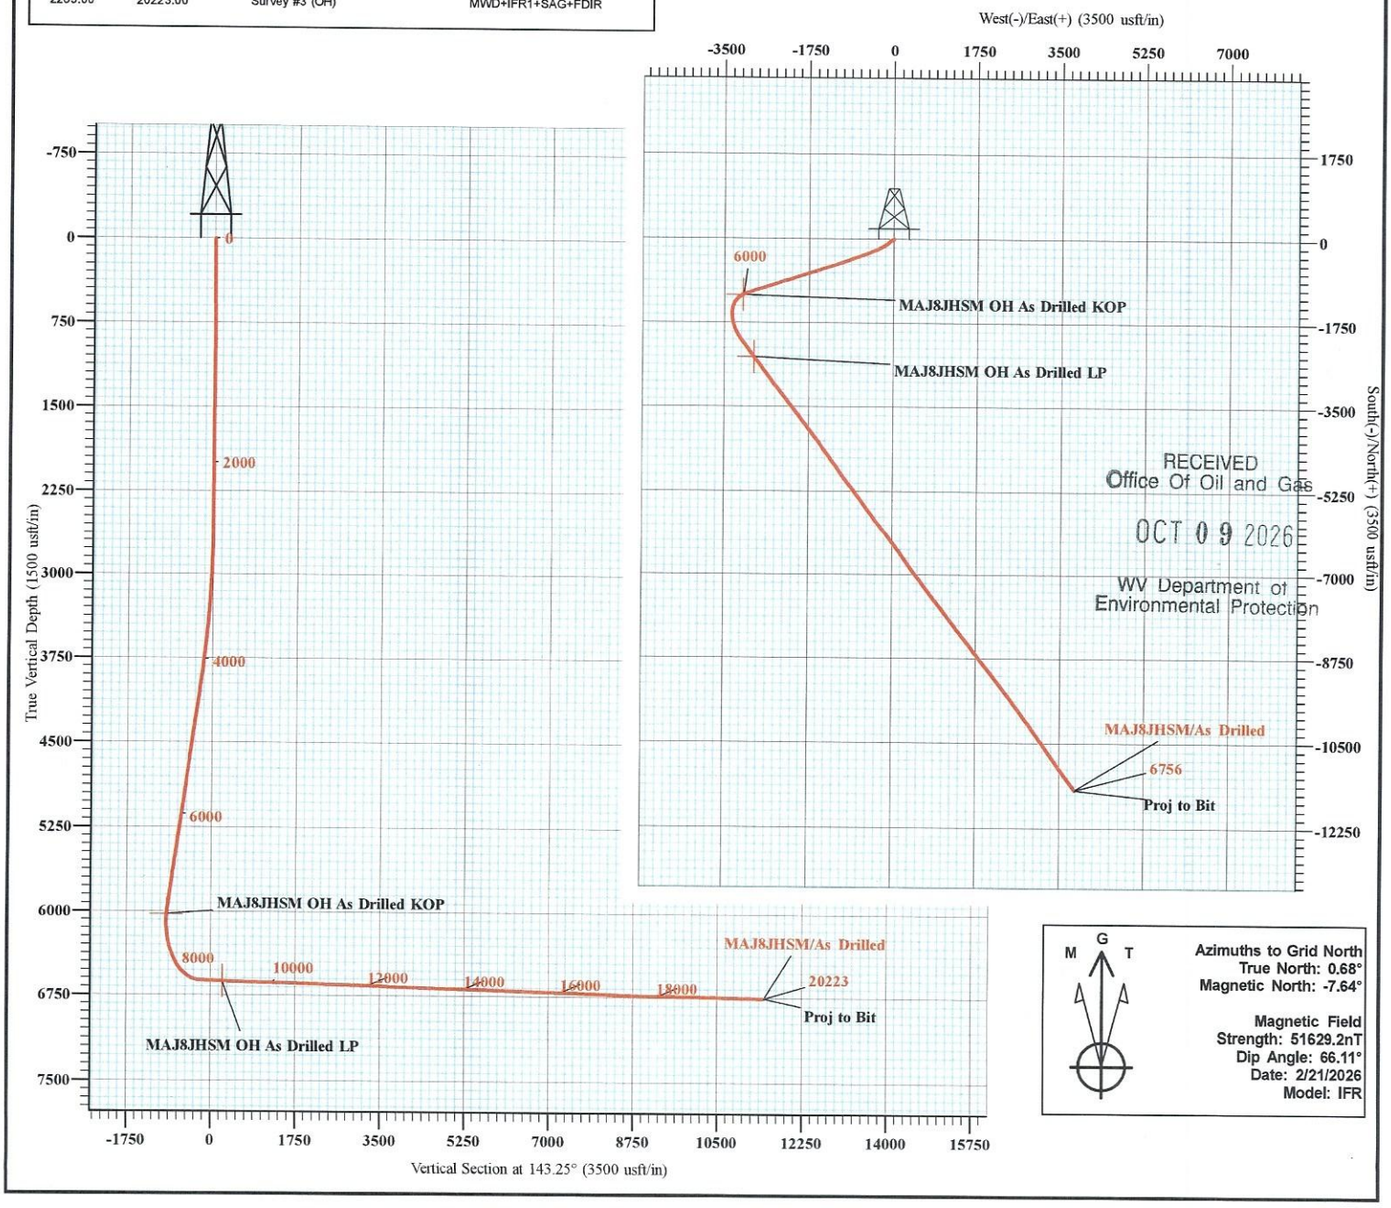


RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

Azimuths to Grid North
True North: 0.68°
Magnetic North: -7.64°

Magnetic Field
Strength: 51629.2nT
Dip Angle: 66.11°
Date: 2/21/2026
Model: IFR

10/23/2026

FEBRUARY 23 2026
SURVEY REPORT

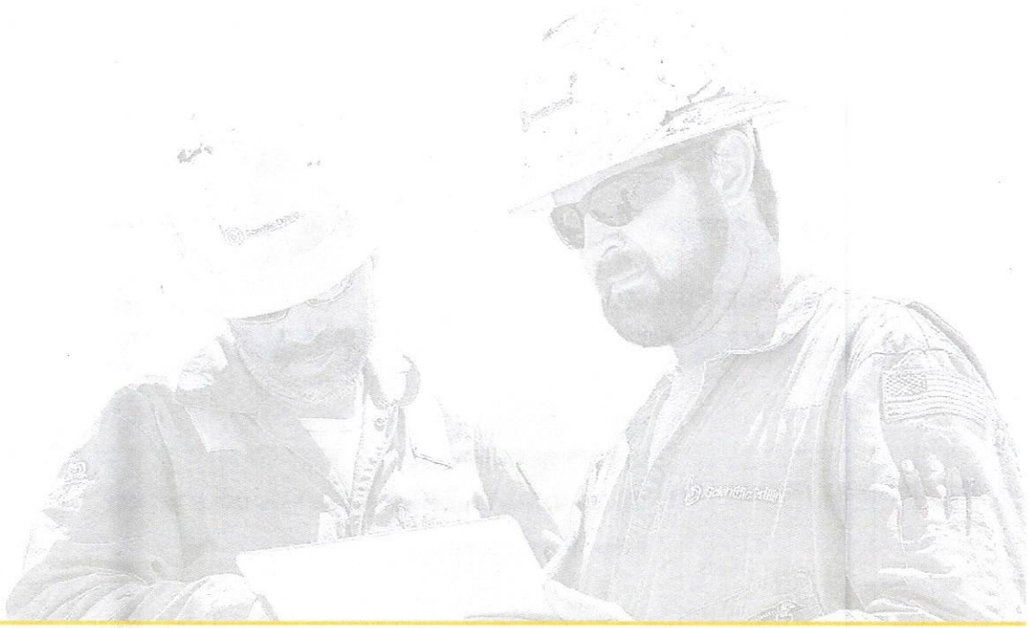

CNX RESOURCES
WELL: MAJ8 JHSM
RIG: PRECISION DRILLING 539

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

SURVEY REPORT MAJ8 JHSM

CUSTOMER	**CNX Resources**
PROJECT	**MAJ8 JHSM**
FIELD	**Marcellus**
SDI JOB NO.	**OP.051521**
SDI DISTRICT	**Northeast**
SDI KIT/UNIT	

SITE INFORMATION

Site Name	**MAJ8 Pad**
Lat/Long	**39.9275261 N, 80.5742268 W**
Northing	**521,744.52 ft**
Easting	**1,698,736.42 ft**
Section	**-**
Township	**-**
Range	**-**

MAP INFORMATION

North Reference	**Grid North**
Grid Correction	**0.69 deg**
System	**US State Plane 1927**
Datum	**North American Datum 1927 (Clarke 1866)**
Map Zone	**West Virginia North: 4701**



WELL INFORMATION


Lat/Long	**39.927349 N, 80.5740441 W**
Northing	**521,679.37 ft**
Easting	**1,698,786.9 ft**
UWI	**47-051-02550**

DEPTH AND ELEVATION REFERENCE

Ground Level	**1190.7 ft above Mean Sea Level**
Reference Datum	**RKB**
Reference Height	**18 ft above G.L.**
Reference Elevation	**1208.7 ft**

VERTICAL SECTION REFERENCE

+N/-S	**0 ft**
+E/-W	**0 ft**
Proposal Direction	**143.24°**
Calculation Method	**Minimum Curvature**



GEOMAGNETIC REFERENCE INFORMATION

Local Gravity: **999.384 mG** [computed]

MD	MODEL	DATE	DECLINATION	TRUE TO GRID	MAG TO GRID
0-20223 ft	IFR1	21 Feb 2026	-8.32°	add 0.69°	subtract 7.63°

SDI Operator Name (Printed) SIGNATURE DATE

WELL NOTES

Gyro Surveys From 0' To 1074.5'

Superior MSA MWD Corrected Surveys From 1208.5' To 20201'

Survey At 20223' Is A Projection To The Bit

OPERATORS

D. BARKER, J. WITKOWSKI

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
0.00	0.00	0.00	0.00	0.00	0.00	0.00	Invalid
54.50	0.50	222.07	54.50	0.05	-0.18	-0.16	0.92
104.50	0.20	162.48	104.50	0.17	-0.42	-0.28	0.87
154.50	0.23	93.94	154.50	0.32	-0.51	-0.15	0.49
204.50	0.35	124.82	204.50	0.53	-0.61	0.07	0.39
254.50	0.35	117.77	254.50	0.81	-0.76	0.33	0.09
304.50	0.32	103.05	304.50	1.06	-0.87	0.60	0.18
354.50	0.36	98.63	354.49	1.27	-0.92	0.90	0.10
404.50	0.26	115.73	404.49	1.49	-0.99	1.15	0.27
454.50	0.39	119.13	454.49	1.74	-1.13	1.40	0.26
504.50	0.36	108.71	504.49	2.03	-1.26	1.70	0.15
554.50	0.30	126.31	554.49	2.28	-1.39	1.96	0.23
604.50	0.42	120.84	604.49	2.58	-1.56	2.22	0.25
654.50	0.40	123.21	654.49	2.91	-1.75	2.52	0.05
704.50	0.42	127.77	704.49	3.25	-1.96	2.81	0.08
754.50	0.51	138.45	754.49	3.65	-2.24	3.11	0.25
804.50	0.33	117.02	804.48	4.00	-2.47	3.38	0.47
854.50	0.13	106.83	854.48	4.18	-2.55	3.56	0.41
904.50	0.09	38.22	904.48	4.21	-2.54	3.64	0.26
954.50	0.21	51.80	954.48	4.20	-2.45	3.74	0.25
1004.50	0.25	37.36	1004.48	4.17	-2.30	3.88	0.14
1054.50	0.18	77.92	1054.48	4.17	-2.20	4.02	0.33
1074.50	0.20	113.07	1074.48	4.21	-2.21	4.08	0.58
1208.50	0.24	305.29	1208.48	4.15	-2.14	4.07	0.33
1295.50	1.27	269.07	1295.47	3.41	-2.05	2.96	1.25
1382.50	3.38	257.70	1382.40	1.78	-2.61	-0.51	2.47
1468.50	5.45	249.80	1468.14	-0.43	-4.56	-6.82	2.50
1556.50	7.36	244.17	1555.59	-2.69	-8.46	-15.82	2.28
1642.50	8.36	240.70	1640.78	-4.55	-13.92	-26.23	1.29
1728.50	9.12	237.07	1725.78	-5.81	-20.68	-37.40	1.09
1814.50	10.05	235.63	1810.58	-6.58	-28.63	-49.32	1.12
1901.50	10.61	235.07	1896.17	-7.15	-37.50	-62.15	0.65
1989.50	11.74	235.19	1982.50	-7.72	-47.25	-76.14	1.28

RECEIVED
Office Of Oil and Gas
OCT 0 9 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
2076.50	11.95	233.25	2067.65	-8.02	-57.69	-90.63	0.52
2161.50	12.35	230.72	2150.74	-7.62	-68.71	-104.72	0.78
2208.50	13.40	231.26	2196.56	-7.21	-75.30	-112.85	2.25
2263.00	13.07	230.52	2249.61	-6.70	-83.17	-122.54	0.68
2352.00	13.64	232.38	2336.21	-6.07	-95.97	-138.62	0.80
2441.00	14.53	232.68	2422.53	-5.80	-109.15	-155.81	1.00
2531.00	15.51	234.52	2509.45	-5.96	-122.98	-174.59	1.21
2620.00	18.33	238.37	2594.60	-7.48	-137.23	-196.20	3.41
2710.00	17.54	238.84	2680.22	-10.07	-151.67	-219.85	0.89
2800.00	20.56	242.19	2765.28	-13.85	-166.06	-245.44	3.57
2889.00	23.17	242.86	2847.88	-19.21	-181.34	-274.85	2.95
2979.00	24.67	244.59	2930.14	-25.86	-197.48	-307.58	1.84
3068.00	27.29	245.76	3010.14	-33.94	-213.83	-342.96	3.00
3157.00	28.05	245.83	3088.97	-42.93	-230.77	-380.66	0.85
3247.00	30.40	248.20	3167.51	-53.42	-247.90	-421.11	2.91
3336.00	31.66	248.99	3243.77	-65.57	-264.63	-463.83	1.49
3426.00	33.62	248.66	3319.55	-78.61	-282.17	-509.09	2.19
3515.00	35.77	248.65	3392.72	-92.07	-300.61	-556.27	2.42
3605.00	37.96	249.39	3464.73	-106.77	-319.93	-606.68	2.48
3694.00	39.88	250.53	3533.97	-122.86	-339.08	-659.21	2.30
3784.00	42.06	249.61	3601.92	-139.93	-359.20	-714.68	2.51
3874.00	42.92	249.51	3668.28	-157.02	-380.43	-771.64	0.96
3963.00	44.61	249.87	3732.56	-174.45	-401.80	-829.37	1.92
4053.00	45.61	249.68	3796.07	-192.60	-423.84	-889.20	1.12
4142.00	45.70	250.30	3858.28	-210.94	-445.62	-949.01	0.51
4232.00	45.66	250.61	3921.16	-230.00	-467.16	-1009.69	0.25
4321.00	47.10	251.72	3982.56	-249.83	-487.95	-1070.67	1.85
4411.00	46.91	251.35	4043.93	-270.50	-508.80	-1133.10	0.37
4501.00	47.06	251.70	4105.33	-291.14	-529.65	-1195.52	0.33
4590.00	47.05	251.45	4165.97	-311.64	-550.24	-1257.33	0.21
4680.00	46.91	251.65	4227.37	-332.31	-571.07	-1319.75	0.22
4769.00	46.92	251.33	4288.16	-352.66	-591.70	-1381.38	0.26

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
4859.00	46.97	251.60	4349.61	-373.23	-612.61	-1443.73	0.23
4948.00	47.02	251.65	4410.31	-393.76	-633.13	-1505.50	0.07
5038.00	47.00	251.26	4471.68	-414.34	-654.06	-1567.92	0.32
5127.00	46.83	251.34	4532.47	-434.49	-674.90	-1629.48	0.20
5217.00	47.00	251.36	4593.95	-454.92	-695.92	-1691.76	0.19
5307.00	47.00	251.52	4655.33	-475.48	-716.88	-1754.16	0.13
5396.00	46.77	251.81	4716.16	-496.01	-737.31	-1815.83	0.35
5485.00	46.45	251.75	4777.30	-516.58	-757.53	-1877.26	0.36
5575.00	46.47	251.96	4839.30	-537.40	-777.85	-1939.26	0.17
5664.00	46.54	251.78	4900.55	-558.03	-797.94	-2000.62	0.17
5753.00	46.63	251.70	4961.72	-578.54	-818.20	-2062.01	0.12
5843.00	46.58	251.95	5023.55	-599.38	-838.60	-2124.15	0.21
5932.00	46.41	251.82	5084.82	-620.02	-858.67	-2185.50	0.22
6022.00	46.58	251.90	5146.78	-640.86	-878.99	-2247.53	0.20
6111.00	46.55	251.72	5207.97	-661.45	-899.17	-2308.93	0.15
6201.00	46.54	251.91	5269.87	-682.26	-919.56	-2371.00	0.15
6290.00	46.52	252.08	5331.10	-703.03	-939.52	-2432.43	0.14
6380.00	46.32	251.78	5393.14	-723.92	-959.74	-2494.41	0.33
6469.00	46.40	252.09	5454.57	-744.56	-979.72	-2555.64	0.27
6559.00	46.46	252.00	5516.60	-765.58	-999.82	-2617.68	0.10
6649.00	46.58	251.91	5578.53	-786.54	-1020.05	-2679.77	0.15
6738.00	46.42	252.23	5639.79	-807.37	-1039.92	-2741.19	0.32
6827.00	46.51	250.88	5701.09	-827.65	-1060.34	-2802.39	1.10
6917.00	46.60	250.87	5762.98	-847.44	-1081.74	-2864.13	0.10
7006.00	46.55	250.86	5824.16	-867.01	-1102.93	-2925.20	0.06
7096.00	46.49	250.84	5886.09	-886.77	-1124.36	-2986.89	0.07
7185.00	46.51	250.35	5947.36	-906.03	-1145.80	-3047.78	0.40
7274.00	46.52	249.07	6008.60	-924.33	-1168.20	-3108.35	1.04
7364.00	46.45	235.14	6070.73	-934.35	-1198.58	-3165.75	11.21
7453.00	46.50	228.20	6132.06	-932.58	-1238.56	-3216.32	5.65
7543.00	46.36	218.67	6194.17	-921.51	-1285.80	-3261.05	7.67
7632.00	46.59	209.35	6255.53	-900.29	-1339.18	-3297.06	7.59
7722.00	48.74	197.36	6316.26	-867.16	-1400.09	-3323.23	10.12

RECEIVED
Office Of Oil and Gas
OCT 09
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
7811.00	51.27	190.00	6373.51	-823.73	-1466.27	-3339.26	6.94
7901.00	55.09	181.93	6427.49	-770.80	-1537.82	-3346.61	8.33
7990.00	59.87	177.74	6475.34	-710.54	-1612.82	-3346.32	6.68
8079.00	65.41	170.44	6516.27	-642.71	-1691.32	-3338.06	9.58
8169.00	70.39	165.48	6550.14	-566.99	-1772.81	-3320.62	7.53
8258.00	73.67	158.45	6577.62	-486.87	-1853.22	-3294.39	8.37
8348.00	79.43	154.05	6598.56	-401.63	-1933.27	-3259.12	7.97
8437.00	84.45	149.81	6611.04	-314.57	-2010.97	-3217.66	7.35
8527.00	88.55	144.96	6616.53	-225.02	-2086.59	-3169.26	7.05
8616.00	88.78	144.02	6618.61	-136.06	-2159.02	-3117.58	1.09
8706.00	89.52	144.38	6619.94	-46.09	-2232.01	-3064.94	0.91
8795.00	89.26	143.28	6620.89	42.90	-2303.85	-3012.42	1.27
8885.00	89.33	142.90	6622.00	132.89	-2375.80	-2958.37	0.43
8974.00	88.22	143.83	6623.90	221.87	-2447.20	-2905.28	1.63
9064.00	88.42	142.64	6626.54	311.83	-2519.27	-2851.43	1.34
9153.00	88.72	143.80	6628.76	400.80	-2590.53	-2798.16	1.35
9243.00	89.36	143.13	6630.27	490.79	-2662.83	-2744.59	1.03
9332.00	89.43	142.85	6631.21	579.78	-2733.90	-2691.02	0.32
9422.00	89.43	143.44	6632.10	669.78	-2805.91	-2637.04	0.66
9511.00	90.17	144.15	6632.41	758.77	-2877.72	-2584.47	1.15
9601.00	89.16	144.00	6632.94	848.76	-2950.60	-2531.67	1.13
9690.00	89.66	142.21	6633.86	937.75	-3021.77	-2478.24	2.09
9780.00	88.05	141.65	6635.65	1027.70	-3092.61	-2422.76	1.89
9870.00	89.16	141.61	6637.84	1117.64	-3163.15	-2366.91	1.23
9959.00	90.34	142.05	6638.23	1206.61	-3233.12	-2311.91	1.42
10048.00	90.04	142.50	6637.94	1295.60	-3303.51	-2257.46	0.61
10137.00	89.60	141.87	6638.22	1384.58	-3373.82	-2202.89	0.86
10227.00	89.40	142.42	6639.00	1474.56	-3444.88	-2147.66	0.65
10316.00	89.53	141.60	6639.83	1563.54	-3515.02	-2092.88	0.93
10406.00	89.40	142.71	6640.67	1653.51	-3586.08	-2037.67	1.24
10495.00	89.70	142.47	6641.37	1742.51	-3656.77	-1983.60	0.43
10585.00	88.42	143.72	6642.85	1832.49	-3728.73	-1929.57	1.99

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
10674.00	89.87	143.00	6644.18	1921.48	-3800.13	-1876.46	1.82
10764.00	89.40	142.94	6644.75	2011.47	-3871.98	-1822.26	0.53
10853.00	89.30	143.36	6645.76	2100.47	-3943.19	-1768.89	0.49
10943.00	88.29	141.69	6647.65	2190.44	-4014.60	-1714.15	2.17
11032.00	89.37	142.97	6649.47	2279.40	-4085.03	-1659.77	1.88
11122.00	89.20	142.55	6650.59	2369.39	-4156.67	-1605.31	0.50
11211.00	88.90	144.15	6652.07	2458.38	-4228.06	-1552.19	1.83
11301.00	89.77	142.90	6653.11	2548.37	-4300.43	-1498.70	1.69
11390.00	90.31	145.53	6653.05	2637.35	-4372.62	-1446.66	3.02
11480.00	88.80	143.41	6653.75	2727.32	-4445.85	-1394.36	2.89
11570.00	89.64	143.29	6654.98	2817.31	-4518.05	-1340.65	0.94
11659.00	89.87	146.29	6655.36	2906.26	-4590.76	-1289.34	3.38
11748.00	88.49	143.09	6656.63	2995.21	-4663.37	-1237.91	3.92
11838.00	90.14	144.62	6657.71	3085.19	-4736.04	-1184.83	2.50
11927.00	89.13	144.98	6658.27	3174.16	-4808.76	-1133.53	1.20
12017.00	89.20	143.32	6659.59	3264.13	-4881.70	-1080.83	1.85
12106.00	90.14	144.34	6660.10	3353.13	-4953.54	-1028.30	1.56
12196.00	87.99	140.64	6661.57	3443.09	-5024.91	-973.52	4.75
12285.00	87.89	142.80	6664.77	3531.99	-5094.73	-918.43	2.43
12374.00	87.89	143.38	6668.04	3620.93	-5165.84	-865.01	0.65
12463.00	90.24	144.86	6669.50	3709.90	-5237.94	-812.86	3.12
12553.00	89.10	143.02	6670.01	3799.89	-5310.69	-759.89	2.40
12643.00	88.43	142.95	6671.95	3889.86	-5382.53	-705.72	0.75
12732.00	90.00	143.81	6673.17	3978.85	-5453.96	-652.64	2.01
12822.00	89.84	144.13	6673.30	4068.84	-5526.74	-599.70	0.40
12912.00	89.13	143.21	6674.11	4158.84	-5599.24	-546.39	1.29
13001.00	88.80	144.23	6675.72	4247.82	-5670.97	-493.73	1.20
13091.00	89.03	144.33	6677.42	4337.79	-5744.03	-441.20	0.28
13181.00	89.27	143.82	6678.76	4427.77	-5816.90	-388.40	0.63
13270.00	89.13	142.61	6680.00	4516.76	-5888.17	-335.11	1.37
13360.00	88.80	143.28	6681.62	4606.74	-5959.99	-280.89	0.83
13449.00	90.04	144.09	6682.52	4695.73	-6031.69	-228.18	1.66
13539.00	89.27	143.28	6683.07	4785.72	-6104.21	-174.88	1.24

RECEIVED
Office Of Oil and Gas
OCT 09 2026
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
13628.00	88.66	144.06	6684.67	4874.71	-6175.90	-122.17	1.11
13718.00	89.50	143.46	6686.12	4964.69	-6248.48	-68.97	1.15
13807.00	89.27	144.51	6687.07	5053.67	-6320.46	-16.64	1.21
13897.00	90.41	143.68	6687.33	5143.66	-6393.36	36.14	1.57
13986.00	88.80	144.14	6687.94	5232.65	-6465.27	88.56	1.88
14076.00	89.03	144.23	6689.64	5322.62	-6538.24	141.22	0.27
14165.00	89.50	144.58	6690.79	5411.60	-6610.61	193.01	0.66
14255.00	88.70	144.04	6692.20	5501.57	-6683.69	245.51	1.07
14345.00	90.34	147.98	6692.95	5591.44	-6758.30	295.81	4.74
14434.00	88.19	142.89	6694.10	5680.33	-6831.55	346.28	6.21
14523.00	89.30	143.31	6696.04	5769.31	-6902.71	399.71	1.33
14613.00	89.37	142.98	6697.09	5859.30	-6974.72	453.68	0.37
14703.00	89.60	143.70	6697.90	5949.30	-7046.91	507.42	0.84
14792.00	90.21	144.04	6698.05	6038.29	-7118.79	559.89	0.78
14881.00	88.93	143.06	6698.71	6127.29	-7190.38	612.77	1.81
14971.00	88.93	142.83	6700.39	6217.27	-7262.19	666.99	0.26
15061.00	88.86	143.79	6702.13	6307.25	-7334.34	720.75	1.07
15150.00	89.27	141.99	6703.58	6396.23	-7405.31	774.44	2.07
15240.00	89.17	142.44	6704.81	6486.21	-7476.43	829.58	0.51
15329.00	88.83	141.37	6706.36	6575.17	-7546.46	884.48	1.26
15419.00	89.37	142.95	6707.77	6665.14	-7617.52	939.68	1.86
15508.00	89.74	142.88	6708.47	6754.14	-7688.52	993.35	0.42
15597.00	89.17	142.86	6709.31	6843.13	-7759.47	1047.07	0.64
15687.00	89.30	141.74	6710.51	6933.11	-7830.68	1102.10	1.25
15777.00	88.90	142.72	6711.93	7023.08	-7901.81	1157.22	1.18
15866.00	89.47	142.55	6713.19	7112.07	-7972.54	1211.22	0.67
15955.00	89.70	142.42	6713.84	7201.06	-8043.13	1265.42	0.30
16044.00	88.93	143.58	6714.90	7290.05	-8114.20	1318.98	1.56
16134.00	89.77	141.60	6715.92	7380.03	-8185.68	1373.65	2.39
16223.00	89.40	142.15	6716.57	7469.00	-8255.69	1428.59	0.74
16313.00	89.23	142.55	6717.64	7558.99	-8326.94	1483.56	0.48
16402.00	89.57	142.35	6718.58	7647.97	-8397.50	1537.80	0.44

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
16492.00	89.33	142.63	6719.44	7737.96	-8468.89	1592.60	0.41
16582.00	89.13	142.54	6720.65	7827.95	-8540.37	1647.28	0.24
16671.00	89.03	142.35	6722.08	7916.93	-8610.91	1701.52	0.24
16760.00	89.40	142.40	6723.30	8005.91	-8681.40	1755.85	0.42
16850.00	89.50	142.93	6724.16	8095.90	-8752.95	1810.43	0.60
16939.00	89.07	142.36	6725.27	8184.89	-8823.69	1864.42	0.80
17029.00	88.50	141.35	6727.18	8274.84	-8894.46	1920.00	1.29
17118.00	89.10	141.71	6729.04	8363.78	-8964.12	1975.35	0.79
17207.00	89.57	141.56	6730.08	8452.74	-9033.90	2030.59	0.55
17297.00	88.66	142.27	6731.47	8542.70	-9104.73	2086.10	1.28
17386.00	89.87	142.06	6732.61	8631.68	-9175.01	2140.68	1.38
17476.00	88.83	141.83	6733.63	8721.65	-9245.87	2196.15	1.18
17565.00	88.93	142.54	6735.37	8810.61	-9316.17	2250.71	0.81
17655.00	89.44	142.85	6736.65	8900.60	-9387.75	2305.25	0.66
17744.00	89.77	142.21	6737.26	8989.59	-9458.38	2359.39	0.81
17834.00	89.67	144.07	6737.70	9079.59	-9530.39	2413.38	2.07
17924.00	88.73	143.57	6738.96	9169.57	-9603.03	2466.50	1.18
18013.00	89.20	143.15	6740.57	9258.56	-9674.43	2519.60	0.71
18103.00	89.47	143.29	6741.61	9348.55	-9746.51	2573.49	0.34
18192.00	89.97	143.92	6742.05	9437.55	-9818.15	2626.29	0.90
18282.00	89.57	143.70	6742.41	9527.54	-9890.78	2679.44	0.51
18372.00	89.97	143.80	6742.77	9617.54	-9963.36	2732.65	0.46
18461.00	90.14	144.43	6742.68	9706.53	-10035.47	2784.82	0.73
18550.00	90.31	144.48	6742.33	9795.50	-10107.88	2836.56	0.20
18640.00	89.74	144.08	6742.30	9885.49	-10180.95	2889.10	0.77
18729.00	89.81	144.24	6742.65	9974.48	-10253.10	2941.21	0.20
18819.00	89.54	144.03	6743.16	10064.46	-10326.03	2993.94	0.38
18908.00	89.27	144.51	6744.08	10153.44	-10398.28	3045.91	0.62
18998.00	88.83	143.05	6745.57	10243.43	-10470.87	3099.08	1.69
19087.00	89.97	145.22	6746.50	10332.40	-10542.99	3151.22	2.75
19177.00	90.54	145.90	6746.10	10422.33	-10617.21	3202.12	0.99
19266.00	88.40	143.62	6746.93	10511.28	-10689.89	3253.46	3.51
19356.00	88.83	143.57	6749.10	10601.25	-10762.31	3306.86	0.48

RECEIVED
Office Of Oil and Gas
OCT 09
WV Department of
Environmental Protection

10/23/2026

MD	INC	AZIM	TVD	VS	+N/-S	+E/-W	DLS
ft	deg	deg	ft	ft	ft	ft	°/100ft
19445.00	90.14	144.94	6749.90	10690.23	-10834.53	3358.85	2.13
19535.00	88.77	144.31	6750.76	10780.20	-10907.91	3410.95	1.68
19624.00	90.04	145.44	6751.68	10869.15	-10980.70	3462.15	1.91
19714.00	90.11	145.50	6751.56	10959.09	-11054.84	3513.17	0.10
19803.00	89.61	142.91	6751.78	11048.07	-11127.03	3565.22	2.96
19893.00	89.03	142.76	6752.85	11138.06	-11198.74	3619.58	0.67
19982.00	89.17	142.90	6754.25	11227.04	-11269.65	3673.35	0.22
20072.00	89.97	143.66	6754.92	11317.04	-11341.79	3727.16	1.23
20162.00	89.54	143.73	6755.31	11407.04	-11414.32	3780.44	0.48
20201.00	89.87	144.07	6755.51	11446.03	-11445.83	3803.42	1.21
20223.00	89.87	144.07	6755.56	11468.03	-11463.64	3816.33	0.00

10/23/2026
